

Stormwater Pollution Control Plan (SWPCP)



**State of Connecticut Department of Energy and
Environmental Protection - Engineering, Sustainability and
Safety Division Engineering Unit**

**Boat Launch Replacement
Squantz Cove Boat Launch
New Fairfield, Connecticut 06812**

DRAFT

Ref. No. R25-00007R01

Prepared for:

Connecticut Department of Energy and Environmental Protection
79 Elm Street
Hartford, Connecticut, 06106

Prepared by:



TABLE OF CONTENTS

1.0 - INTRODUCTION	1
2.0 - SITE DESCRIPTION.....	2
3.0 - CONSTRUCTION ACTIVITIES.....	4
4.0 - RUNOFF REDUCTION AND LOW IMPACT DESIGN	6
5.0 - CONSTRUCTION SEQUENCING.....	7
6.0 - POLLUTANTS OF CONCERN.....	8
7.0 - STORMWATER CONTROL MEASURES	9
7.1 - Erosion and Sediment Controls	9
7.2 - Sediment Barriers and Filters	10
7.3 - Absorbent Materials.....	10
7.4 - Wetland Protection.....	10
7.5 - Tire-Tracked Soils	11
7.6 - Stockpile Maintenance	11
7.7 - Dewatering Wastewaters	11
7.8 - Waste Disposal.....	12
7.9 - Washout Controls.....	12
7.10 - Offsite Deposition of Materials	12
7.11 - Emergency Spill Response	13
7.12 - Maintenance.....	13
7.13 - Post-Construction Stormwater Management.....	14
Good Housekeeping.....	15
Preventative Maintenance.....	15
Sediment and Erosion Control.....	15
7.14 - Other Controls	16
8.0 - INSPECTIONS, RECORDKEEPING AND REPORTING REQUIREMENTS.....	17
8.1 - Plan Implementation Inspections.....	17
8.2 - Routine Inspections	17
8.3 - Post-Construction Inspection.....	18
8.4 - Final Stabilization Inspection	18
8.5 - Termination Inspection	19
8.6 - Recordkeeping Requirements.....	19
8.7 - Reporting Requirements	19
9.0 - CONTRACTORS	21
10.0 - PLAN AMENDMENTS.....	22
11.0 - SIGNATURES OF REPORT AUTHORS	23

FIGURES

Figure 1	Site Location Map
Figure 2	Existing Conditions Plan
Figure 3	Site Plan Showing Sediment and Erosion Controls
Figure 4	Sediment and Erosion Control Details
Figure 5	FEMA Floodplain Map
Figure 6	Soils Map
Figure 7	Historic Places Screening Map

APPENDICES

Appendix A Stormwater Pollution Control Plan Certifications

Appendix B NDDB Determination Letter

Appendix C Wetland and Soil Report

Appendix D Sample Forms

Appendix E Inspector Qualifications

Appendix F Record of Plan Amendments

Appendix G Grading and Drainage Plans

Appendix H CT DEEP National Pollutant Discharge Elimination System General Permit for the
Discharge of Stormwater from Construction Activities (effective January 2026)

REGULATORY CROSS-REFERENCE
Squantz Cove – 210 Route 39 (Sherman Road) Boat Launch
Stormwater Pollution Control Plan (SWPCP)

DEPT. OF ENERGY & ENVIRONMENTAL PROTECTION			
Stormwater Pollution Control Plan Elements		Found In (SWPCP):	
Section	Title	Section	Page
5.	Conditions of General Permit	Section 1.0	1
2.	Stormwater Pollution Control Plan	Section 1.0	1
1.	Development and Contents of Plan	Section 1.0	1
(1)	Plan Consists of Site Plan Drawings and Narrative	Various	--
(2)	Plan Contents		
(a)	Stormwater Design Factors	Figures 2-4, Appendix G	--
(b)	Project Description and Construction Sequencing	Section 3.0 and Section 5.0	4,7
(c)	Site Description	Section 2.0	2
	Description of Construction Activity	Section 3.0	4
	Total Area of Site Disturbed by Construction Activities	Section 3.0	4
	Average Runoff Coefficient After Construction is Completed	Section 4.0	6
	Immediate and Ultimate Receiving Waters	Section 3.0, Appendix G	4
	Extent of Wetland Acreage at Site	Section 2.0, Figure 2	2
(d)	Site plan Drawings	Proposed Drawings	
(e)	Pollutants of Concern	Section 6.0	8
(f)	Control Measures	Section 7.0	9
	Sediment and Floatables Removal Controls Calculations	NA	NA
	Velocity Dissipation Controls Calculations	NA	NA
(g)	Runoff Reduction and Low Impact Development (LID) Information	Section 4.0	6
	Location of Resource Areas	Figure 2, Appendix G	NA
	Natural Drainage Patterns, Swales, Drainage Ways	Figure 2, Appendix G	NA
	Location of Areas with Soils Suitable for Infiltration, Runoff Reduction Practices, and LID Measures	NA	NA
	Location of Areas Unsuitable or Least Suitable for Infiltration for Siting of Areas of Development	NA	NA
	Location of Post-Construction Stormwater Management Measures	Figure 3, Appendix G	NA
	Identification of Areas with Uses with Significant Potential for Groundwater Pollution	Section 7.7	11
	Description of Post-Construction Measures, Runoff Reduction Practices, and LID Measures	Section 4.0	6
	Calculations for Retention of Water Quality Volume and Impact of Runoff Reduction and/or LID Practices	NA	NA
	Site Constraints that Prevent Retention of Appropriate Volume	NA	NA
	Calculations showing proposed effective impervious cover for site	NA	NA
(h)	Site Inspections	Section 8.0	17

REGULATORY CROSS-REFERENCE
Squantz Cove – 210 Route 39 (Sherman Road) Boat Launch
Stormwater Pollution Control Plan (SWPCP)

(i)	Plan Implementation Inspections	Section 8.1	16
(ii)	Routine Inspections	Section 8.2	16
	Plan Implementation and Inspections for Solar Arrays	NA	NA
	Inspection Checklists	Appendix D	
(i)	Contractors	Section 9.0	21
(i)	Identification of contractor/subcontractor	Section 9.0	21
	Contractor Certification Statement (per 5.1.6.2)	Appendix A	
(ii)	Subdivisions	NA	NA
(j)	Impaired Waters	Various	
2.	Stormwater Control Measures	Section 7.0	9
(1)	Erosion and Sediment Controls	Section 7.1 & 7.2	9
(a)	Soil Stabilization and Protection	Section 7.1	9
(b)	Erosion Control Barriers	Section 7.2	10
(2)	Soil Stabilization Timeline	Section 7.1	9
(3)	Maintenance of Vegetation	Section 7.12	12
(4)	Slope Benches	NA	NA
(5)	Wetland Protection	Section 7.4	10
(6)	Structural Measures	Section 7.5	10
(7)	Maintenance	Section 7.12	13
(8)	Dewatering	Section 7.7	11
(a)	Narrative Description	Section 7.7	11
(b)	Turbidity Monitoring	Section 7.7	11
(c)	Contamination	Section 7.7	11
(d)	Pollutants Presence	Section 7.7	11
(9)	Post-Construction Performance Standards	Section 7.13	15
(a)	Redevelopment	NA	NA
(b)	Linear Development	NA	NA
(c)	Other Development	Section 7.13	15
(10)	Post-Construction Control Measures	Section 7.13	15
(a)	Runoff Reduction and LID Practices	Section 4.0	6
(b)	Suspended Solids and Floatables Removal	Section 7.13	14
(c)	Velocity Dissipation	NA	NA
(11)	Other controls	NA	NA
(a)	Waste Disposal	Section 7.8	12
(b)	Washout Areas	Section 7.9	12
(c)	Off-Site Vehicle Tracking/Dust Suppression	Section 7.5 & 7.10	10 & 13
(d)	Cleaning	Section 7.12	13
(e)	Storage of Chemical and Petroleum Products	Section 7.14	16
(f)	Emergency Spill Response	Section 7.11	13
(g)	Cold Water Stream Habitat	NA	NA
(3)	Additional Control Measures for Impaired Waters	NA	NA
(4)	Inspections	Section 8.0	17
(1)	Plan Implementation Inspections	Section 8.1	17

REGULATORY CROSS-REFERENCE
Squantz Cove – 210 Route 39 (Sherman Road) Boat Launch
Stormwater Pollution Control Plan (SWPCP)

(a)	Inspector Requirements for non-state agency projects >1 acre	Section 8.1	17
(i)	Not be an employee of the registrant, and	Section 8.1	17
(ii)	Has no ownership interest in the project	Section 8.1	17
(b)	Inspector Requirements for state agency projects >1 ac	NA	NA
(i)	Not be employee of the registrant	NA	NA
(ii)	Is included in list of qualified professionals approved by State agency	NA	NA
(2)	Routine Inspections	Section 8.2	17
(a)	Frequency of Inspections	Section 8.2	17
(b)	Evaluation of E&S Controls	Section 8.2	17
(c)	Inspection report	Section 8.3	18
(d)	Solar projects	NA	NA
(e)	DEEP inspectors	Section 8.4	18
(3)	Post-Construction Inspection	Section 8.3	18
(a)	Locally approvable projects	Section 8.3	18
(b)	Locally Exempt Projects	NA	NA
(c)	Projects conducted by state agencies	NA	NA
(4)	Final Stabilization Inspection	Section 8.4	18
(5)	Termination Inspection	Section 8.5	19
(5)	Keeping Pollution Control Plan Current	Section 10.0	22
(1)	Plan amendments	Section 10.0	22
(2)	Notification of non-compliance	Section 10.0	22
	Deadline for updated Plan	NA	NA
(3)	Qualified Person maintaining permit	NA	NA
(4)	Retain plan modifications	NA	NA
(5)	Failure to Prepare, Maintain, or Amend Plan	Section 10.0	22
(6)	Plan Signature	Appendix A	--
(a)	Permittee Certification	Appendix A	--
(b)	Contractor/subcontractor Certification	Appendix A	--
(c)	Engineer or Landscape Architect Certification	Appendix A	--
(7)	Plan Review Certification	Appendix A	--
3.	Reporting and Record Keeping Requirements	Section 8.6	19
(1)	Record Keeping	Section 8.6	19
(1)	Permittee Plan Retention Period	Section 8.6	19
(2)	Plan Retention at Construction Site	Section 8.6	19
(3)	Inspection Records Retention Period	Section 8.6	19
(a)	Conducting and Recording Plan Implementation Inspections	Section 8.6	19
(b)	Conducting and Recording Routine Inspections	Section 8.6	19
(4)	Plan Modification	Section 8.6	19
(2)	Reporting	Section 8.7	19
(1)	Reporting timeframe	Section 8.7	19
(2)	Turbidity Monitoring Reports	Section 8.7	19

1.0 - INTRODUCTION

Triton Environmental, LLC. (Triton) has prepared this Stormwater Pollution Control Plan (SWPCP or Plan) on behalf of the Connecticut Department of Energy and Environmental Protection (CT DEEP) for the boat launch construction and associated site improvements at its property located at 210 Route 39 (Sherman Road) in New Fairfield, Connecticut (see Figure 1). This Plan is updated in accordance with the Connecticut Department of Energy and Environmental Protection (CT DEEP) National Pollutant Discharge Elimination System General Permit for the Discharge of Stormwater from Construction Activities, effective January 1, 2026 (General Permit). CT DEEP is constructing an approximately 5,500 ft² new boat launch adjacent to its existing boat launch with associated site improvements to enhance public use of the property with a new boat launch structure, bathroom facilities, and parking and off-loading/loading areas. The project includes significant grading, construction of the new boat launch structure, bathroom facilities, parking and off-loading/loading areas, stormwater infrastructure, and landscaping.

This SWPCP has been prepared to align with the requirements of the General Permit effective January 1, 2026. It is designed to address two components of stormwater pollution: (1) impacts caused by soil erosion and sedimentation during and after construction; and (2) stormwater impacts caused by use of the site after construction is completed, including but not limited to parking lots, roadways and the maintenance of grass areas. This document has been prepared in conjunction with the attached figures.

A Regulatory Cross-Reference is provided at the beginning of this document presenting the requirements of the General Permit and their locations in the SWPCP.

2.0 - SITE DESCRIPTION

CT DEEP's site is located on an approximately 7-acre parcel, bordered by Candlewood Lake to the north and east, Old Bogus Road to the south, and Route 39 to the west within New Fairfield, Connecticut (Fairfield County) (see Figure 1).

The land cover generally consists of paved and gravel areas for access and parking, an open grass area, wooded areas, and other vegetation along the western shoreline of Candlewood Lake. The toilet building, existing boat launch, and other site features are depicted on the property survey (see Figure 2). The topography of the property survey ranges from elevation approximately 442.00' at the site driveway entrance and slopes up to a ridge line running north to south through the property. The site slopes to the east to elevation 428.00' at the water's edge. Existing and future discharges will be to either the stormwater collection system in Route 39, Candlewood Lake, or infiltrate into the ground.

The shoreline of the property is located within the Special Flood Hazard Area (SFHA), Zone A, without an established Base Flood Elevation (BFE). The Flood Insurance Rate Map (FIRM) has depicting the SFHA overlaid on top of the property has been included (see Figure 5). The wetlands boundary is defined by the water elevation of Candlewood Lake. Candlewood Lake has been identified on the CT 2024 Integrated Water Quality Report as CT6400-00-1-L5_01 and is not considered an impaired waterbody. No additional inland wetlands are located on the site. These wetlands have been flagged by a certified wetland scientist, and a soil report has been provided with this application (see Appendix D). The parcel is not located in an Aquifer Protection Zone or any public water supply watersheds.

A review of CT DEEP Natural Diversity Database (NDDB) was conducted as part of the initial site review process for the project to determine whether state-listed special concern, threatened and/ or endangered species occur within the project limits. An NDDB determination was performed and issued on November 26, 2024, and is valid until November 26, 2026 (see Appendix C). Based on the review, no negative impacts to populations of NDDB-listed species are anticipated from the project.

A search on the Connecticut State Cultural Resource Information System (CRIS) database revealed that the property is not located within an archeologically sensitive area and is not located on or immediately adjacent to a property listed or determined to be eligible for listing

on the National or State Registers of Historic Places. A printout of the historic places screening map is presented in Figure 7.

CT DEEP's property is used by the public as a public boat launch and associated parking area. Public access is provided by a paved access drive from Route 39. The existing boat launch is a single concrete ramp that extends into the lake and beneath the lake bottom. The parking area consists of a gravel drive, unmarked spaces in a grassy area, and a perimeter wooden guide rail. The parking area also provides space for non-boaters. The grassy area of the property located east of the gravel lot is used by the public as a recreational space and contains a small number of standalone charcoal grills.

3.0 - CONSTRUCTION ACTIVITIES

The proposed construction project consists of a ticket kiosk, formal parking area, dedicated off-loading/loading areas, ADA accessible facilities, pedestrian egress paths, new paved access drive with improved traffic separation and circulation, two-lane width concrete boat ramp, kayak and canoe launch area, two floating docks, and a new vault pit toilet building.

Vehicles will enter the facility from Route 39 at the same location as the existing access drive. The access drive will be reconstructed to widen the entrance and will include a separation median to control incoming and outgoing traffic. All incoming traffic will be directed to a proposed DEEP kiosk and continue to the new and/or existing boat/kayak/canoe launches via a dedicated access lane or to the reconstructed parking area bypassing the boat launch. Access to the launches will be provided by a one-way paved access road with a counterclockwise traffic flow. The access drive to and from the boat launches will include a turnoff area for boaters to prepare their boats prior to and following unloading/loading. Following unloading/ loading, launch users will exit the facility or proceed to the parking area.

The existing gravel lot will be reconstructed and formalized to delineate trailered and non-trailered parking spaces for public use of the launch and/or the picnic area. Earthwork will be conducted throughout the gravel lot to ensure grading will be sufficient for vehicular and pedestrian traffic. The proposed grading has been designed to ensure adequate parking conditions and maintain pedestrian access to the boat launch. The proposed lot will accommodate a total of 100 vehicles on the property including four ADA accessible spaces.

The reconstructed motorized boat launch will consist of a two-lane width, center-oriented concrete ramp between a set of floating docks. The ramp will consist of precast concrete panels mechanically attached to a poured concrete anchor wall on the landward side at the junction between the asphalt access road and the concrete ramp. The panels will be anchored at the terminus of the ramp underwater with a concrete transition pad that will terminate beneath the lake bottom. Each set of floating docks will be mechanically attached to a stationary reinforced concrete pier at the landward side and by one or more timber piles on the waterward side. The boat launch will also include a dedicated cartop unloading and

launch area on the southern side of the motorized boat ramp. The cartop launch will consist of interlocking concrete blocks that will then transition to the existing lake floor.

A concrete sidewalk will be installed through the middle of the parking lot in a north-south fashion, and along the south side of the parking lot to connect the parking area to the boat launch. A processed aggregate sidewalk will be installed along the north and east sides of the parking lot leading to and from the concrete sidewalk south of the parking area and ultimately lead to the boat launch. The site improvements also include the removal of the existing toilet building and septic system and the construction of a new vault pit toilet building. A vault toilet will be located at the east side of the parking lot.

Construction will occur over an approximate area of 230,000 ft² and will involve significant earth movement for construction. The overall elevation of the property throughout the construction area will slope to a lower elevation at the south portion of the property for vehicular traffic access. Over the duration of the construction project, up to 5.28 acres may be disturbed, but not greater than five acres will be disturbed at one time. Future stormwater discharges will be consistent with existing conditions, with the west portion of the site discharging to the municipal stormwater infrastructure along Route 39, and the remaining discharge being directed to Squantz Cove. The impervious areas onsite will increase 55% to 0.15% of the total site following completion of the construction project.

Excavated materials disturbed during construction will be reused and stabilized onsite to the extent possible or disposed of in an offsite location in accordance with all regulatory requirements.

4.0 - RUNOFF REDUCTION AND LOW IMPACT DESIGN

Stormwater Best Management Practices (BMPs) have been adopted by CT DEEP for stormwater management and are consistent with those adopted by the Environmental Protection Agency and the State of Connecticut.

The BMPs that will be practiced at the site will be adequate for reducing the potential for stormwater contamination and include good housekeeping, preventative maintenance, spill prevention and response, and sediment and erosion control. Stormwater modifications will include the construction of new stormwater infrastructure. The BMPs adopted by CT DEEP will be implemented during and after construction and will provide adequate protection required for the waters of the state.

The proposed runoff coefficient for the entire property is 0.61-0.96. The proposed development will have landscaping, grass, parks, process aggregate and concrete sidewalks, asphalt access roads, boat launches, and public access areas. The Boat Launch construction plan has been developed using Low Impact Development (LID) style Best Management Practices (BMPs) as part of the overall stormwater design where appropriate.

5.0 - CONSTRUCTION SEQUENCING

Construction is anticipated to begin in Fall of 2026 and end in Summer of 2027. Prior to the start of construction, full soil erosion and sediment controls will be installed and maintained to isolate each work area. Work under the general permit is limited to the Boat Launch and Parking Area construction (see Figure 3). The sequencing of construction will be as follows:

- Pre-Construction meeting
- Utility Delineation by public and/or private utility location firm
- Mark boat launch, lot limits, toilet buildings, drainage feature locations, drive limits, and clearing limits
- Install soil erosion and sedimentation control measures
- Perform tree, stump removal and clear and grub vegetation
- Perform saw cutting
- Perform rough grading
- Install boat launch
- Install trench drain, and floating docks
- Install proposed toilet building
- Install subbase for lot limits and access drive
- Perform final grading and compaction
- Install concrete and processed aggregate sidewalks
- Install drainage swales to east and west of proposed lot
- Install pavement binder course and curbing
- Install final pavement course
- Perform line tripping
- Install signage, concrete wheel stops, and painted symbols
- Install seeding

All disturbed surfaces will be stabilized as soon as construction has been completed, and the soil erosion and sediment controls will be maintained in place until final stabilization of disturbed areas.

6.0 - POLLUTANTS OF CONCERN

Stormwater discharges associated with construction activities at the site may contain the following pollutants of concern, based on site conditions, historical site use, and proposed remediation and construction activities:

- Sediment and suspended solids, including soils disturbed during grading, excavation, utility installation, dewatering, etc.
- Trace quantities of hydrocarbons associated with vehicle and equipment operation.
- Concrete wash water from concrete placement and washout activities.
- Construction debris and solid waste.
- Dust and airborne particulates generated during earthwork and material handling.

All disturbed areas will be managed using erosion and sedimentation (E&S) control measures, such as silt fencing, filter socks, or other approved controls, to minimize the mobilization and off-site transport of these pollutants and potential of polluted runoff. Stockpiling of impacted materials will be minimized, and any temporary staging will occur within the designated areas using appropriate containment and perimeter controls as described in section 7.2 and 7.6 to prevent contact with stormwater.

7.0 - STORMWATER CONTROL MEASURES

7.1 - Erosion and Sediment Controls

Sedimentation and erosion control measures have been developed for the construction project (see Figure 3 and Figure 4). The erosion and sediment control measures have been designed and will be installed and maintained in accordance with the “2024 Connecticut Guidelines for Soil Erosion and Sediment Control” (Guidelines), as amended.

It is the responsibility of CT DEEP to perform or oversee and administer construction related activities as generally described in the SWPCP. CT DEEP will be responsible for the timely installation, inspection, repair or replacement of erosion control devices to ensure proper operation. CT DEEP will be responsible for controlling unsatisfactory erosion conditions not effectively controlled by the erosion and sediment control plans, as observed by inspection of field conditions, and will install additional measures, if necessary.

Where construction activities have permanently ceased or when final grades are reached in any portion of the site, stabilization and protection practices shall be implemented within seven (7) days. Notwithstanding any provisions of the Guidelines, areas that will remain disturbed but inactive for at least fourteen (14) calendar days shall receive temporary seeding or soil protection within seven (7) days. Areas that will remain disturbed beyond the seeding season shall receive long-term, non-vegetative stabilization and protection sufficient to protect the site through the winter. In all cases, stabilization and protection measures shall be implemented as soon as possible. Temporary or permanent vegetation or other ground cover shall be always maintained in all areas of the site, except those undergoing active disturbance, to prevent erosion and soil compaction during construction activities. All new temporary and permanent vegetation shall consist of native plant species. With respect to such vegetation, CT DEEP will not use chemical fertilization, herbicides, or pesticides except as necessary to establish such vegetation.

As earthwork operations proceed, additional measures will be installed at the bottom of fill slopes and around soil stockpiles as necessary. In all cases, stabilization measures will be implemented as soon as possible after earthwork operations begin.

7.2 - Sediment Barriers and Filters

The primary function of these measures is to slow the velocity of sediment laden waters enough to allow suspended sediments to drop out of solution. Secondary functions can include the filtering of sediment laden waters and the creation of a physical barrier that prevents the sediment laden water from mixing with clean waters. To mitigate the transportation of disturbed sediment from entering the stormwater system, CT DEEP will implement the following measures: filter socks, geotextile silt fence (GSF), and/or catch basin inserts.

Filter socks and/or GSF will be placed at downslope work limits, around existing catch basins, or as otherwise shown on Figure 3. A double row of barriers will be installed and maintained in those limited areas that are equal to or greater than 8% slope and downslope of disturbed areas within 50 feet of waters of the state. Soil stockpiles will be located away from any potentially sensitive areas or areas subject to stormwater runoff and will include a barrier around the stockpile area, approximately ten feet away from the proposed toe of the slope. Filter socks installed on hardscaped areas will be weighed down with concrete blocks or other ballast.

Catch basin inserts (aka silt sack) will be installed within newly installed and nearby existing catch basins during construction. This measure shall be used where the drainage area to an inlet is disturbed, it is not possible to temporarily divert the storm drain outfall into a trapping device, or where watertight blocking of inlets is not advisable. The measure will be installed as an “internal inlet protection” product, installed inside the structure to capture sediment after it enters the structure.

7.3 - Absorbent Materials

If disturbed soil creates a visible sheen or a visible sheen is observed in any catch basins, absorbent materials such as an oil sock, will be installed within the catch basin. Additionally, an absorbent sock(s) will be installed surrounding the inlet, as necessary.

7.4 - Wetland Protection

Where site disturbance occurs within 50 feet of waters of the state (along the southern edge of the site), a double row of sediment barriers will be installed in

accordance with the Guidelines between the disturbed area and downgradient waters. Any dewatering activities near the shoreline will follow the requirements of Section 7.7.

7.5 - Tire-Tracked Soils

The construction area is located adjacent to paved public roads. Therefore, the Contractor will construct a construction entrance at each exit point from the construction area to the public roadways and will be maintained for the duration of the project until final stabilization. If tracking of sediment becomes apparent during construction, the Contractor will implement additional measures (e.g., extended length, wash rack, additional cover stone, sweeping, etc.) as necessary.

7.6 - Stockpile Maintenance

Soil stockpiles will be located away from construction activities and adjacent watercourse. If topsoil is to be stockpiled longer than 30 days, it will be protected with a temporary seeding, matting or other acceptable means of preventing erosion. Separate stockpiles will be maintained for soils to be reused onsite and for soils to be disposed of offsite. The anticipated stockpile areas will be constructed as shown in the drawings. The management of the stockpiles and stormwater runoff will be performed in conformance with the Guidelines.

7.7 - Dewatering Wastewaters

Any dewatering wastewater generated during construction will be directed to a treatment system that includes frac tanks, bag filters, etc. (see Figure 3 for treatment system location).

Once the analytical test results confirm that water quality is acceptable for release, the water will be discharged into the nearby existing municipal stormwater infrastructure or Squantz Cove. Additionally, each dewatering discharge point will be monitored initially and weekly for turbidity for the duration of dewatering operations. Samples will be taken after the dewatering water has been treated with the first turbidity measurement taken within 30 minutes of initiating the dewatering discharge. A record of the turbidity monitoring results will be kept on-site. Dewatering activities will be monitored and adjusted, as needed. The treatment and discharge of dewatering wastewater will be conducted under the terms of the General Permit.

7.8 - Waste Disposal

During construction, the Contractor will ensure litter or other debris, and any waste materials are removed from the premises, as necessary, to prevent such materials from entering the storm drainage system and/or waters of the state. After construction, CT DEEP will be responsible for performing this activity.

7.9 - Washout Controls

Washout of applicators, containers, vehicles and equipment for concrete, paint, and other materials, if applicable, will be conducted in a designated washout area. There will be no surface or ground water discharge of washout wastewater(s) from this area. The contractor will conduct washout operations:

1. Outside of any wetland buffers and at least 50 feet from any stream, wetland, and other sensitive resource; and,
2. In an entirely self-contained washout system.

The Contractor will designate areas to be used for washing and conduct such activities only in these areas. The Contractor will direct wash water into a container or pit designed so that no overflows can occur during rainfall or after snowmelt. If an excavated pit is utilized, the pit will be established as an impervious structure (e.g. lined basin, etc.) and will use diversion measures to divert surface runoff from entering the pit. Dumping of liquid wastes in storm sewers is prohibited.

At least once per week, CT DEEP will inspect any containers or pits used for washout to ensure structural integrity, adequate holding capacity, and to check for leaks or overflows. If there are signs of leaks, holes or overflows in the containers or pits that could lead to a discharge, the contractor will repair them prior to further use. For concrete washout areas, the Contractor will remove hardened concrete waste whenever the hardened concrete has accumulated to a height of half of the container or pit, or as necessary to avoid overflows.

7.10 - Offsite Deposition of Materials

CT DEEP will minimize off-site vehicle tracking of sediments and dust generation during construction in accordance with the above referenced Guidelines.

Vehicle parking lots and drives will be paved and landscaped areas will be seeded and

mulched. As such, dust and sediment tracking after construction is completed will be addressed by these measures. A street sweeper may be used to remove tracked sediment from adjacent local roads or site pavements, if necessary.

Wet dust suppression will be used for any construction activity that causes airborne particulates. The volume of water used for dust control will be minimized to prevent the runoff of water. Discharges of dust control water will not contain or cause visible oil sheen, floating solids, visible discoloration, or foaming in the receiving water body.

7.11 - Emergency Spill Response

The construction activities for this project will include the use of heavy equipment. Spill prevention measures will be implemented in accordance with EPA best management practices for spill prevention and material handling as applicable. This includes performing refueling activities in designated areas with appropriate containment measures, inspecting heavy equipment daily for leaks, and training construction personnel on spill prevention and proper handling of fuels and oils. The contractor will maintain spill kits on site for the duration of the construction. Kits will include enough absorbent and barrier materials to properly contain spills.

7.12 - Maintenance

Maintenance of erosion control practices on the construction site will be performed in accordance with the Guidelines and Table 1 below, provided that, if additional maintenance will protect the waters of the state from pollution, the Plan will be amended to include a description of the additional procedures, including vegetation and other protective measures identified in the site plan. CT DEEP will be responsible for cleaning any construction debris or sediment from existing roads as ordered by the Town and/or State if any debris or sediment from construction activities enter onto these roadways. Accumulated sediment removed from erosion control devices will be spread and stabilized in level erosion-resistant locations. Additionally, all post-construction stormwater structures shall be cleaned of construction sediment, and any remaining silt fence shall be removed upon stabilization of the site.

Table 1-Maintenance Schedule

Erosion and Sediment Control Practice	Maintenance Items	Frequency
Filter Sock or Geotextile Silt Fence (GSF)	- Inspect controls for displacement, damage, undercutting, or bypass. - Remove sediment or install a secondary barrier upgradient of the original control when deposits reach approximately half of the height of the control.	Weekly and after a Storm Event that Creates a Discharge*
Inlet Protection	- Inspect the measure for damage, displacement, bypass, or surface ponding. - Inspect for sediment accumulation. Remove sediment and reinstall insert.	Weekly and after a Storm Event that Creates a Discharge
Absorbent Materials (if required)	Inspect for oil accumulation. Replace when internal sock has become 50% saturated with oil. Replace external sock when oil accumulation is visible.	Weekly and after a Rainfall Event that Creates Discharge
Construction Entrance	- Inspect for effectiveness (tracking of sediment out of construction area) - Install top dressing with additional aggregate, as required. - Remove immediately sediment spilled, dropped, or washed onto public right-of-way.	Weekly and after a Storm Event that Creates a Discharge
Temporary Seeding (if required)	- Erosion, poor seedling emergence - Reseed, as necessary to stabilize	Weekly and after a Storm Event that Creates a Discharge
Soil Stockpile	See Above for Filter Sock or GSF and Temporary Seeding	Weekly and after a Storm Event that Creates a Discharge
Dewatering (if required)	- Inspect for damage, excessive pump rate, discharge quality - Maintenance as necessary.	Daily During Dewatering Operations
Washout (if required)	- Inspect containers/pits to ensure structural integrity, adequate holding capacity, and to check for leaks or overflows - Remove hardened concrete waste when the waste has accumulated to a height of half of the washout, or as necessary to avoid overflows	Weekly and after a Storm Event that Creates a Discharge

*For storms that end on a weekend, holiday, or other time after which normal working hours will not commence within 24 hours, a routine inspection is required within 24 hours only for storms that equal or exceed 0.5 inches. For storms of less than 0.5 inches, an inspection shall occur immediately upon the start of the subsequent normal working hours.

7.13 - Post-Construction Stormwater Management

This section describes the Best Management Practices (BMPs) adopted by CT

DEEP for stormwater management, which are consistent with those adopted by the EPA

and the State of Connecticut. The typical stormwater constituents of concern found in urban runoff (suspended solids, metals, trash, floatable material, etc.) can be effectively treated by conventional methods (e.g., stormwater basins, swales, filtering practices, etc.) and/or proprietary treatment devices. As such, the proposed stormwater management strategy to meet the effluent guidelines includes a combination of conventional treatment practices and good housekeeping BMPs.

Good Housekeeping

Pollutants will be controlled at the source to the maximum extent feasible as ensured by the BMPs under the General Permit. Good housekeeping BMPs will be used to maintain a clean and orderly workplace to reduce the potential for discharge.

CT DEEP will use dumpsters and/or trash receptacles to facilitate the proper disposal of refuse. The dumpsters may be in direct contact with stormwater. To minimize adverse impacts, dumpsters will be equipped with covers, which will be kept closed when not in use. In addition, dumpster drain ports (where applicable) will be plugged.

Preventative Maintenance

Following construction, CT DEEP will conduct the following specific preventative maintenance tasks:

1. Regular inspections of trench drains and stormwater quality structures throughout the site will be inspected on a regular basis throughout the year for presence of accumulated trash, debris, and sediment accumulation.
2. Regular inspections of outfalls to ensure that debris or other materials are not being collected and discharged with stormwater.
3. Stormwater structures will be pumped out with a vac-truck at least once per year or as determined based on the inspection results.
4. Dumpsters at the facility will be covered at all times with bottom drains plugged.
5. The paved parking areas will be kept clear of unnecessary equipment and debris and swept as necessary.

Sediment and Erosion Control

The site design has integrated sediment and erosion control measures. Post-construction, the site will have minimal potential for sediment generation. However, during significant storm events, there is potential for typical urban constituents (e.g.,

sediment, trash, vehicle-related hydrocarbons, etc.) to be mobilized in stormwater and collected by the new stormwater system. CT DEEP has established trench drains, sumps and water quality structures designed to capture these typical constituents prior to discharge. The development includes water quality swales sized to treat the water quality volume storm event peak flow rate.

7.14 - Other Controls

Chemical and Petroleum Storage

All chemical and petroleum product containers stored on the site (excluding containers within vehicles/equipment) will have impermeable secondary containment that holds at least 110% of the volume of the largest container, or 10% of the total volume of all containers in the area, whichever is larger, without overflow from the containment area. All chemicals and their containers will be stored under a roofed area except for those chemicals stored in containers of 100 gallons or more, in which case a roof is not required. Double-walled tanks satisfy this requirement.

8.0 - INSPECTIONS, RECORDKEEPING AND REPORTING REQUIREMENTS

8.1 - Plan Implementation Inspections

Prior to commencement of each phase of construction activity on the site, CT DEEP will contact the qualified designing professional who will ensure that all required inspections are conducted. For each phase of construction, the site will be inspected at least once within the first thirty (30) days of construction activity and at least three times, with seven (7) or more days between inspections, within the first ninety (90) days of construction activity to confirm compliance with the Permit and proper initial implementation of all control measures as detailed in this Plan for each phase of construction. The inspector must meet the following conditions:

- Cannot be an employee of the registrant.
- Cannot have ownership interest of any kind in the project for which the registration is being submitted.

8.2 - Routine Inspections

CT DEEP will maintain a rain gauge on-site to document rainfall quantities. A qualified inspector, provided by CT DEEP, will inspect all disturbed areas of the construction activity that have not been finally stabilized, erosion and sediment control measures, structural control measures, soil stockpile areas, washout areas, and locations where vehicles enter or exit the site at least once every seven calendar days and within 24 hours of the end of a storm that generates a discharge. For storms that end on a weekend, holiday or outside normal working hours, an inspection is required within 24 hours only for storms that are equal to or greater than 0.5 inches. For storms of less than 0.5 inches, an inspection will occur immediately upon the start of the subsequent normal working hours. Where areas have been temporarily stabilized, a routine inspection will continue no less than once per seven calendar days until final stabilization has been achieved, after which inspections may occur once per month for the required three-month period.

Disturbed areas and areas used for storage of materials that are exposed to precipitation will be inspected for evidence of, or the potential for, impacts (i.e., fine sediment, fuel oil, etc.) entering the drainage system or waters of the state. Erosion and sediment control measures will be observed to ensure that they are operating correctly. Where discharge locations or points are

accessible, they will be inspected to determine whether erosion control measures are effective in preventing significant impacts to receiving waters. Locations where vehicles enter or exit the site will be inspected for evidence of off-site sediment tracking.

A report summarizing the scope of the inspection, name(s) and qualifications of personnel making the inspection, the date(s) of the inspection, major observations relating to the implementation of the Plan, and actions collected will be made and retained as part of the Plan for at least five years after the date of inspection. The report will include a statement that, in the judgment of the qualified inspector(s) conducting the site inspection, the site is either in compliance or out of compliance with the terms and conditions of the Plan and permit. If the site inspection indicates that the site is out of compliance, the inspection report will include a summary of the remedial actions required for the site to be in compliance. The report will be signed by the Owner or an authorized representative in accordance with the requirements of the Guidelines.

Original inspection reports will be signed by the assigned personnel and filed onsite. A copy of the signed inspection report will also be maintained onsite, if the original is not maintained on the site. Where sites have been temporarily or permanently stabilized, such inspection will be conducted at least once every month for three months. Sample inspection forms are included in Appendix D.

8.3 - Post-Construction Inspection

Once all post-construction stormwater measures have been installed in accordance with the Permit, CT DEEP will ensure that a qualified inspector will inspect the site to confirm compliance with all such measures. A report will be prepared and certified in accordance with the applicable sections of the general permit to indicate compliance with this requirement on the Notice of Termination form.

8.4 - Final Stabilization Inspection

A qualified inspector will conduct a final stabilization inspection to confirm that disturbed areas have been stabilized. This inspection will be conducted in the year following the end of construction and after at least one full growing season (April-October) has elapsed and will confirm that stabilization measures are fully established and that the temporary erosion and sediment control measures can be removed.

8.5 - Termination Inspection

A qualified inspector will conduct a termination inspection once all disturbed areas have achieved final stabilization no sooner than one (1) year after completion of activities. This inspection will confirm that stabilization measures remain fully established. Upon verification that the site meets permit requirements, the permittee shall submit the Termination Inspection report with the Notice of Termination form in accordance with the Permit.

8.6 - Recordkeeping Requirements

CT DEEP will retain the Plan and all reports required by the Permit, and records of data used to complete the permit registration, for at least five years from the date the Notice of Termination is accepted by the Commissioner unless the commissioner specifies another time period in writing. CT DEEP will retain an updated copy of the Plan at the site from the date construction is initiated at the site until the date construction at the site is completed. Inspection records, including plan implementation inspections and routine inspections, will also be retained at the site for a period of five years from the date recorded on the inspection form. The construction site “working” copy will be kept onsite at CT DEEP. A copy of the SWPCP will also be made available via a publicly accessible URL during the term of the permit.

CT DEEP will retain a copy of the Plan, as amended, for a period of at least five years from the date that construction at the site is completed (unless the DEEP Commissioner specifies another time period in writing) and maintain a copy at the construction site from the date construction is initiated to the date of completion. CT DEEP’s copy will be kept at:

Connecticut Department of Energy and Environmental Protection
Engineering, Safety, and Sustainability Division – Engineering Unit
163 Great Hill Road
Portland, CT 06480

8.7 - Reporting Requirements

CT DEEP will provide the Plan, upon request, to the Commissioner within the timeframe specified in any request by the Commissioner. If no timeframe is specified in any such request, reporting shall be provided no later than thirty days from the request. CT DEEP, or the Signatory Authority, will submit all reporting of inspections, Plan updates or other reporting electronically. Electronic reporting shall commence no later than thirty (30) days after authorization under this permit unless otherwise approved in writing from the Commissioner.

Upon learning of a violation of a condition of the permit, CT DEEP will immediately cease all construction activities and take reasonable action to determine the cause of such violation, return to compliance, correct and mitigate the results of such violation, prevent further such violation from recurring, and report such violation and such corrective action to the CT DEEP stormwater staff within two (2) hours of CT DEEP learning of such violation. CT DEEP stormwater staff can be contacted at the following:

- email (deep.stormwaterstaff@ct.gov) and;
- phone (860.424.3025).

In addition to contacting CT DEEP stormwater staff upon discovery of any violation(s), CT DEEP will prepare and submit to the commissioner a written report documenting the violation including the duration (date and time) of the violation, corrective actions taken to address the violation, and any action taken or planned to prevent future occurrences within five (5) days of the violation.

If dewatering is performed, records of water quality monitoring conducted will be submitted to the Commissioner on the first day of each month following the initiation of the dewatering discharge for as long as the discharge exists.

9.0 - CONTRACTORS

The SWPCP includes a blank form in Appendix A to clearly identify each contractor and subcontractor that will perform actions on the site which may reasonably be expected to cause or have the potential to cause impacts to the waters of the state. The form includes a certification statement noting compliance to adhere to the general permit terms and conditions to be signed by all contractors and subcontractors. CT DEEP will provide a copy of the Plan to all contractors prior to any disturbance activities.

10.0 - PLAN AMENDMENTS

CT DEEP has the authority and responsibility to modify the Plan in accordance with the Permit conditions, requirements or guidelines, and will maintain a copy of the Plan, Plan modifications, if any, and site inspection reports. CT DEEP will amend the Plan whenever:

- there is a change in contractors or subcontractors at the site;
- a change in design, construction, operation, or maintenance at the site which has the potential for the discharge of pollutants to the waters of the state and which has not otherwise been addressed in the Plan, or;
- if the actions required by the Plan fail to prevent pollution to waters of the state.

It should be noted that if plan changes are not made in a timely manner, it does not relieve CT DEEP of the responsibility to implement any actions to protect the waters of the state and comply with all conditions of the permit. This includes, but is not limited to, installation and maintenance of all controls and management measures described within the Plan.

If the amount of disturbed area increases from the amount specified in the registration approved by the Commissioner or there are changes to engineered or non-engineered construction or post-construction control measures that have the potential to increase the quality or quantity of pollution in the site's stormwater discharges, CT DEEP shall submit a new registration to the commissioner in accordance with Section 4 of the Permit.

If notified at any time by the commissioner that the Plan and/or site do not meet one or more of the minimum requirements of the Permit, CT DEEP will make the required changes to the Plan and perform all actions required by such revised Plan within seven days. Within 15 days of such notice, or such other time as the commissioner may allow, CT DEEP will submit to the commissioner a written certification that the requested changes have been made and implemented and such other information as the commissioner requires, accordance with the permit.

Additionally, if warranted by the results of the inspection, the description of potential sources and pollution prevention measures identified in the Plan will be revised as appropriate as soon as practicable after such inspection. Such modifications will provide for timely implementation of any changes to the site within 24 hours and implementation of any changes to the Plan within three calendar days following the inspection. The Plan will be revised and the site controls updated in accordance with sound engineering practices, the Guidelines, and the Permit.

11.0 - SIGNATURES OF REPORT AUTHORS

This report has been prepared by Triton Environmental, LLC. The names listed below are the principal authors of this report. Requests for information regarding the content of this report should be directed to those individuals.

Stephen Benben, P.E.
Vice President

J. Carver Glezen, LEP
President

FIGURES

FIGURE 1

Site Location Map


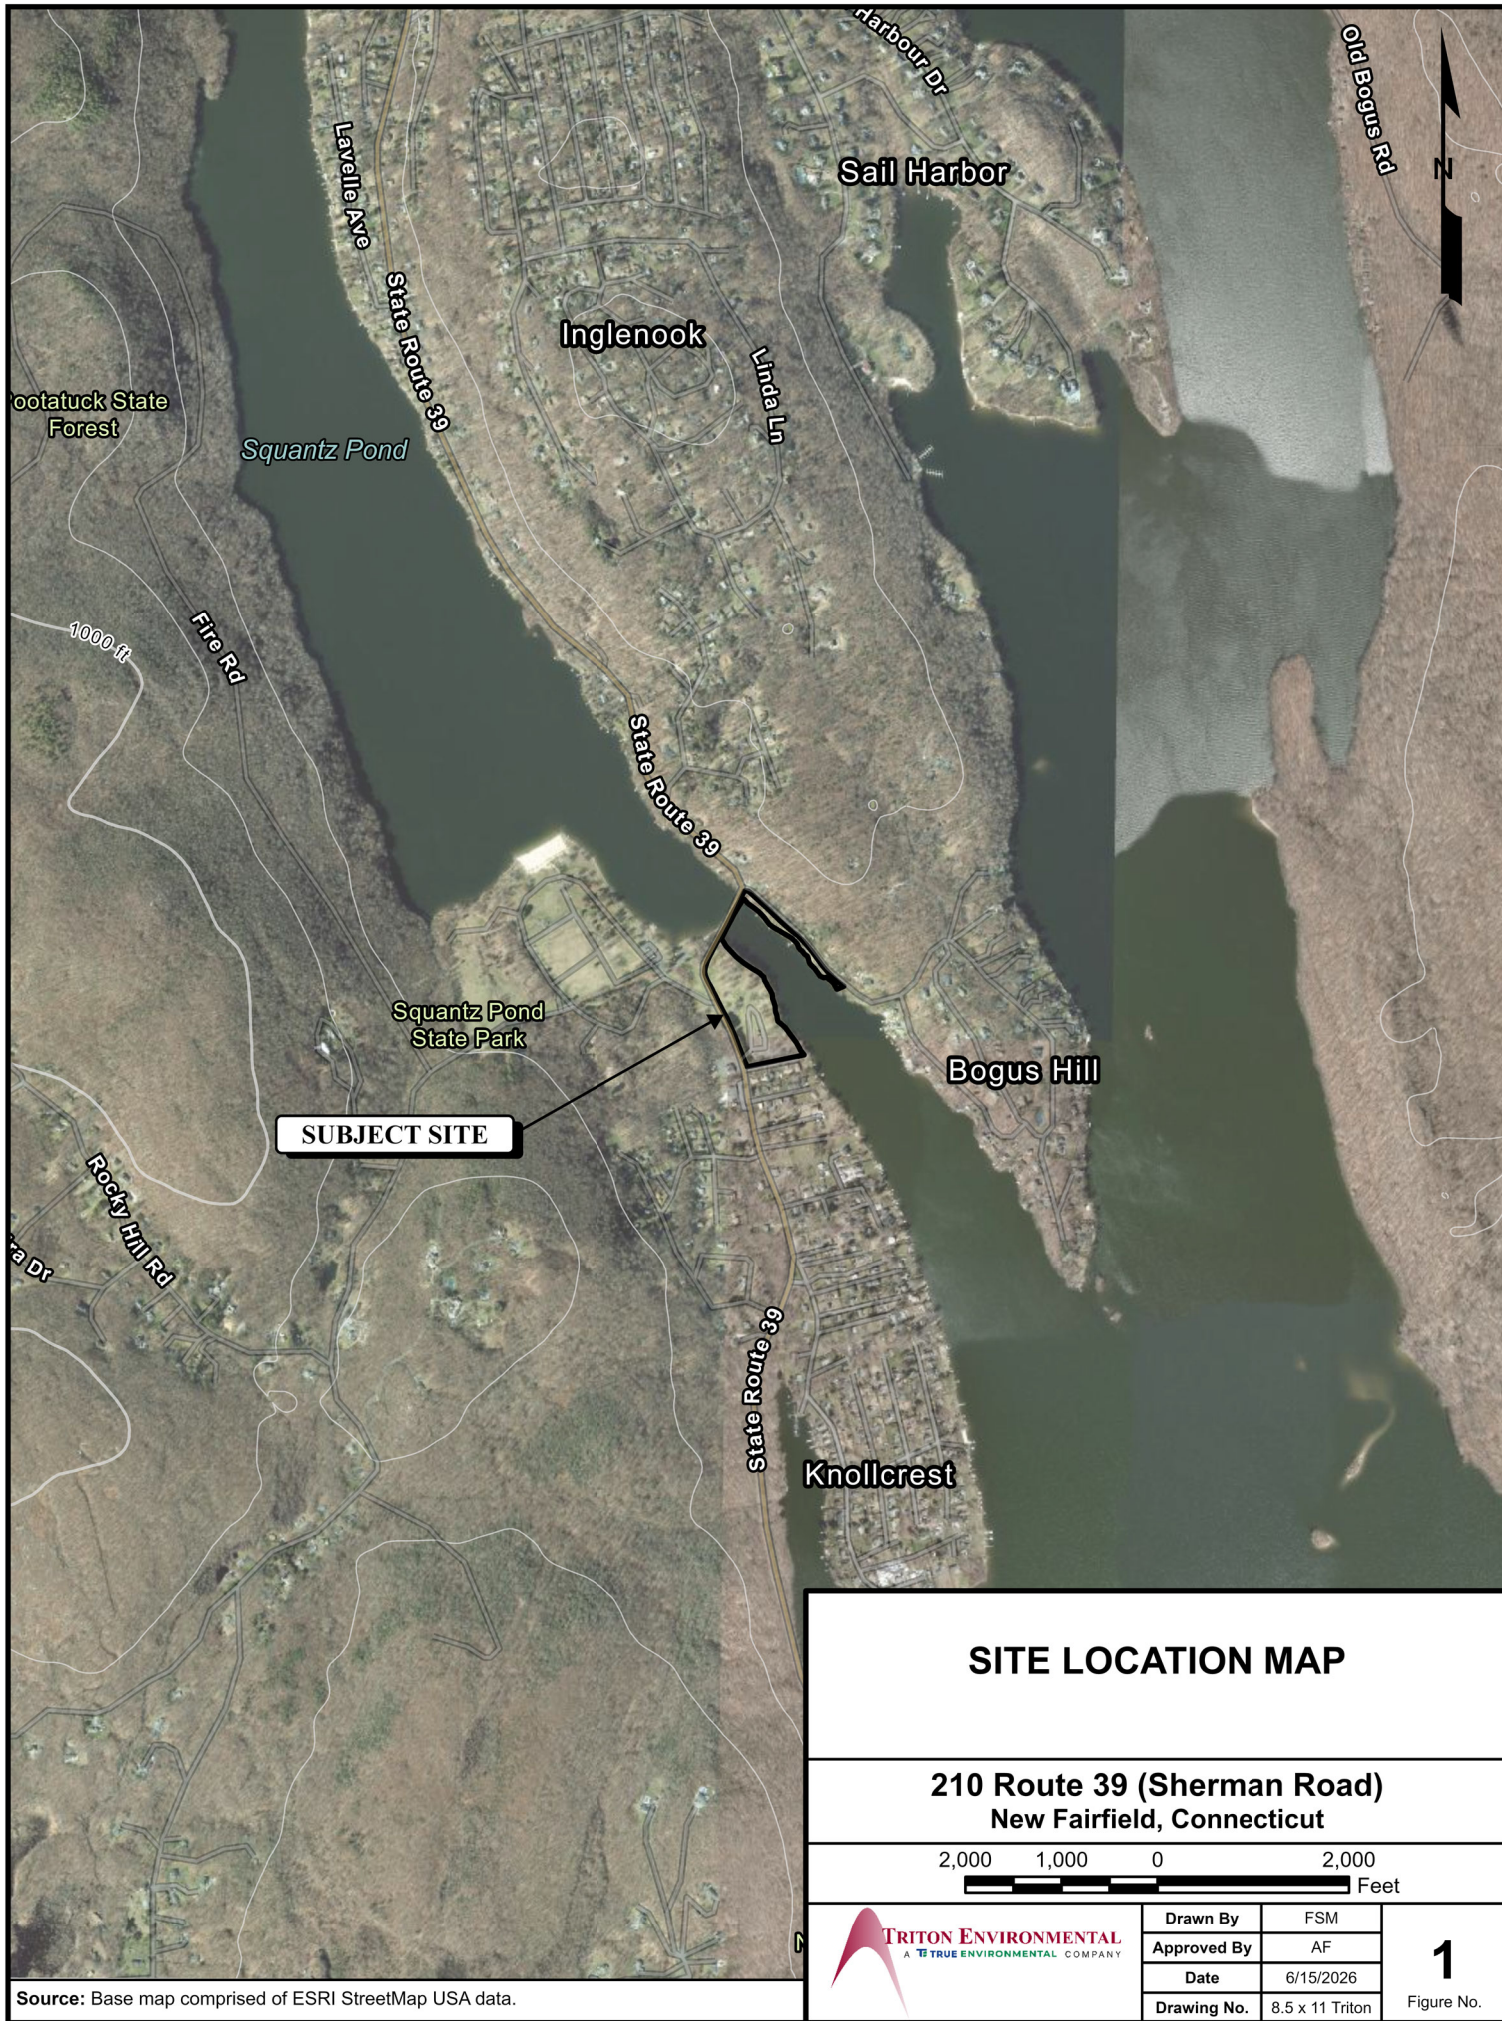


FIGURE 2
Existing Conditions Plan

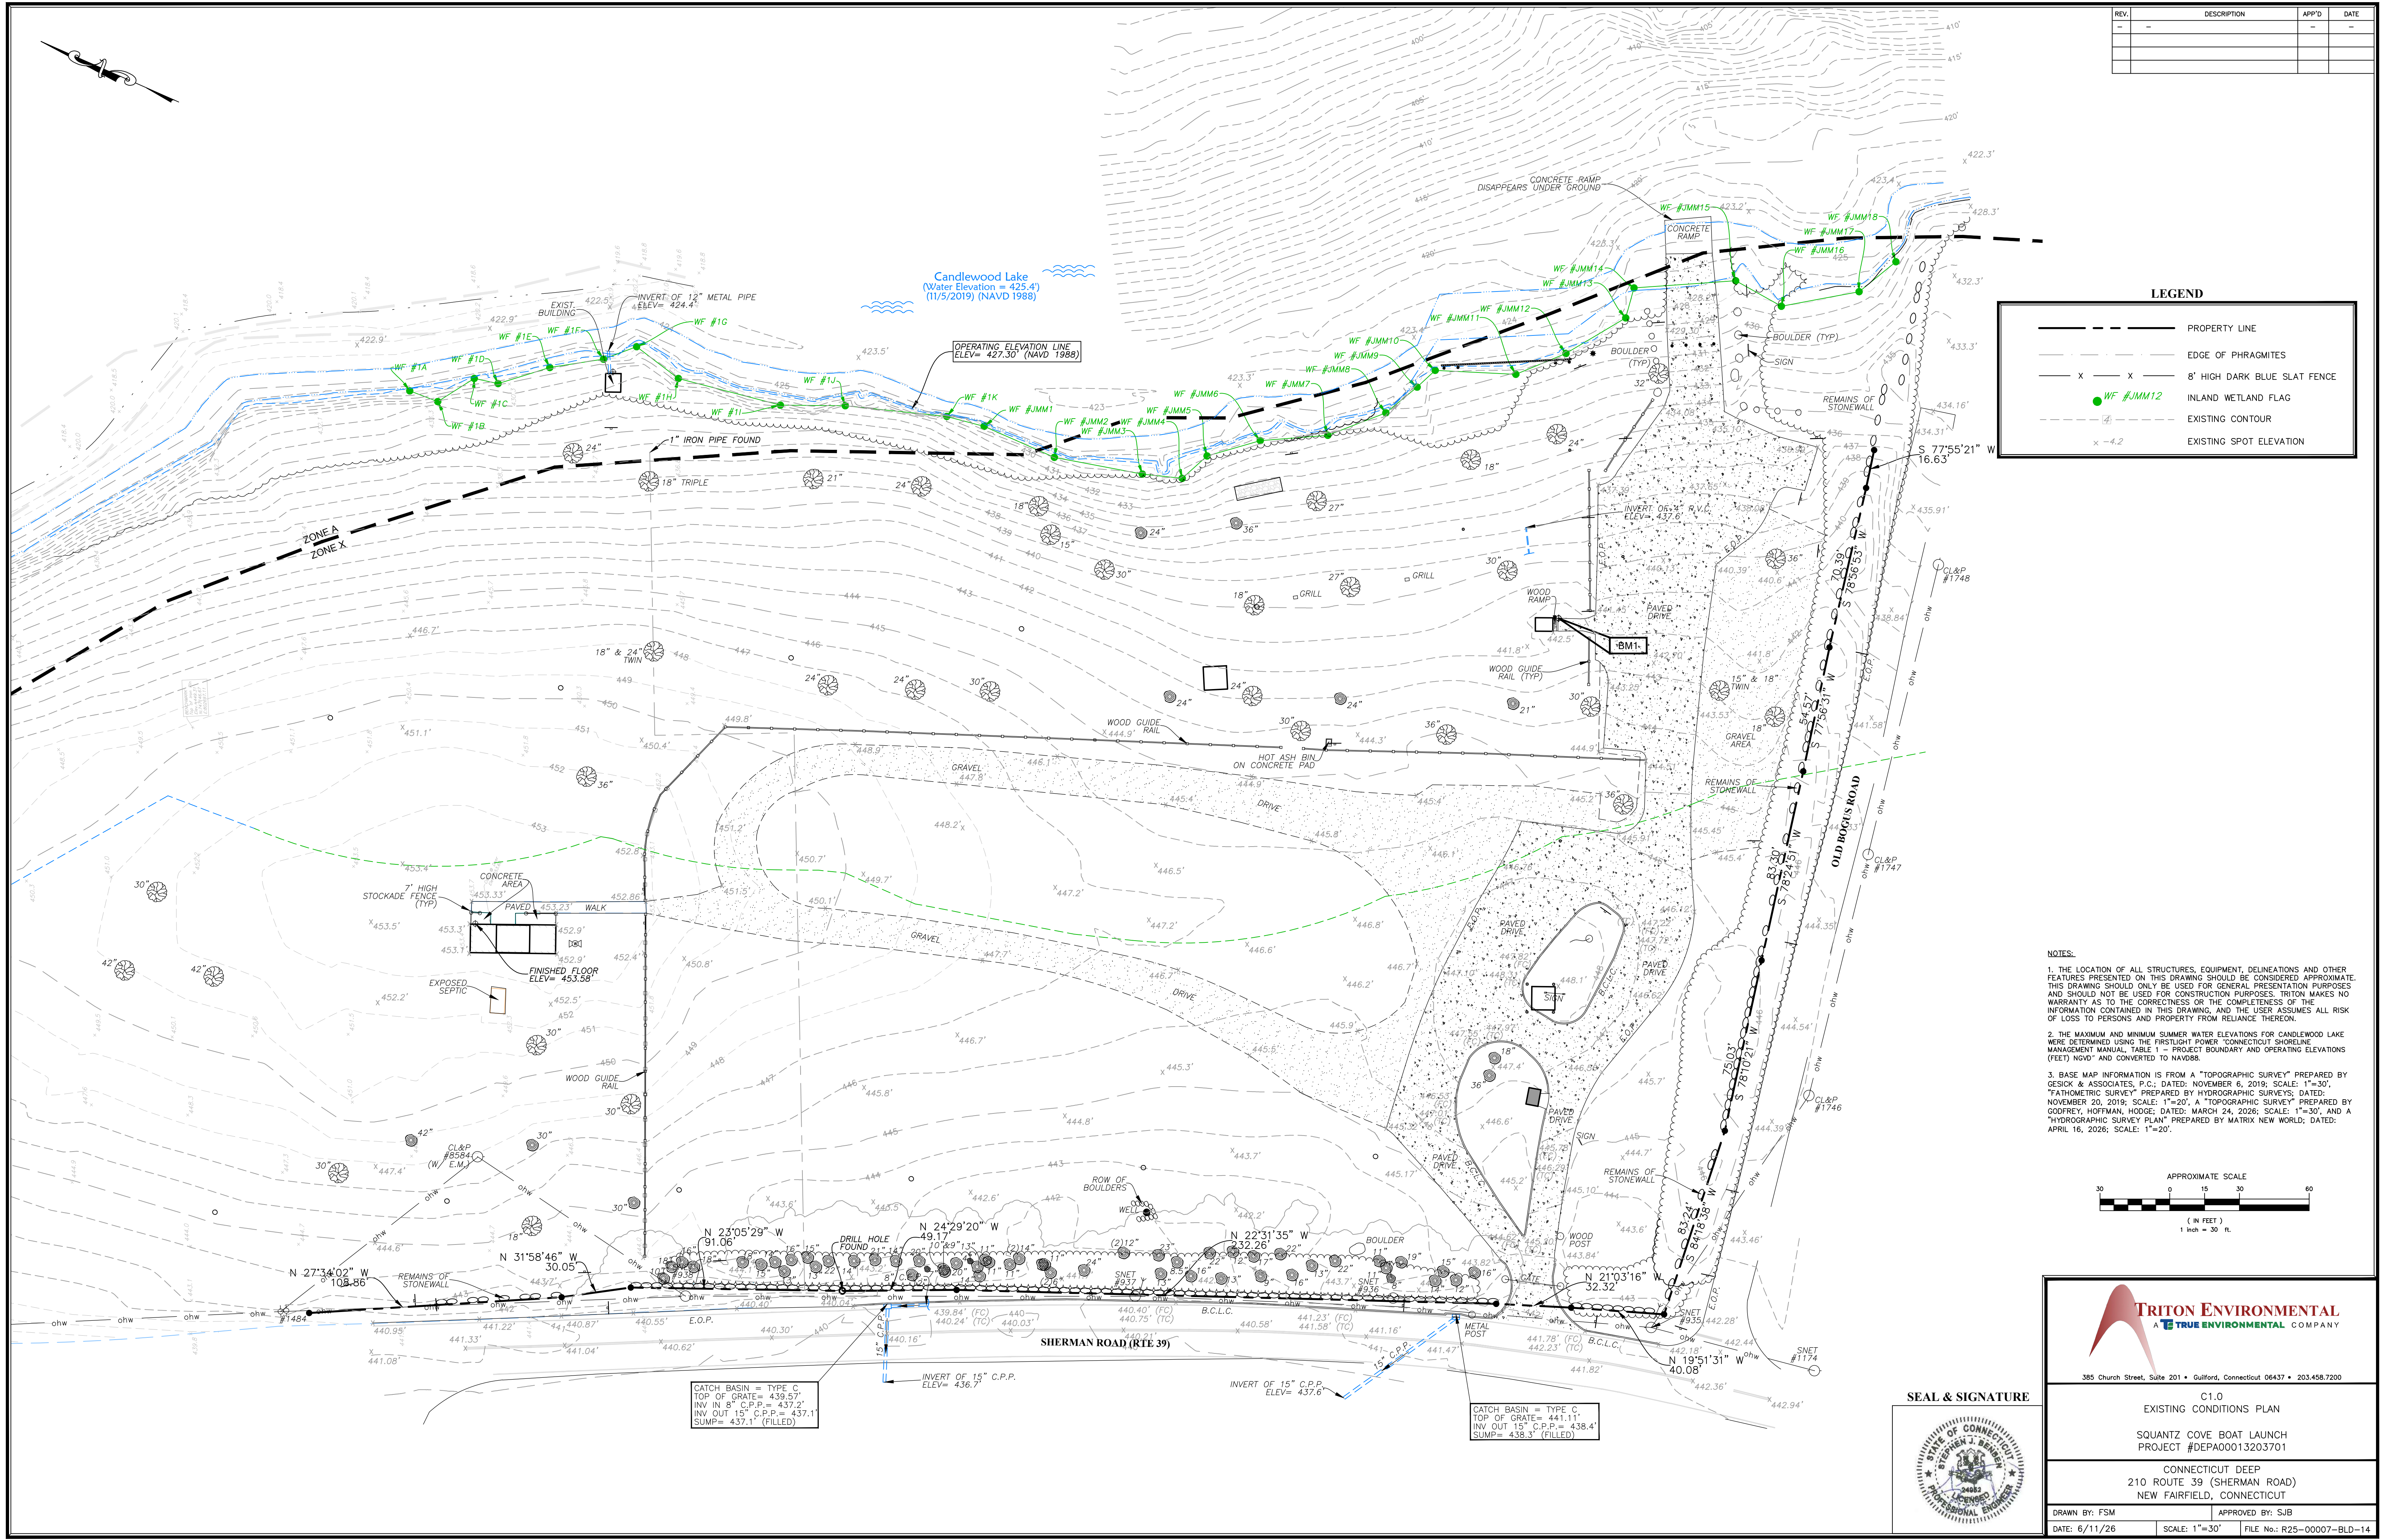

REV.	DESCRIPTION	APP'D	DATE
1			
2			
3			
4			
5			
6			
7			
8			
9			
10			

LEGEND


- PROPERTY LINE
- - - EDGE OF PHRAGMITES
- x - 8' HIGH DARK BLUE SLAT FENCE
- WF #JMM12 INLAND WETLAND FLAG
- - - EXISTING CONTOUR
- x -4.2 EXISTING SPOT ELEVATION

NOTES:

1. THE LOCATION OF ALL STRUCTURES, EQUIPMENT, DELINEATIONS AND OTHER FEATURES PRESENTED ON THIS DRAWING SHOULD BE CONSIDERED APPROXIMATE. THIS DRAWING SHOULD ONLY BE USED FOR GENERAL PRESENTATION PURPOSES AND SHOULD NOT BE USED FOR CONSTRUCTION PURPOSES. TRITON MAKES NO WARRANTY AS TO THE CORRECTNESS OR THE COMPLETENESS OF THE INFORMATION CONTAINED IN THIS DRAWING, AND THE USER ASSUMES ALL RISK OF LOSS TO PERSONS AND PROPERTY FROM RELIANCE THEREON.

2. THE MAXIMUM AND MINIMUM SUMMER WATER ELEVATIONS FOR CANDLEWOOD LAKE WERE DETERMINED USING THE FIRSTLIGHT POWER CONNECTICUT SHORELINE MANAGEMENT MANUAL, TABLE 1 - PROJECT BOUNDARY AND OPERATING ELEVATIONS (FEET) NGVD, AND CONVERTED TO NAVD83.


3. BASE MAP INFORMATION IS FROM A "TOPOGRAPHIC SURVEY" PREPARED BY GOSK & ASSOCIATES, P.C., DATED: NOVEMBER 6, 2019; SCALE: 1"=30', "FATHOMETRIC SURVEY" PREPARED BY HYDROGRAPHIC SURVEYS, DATED: NOVEMBER 20, 2019; SCALE: 1"=20', A "TOPOGRAPHIC SURVEY" PREPARED BY GOSK & ASSOCIATES, P.C., DATED: MARCH 24, 2020; SCALE: 1"=30', AND A "HYDROGRAPHIC SURVEY" PREPARED BY MATRIX NEW WORLD, DATED: APRIL 16, 2020; SCALE: 1"=20'.



TRITON ENVIRONMENTAL
A TRUE ENVIRONMENTAL COMPANY

385 Church Street, Suite 201 • Guilford, Connecticut 06437 • 203.458.7200

SEAL & SIGNATURE



C1.0
EXISTING CONDITIONS PLAN

SQUANTZ COVE BOAT LAUNCH
PROJECT #DEPA00013203701

CONNECTICUT DEEP
210 ROUTE 39 (SHERMAN ROAD)
NEW FAIRFIELD, CONNECTICUT

DRAWN BY: FSM
APPROVED BY: SJB

DATE: 6/11/26
SCALE: 1"=30'
FILE: R25-00007-BLD-14

FIGURE 3

Site Plan Showing Sediment and Erosion Controls

VEGETATIVE COVER FOR DISTURBED AREAS

SEEDING SCHEDULE			
	SEED MIX	SEEDING SEASON	
TEMPORARY:	100% ANNUAL RYEGRASS	MARCH 1 TO JUNE 15 AUGUST 1 TO OCT. 15	
PERMANENT:	48% CREEPING RED FESCUE 4% RED TOP 48% TALL FESCUE OR SMOOTH BLUEGRASS OR EQUAL	APRIL 15 TO JUNE 15 AUGUST 15 TO SEPT. 15	

APPLICATION RATES PER 1000 SF			
	SEED MIX	FERTILIZER	LIME HAY MULCH
TEMPORARY:	1 LB.	7.5 LBS.	45 LBS. 70-90 LBS.
PERMANENT:	0.95 LB.	7.5 LBS.	90 LBS. 70-90 LBS.

TEMPORARY HAY MULCH

TO BE USED IN AREAS WHICH CANNOT BE SEEDED WITHIN THE SPECIFIED SEEDING SEASONS.

APPLICATION RATE: 70-90 LBS. PER 1000 SQUARE FEET


A SYNTHETIC LIQUID MULCH BINDER SHALL BE APPLIED OVER ALL HAY MULCH AT THE RATES SPECIFIED BY THE MANUFACTURER.

EROSION CONTROL MEASURES	
MAP SYMBOL	DESCRIPTION
ECB	EROSION CONTROL BLANKET
GSF	GEOTEXTILE SILT FENCE
PS	PERMANENT SEEDING
PUP	PUMP INTAKE PROTECTION
DWM	DEWATERING OF EARTH MATERIALS
CE	CONSTRUCTION ENTRANCE
PST	PORTABLE SETTLING TANK


REV.	DESCRIPTION	APP'D	DATE
1			
2			
3			

LEGEND

	PROPERTY LINE
	PROPOSED CLEARING LIMIT
	SURFACE FLOW DIRECTION
	INLAND WETLAND FLAG
	EXISTING CONTOUR
	EXISTING SPOT ELEVATION
	PROPOSED CONTOUR
	PROPOSED SPOT ELEVATION
	GEOTEXTILE SILT FENCE
	COFFERDAM
	CONSTRUCTION ENTRANCE
	EROSION CONTROL BLANKET
	GEOTEXTILE SILT BAG

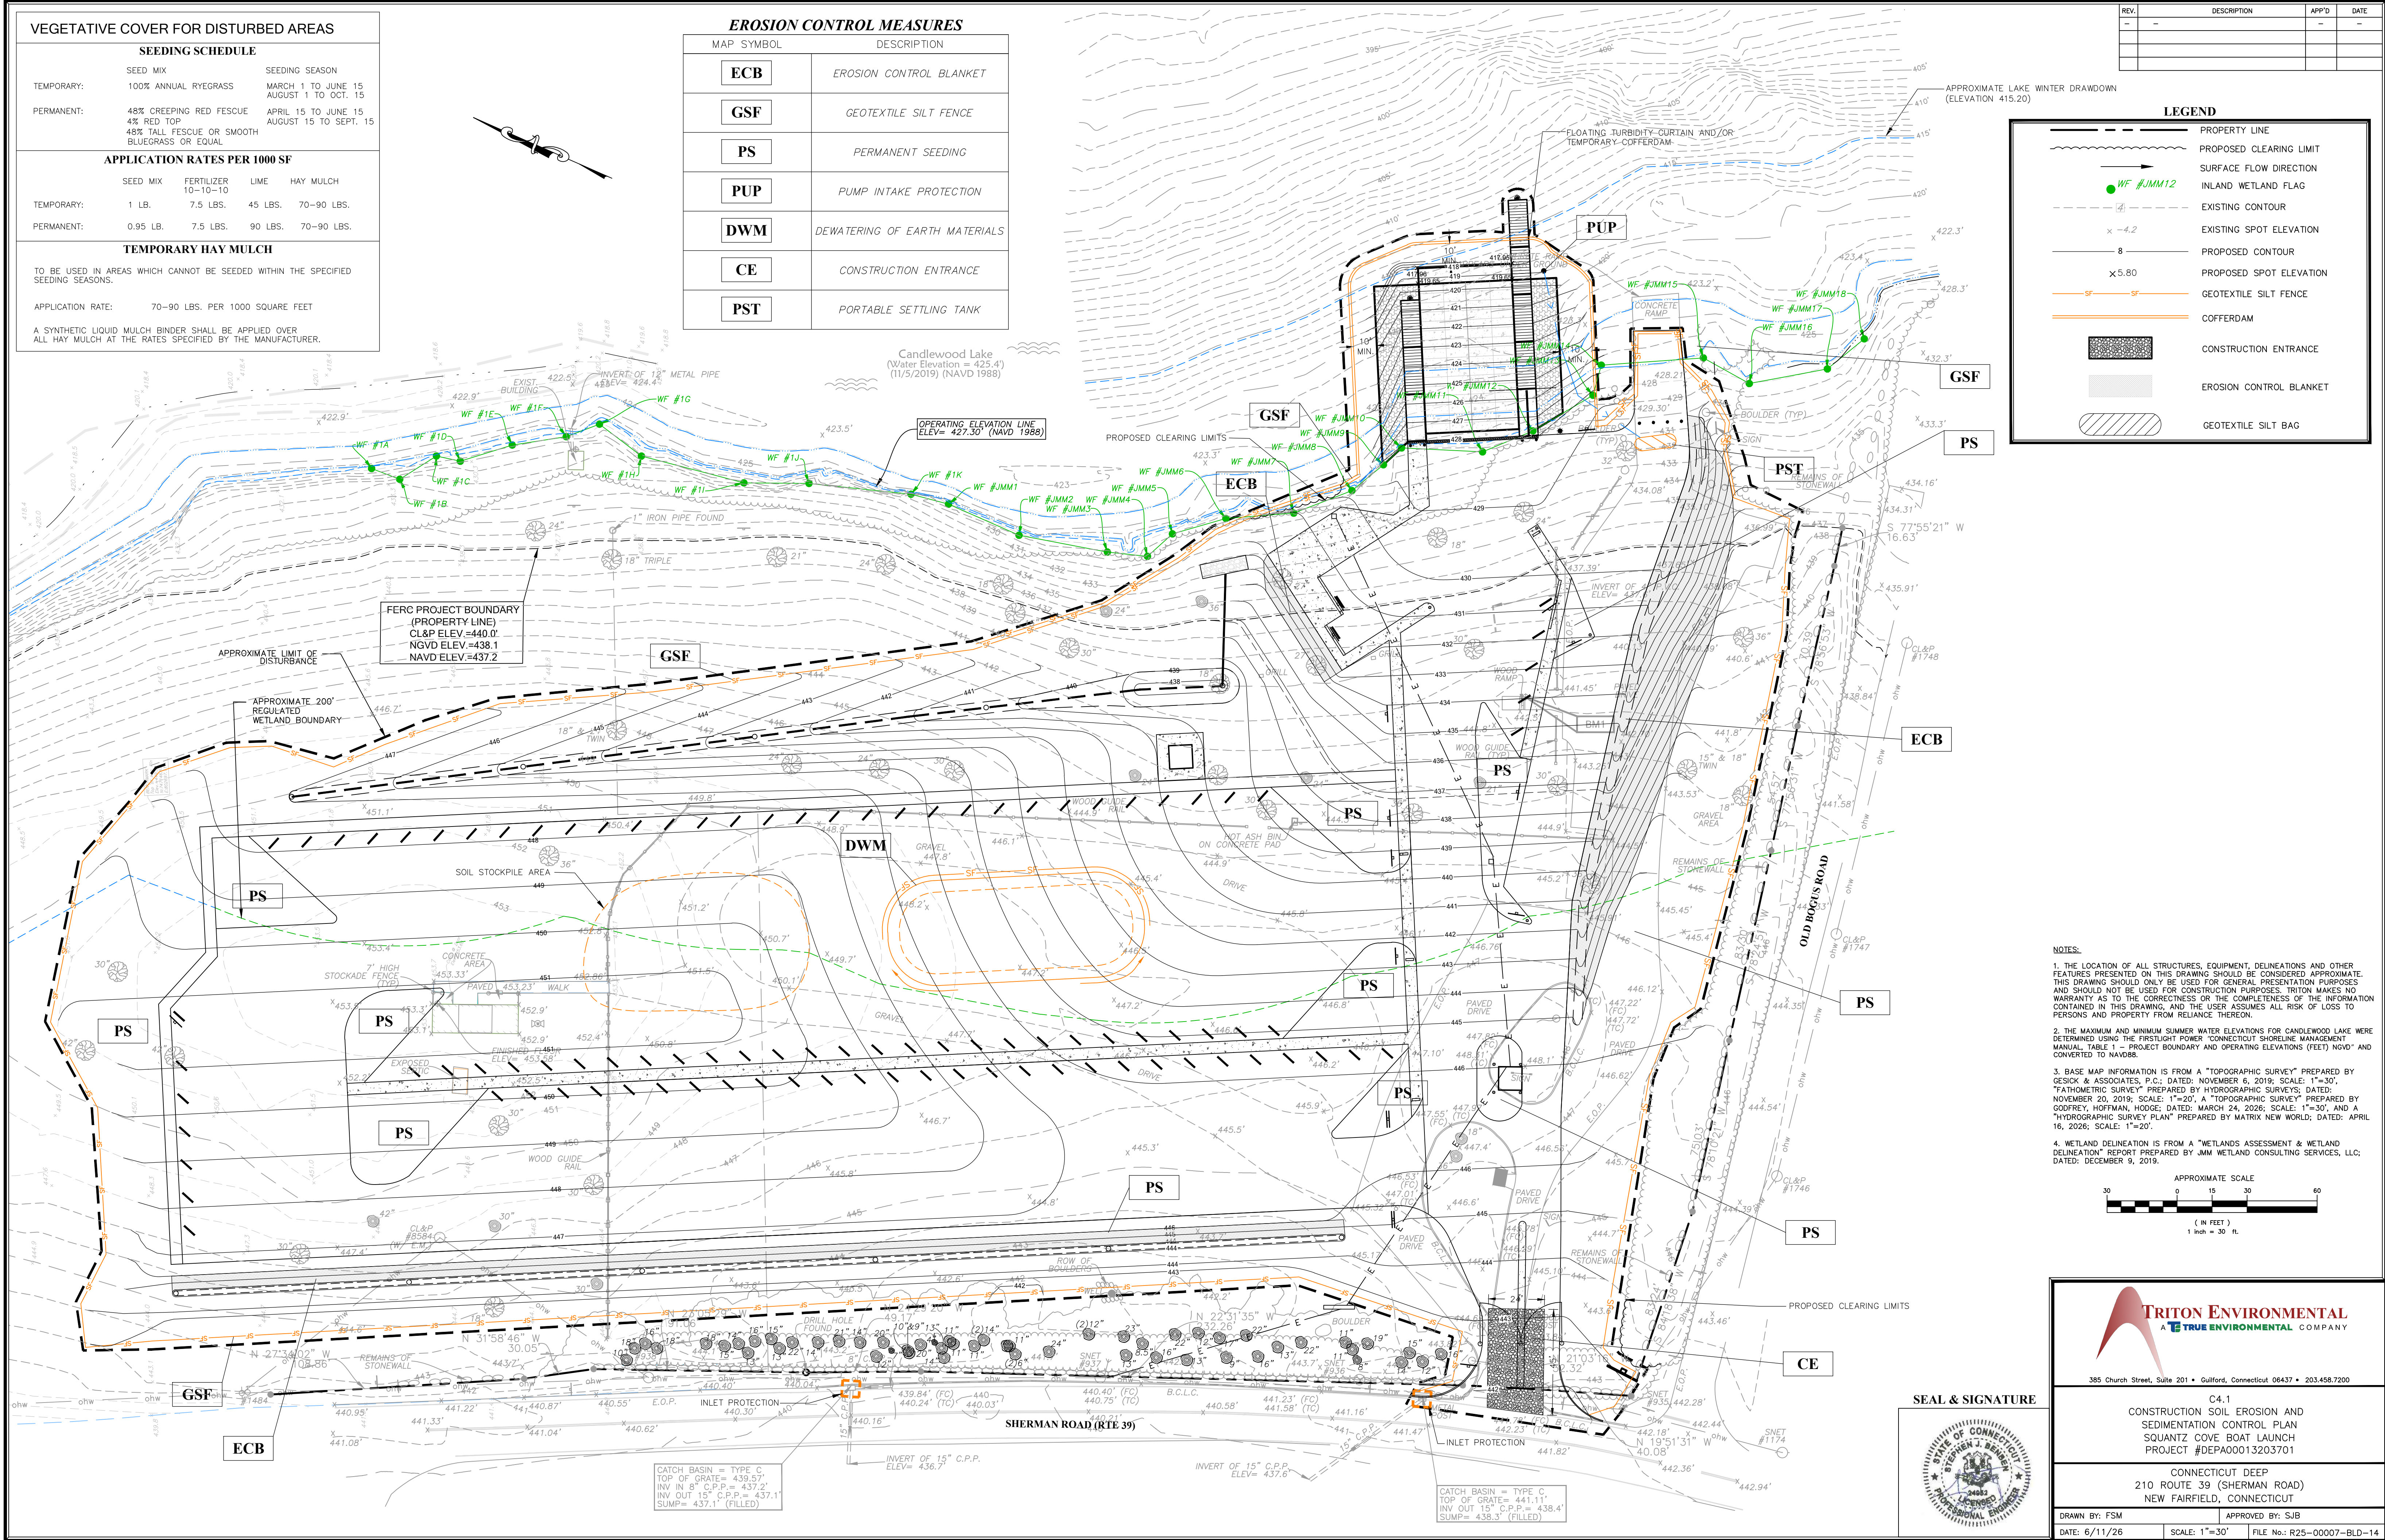

- NOTES:
- THE LOCATION OF ALL STRUCTURES, EQUIPMENT, DELINEATIONS AND OTHER FEATURES PRESENTED ON THIS DRAWING SHOULD BE CONSIDERED APPROXIMATE. THIS DRAWING SHOULD ONLY BE USED FOR GENERAL PRESENTATION PURPOSES AND SHOULD NOT BE USED FOR CONSTRUCTION PURPOSES. TRITON MAKES NO WARRANTY AS TO THE CORRECTNESS OR THE COMPLETENESS OF THE INFORMATION CONTAINED IN THIS DRAWING, AND THE USER ASSUMES ALL RISK OF LOSS TO PERSONS AND PROPERTY FROM RELIANCE THEREON.
 - THE MAXIMUM AND MINIMUM SUMMER WATER ELEVATIONS FOR CANDLEWOOD LAKE WERE DETERMINED USING THE FIRSTLIGHT POWER "CONNECTICUT SHORELINE MANAGEMENT MANUAL, TABLE 1 - PROJECT BOUNDARY AND OPERATING ELEVATIONS (FEET) NAVD" AND CONVERTED TO NAVD88.
 - BASE MAP INFORMATION IS FROM A "TOPOGRAPHIC SURVEY" PREPARED BY GESICK & ASSOCIATES, P.C.; DATED: NOVEMBER 6, 2019; SCALE: 1"=30', "FATHOMETRIC SURVEY" PREPARED BY HYDROGRAPHIC SURVEYS; DATED: NOVEMBER 20, 2019; SCALE: 1"=20', A "TOPOGRAPHIC SURVEY" PREPARED BY GODFREY, HOFFMAN, HODGE; DATED: MARCH 24, 2026; SCALE: 1"=30', AND A "HYDROGRAPHIC SURVEY PLAN" PREPARED BY MATRIX NEW WORLD; DATED: APRIL 16, 2026; SCALE: 1"=20'.
 - WETLAND DELINEATION IS FROM A "WETLANDS ASSESSMENT & WETLAND DELINEATION" REPORT PREPARED BY JMM WETLAND CONSULTING SERVICES, LLC; DATED: DECEMBER 9, 2019.



385 Church Street, Suite 201 • Guilford, Connecticut 06437 • 203.458.7200

C4.1
CONSTRUCTION SOIL EROSION AND
SEDIMENTATION CONTROL PLAN
SQUANTZ COVE BOAT LAUNCH
PROJECT #DEPA00013203701

CONNECTICUT DEEP
210 ROUTE 39 (SHERMAN ROAD)
NEW FAIRFIELD, CONNECTICUT

DRAWN BY: FSM	APPROVED BY: SJB
DATE: 6/11/26	SCALE: 1"=30' FILE No.: R25-00007-BLD-14

SEAL & SIGNATURE

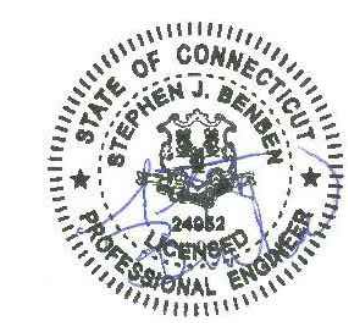


FIGURE 4

Sediment and Erosion Control Details

GENERAL EROSION AND SEDIMENT CONTROL NOTES

1. LAND DISTURBANCE WILL BE KEPT TO A MINIMUM; RESTABILIZATION WILL BE SCHEDULED AS SOON AS POSSIBLE.
2. SILT FENCE WILL BE INSTALLED ALONG THE TOE OF ALL CRITICAL CUT AND FILL SLOPES, SOIL STOCKPILE AREAS, AND IN THOSE AREAS SHOWN ON THE PLANS.
3. ALL EROSION AND SEDIMENT CONTROL MEASURES WILL BE CONSTRUCTED IN ACCORDANCE WITH THE STANDARDS AND SPECIFICATIONS OF THE STATE OF CONNECTICUT GUIDELINES FOR SOIL EROSION AND SEDIMENT CONTROL 2026.
4. EROSION AND SEDIMENT CONTROL MEASURES WILL BE INSTALLED PRIOR TO LAND DISTURBANCE WHENEVER POSSIBLE.
5. ALL TEMPORARY EROSION AND SEDIMENTATION CONTROL MEASURES SHALL BE PROPERLY MAINTAINED UNTIL STABILIZATION HAS BEEN ACHIEVED.
6. ADDITIONAL CONTROL MEASURES WILL BE INSTALLED DURING THE CONSTRUCTION PERIOD IF NECESSARY OR REQUIRED. A MINIMUM OF 50 FEET OF SILT FENCE SHALL BE STORED AT THE SITE FOR EMERGENCY USE.
7. ANY EXCAVATIONS THAT MUST BE DEWATERED WILL BE PUMPED INTO AN ACTIVE DRAINAGE SYSTEM OR DISPERSED IN AN UNDISTURBED AREA NOT SUBJECT TO EROSION, AND USE OF A DE-WATERING BAG OR OTHER OUTLET TREATMENT METHOD. THE INLETS OF ALL PUMPS ARE TO BE FLOATED A MINIMUM OF 24 INCHES OFF THE BOTTOM OF EXCAVATION.
8. WATER AND CALCIUM CHLORIDE SHALL BE APPLIED TO UNPAVED ACCESSWAYS TO PREVENT WIND GENERATED SEDIMENTS AND DUST.
9. DEBRIS AND OTHER WASTES RESULTING FROM EQUIPMENT MAINTENANCE AND CONSTRUCTION ACTIVITIES WILL NOT BE DISCARDED ON-SITE.
10. SEDIMENT REMOVED FROM CONTROL STRUCTURES WILL BE DISPOSED OF IN A MANNER WHICH IS CONSISTENT WITH INTENT OF THE PLAN.
11. SILT FENCES SHALL HAVE SEDIMENT REMOVED WHEN THE DEPTH OF THE SEDIMENT IS EQUAL TO 1/3 TO 1/2 THE HEIGHT OF THE FENCE. FENCES SHALL BE PROPERLY INSTALLED AND RIPPED FENCE OR BROKEN POSTS REPAIRED AS SOON AS PRACTICAL.
12. ANTI-TRACKING PADS AND GRAVEL CHECK DAMS SHALL BE REPLACED WHEN VOID SPACES ARE FULL OR STRUCTURES ARE BREACHED, AS APPLICABLE.
13. TEMPORARY EROSION CONTROL MEASURES SHALL BE REMOVED AND THE SOIL SURFACE STABILIZED WHEN CONSTRUCTION IS COMPLETE AND THE SOIL SURFACES ARE PERMANENTLY STABILIZED. STRUCTURAL COMPONENTS SHALL BE CLEANED OF ALL SEDIMENT UPON COMPLETION OF CONSTRUCTION.
14. THE OWNER IS ASSIGNED THE RESPONSIBILITY FOR IMPLEMENTING THIS EROSION AND SEDIMENT CONTROL PLAN. THIS RESPONSIBILITY INCLUDES INSTALLATION AND MAINTENANCE OF CONTROL MEASURES, INFORMING ALL PARTIES ENGAGED ON THE CONSTRUCTION SITE OF THE REQUIREMENTS AND OBJECTIVES OF THE PLAN, NOTIFYING THE PLANNING AND ZONING COMMISSION OF ANY TRANSFER OF THIS RESPONSIBILITY, AND FOR CONVEYING A COPY OF THE EROSION AND SEDIMENT PLAN IF AND WHEN THE TITLE OF LAND IS TRANSFERRED.

EROSION AND SEDIMENT CONTROL AND CONSTRUCTION SEQUENCE


1. CONSTRUCTION SCHEDULE: THE ANTICIPATED CONSTRUCTION SEQUENCE IS LISTED BELOW. THE TIMEFRAME FOR THE PROPOSED WORK IS ANTICIPATED TO BEGIN IN THE FALL OF 2026 AND BE COMPLETED BY SUMMER OF 2027.
2. CONTACT PERSON: THE OWNER WILL BE THE CONTACT PERSON. THE CONTRACTOR WILL BE RESPONSIBLE FOR MAINTENANCE OF THE EROSION CONTROL MEASURES.
3. ANTICIPATED CONSTRUCTION SEQUENCE:

- GENERAL NOTES
- a. PRE-CONSTRUCTION CONFERENCE
 - b. UTILITY DELINEATION BY CALL BEFORE YOU DIG AT 1-800-922-4455 AND/OR PRIVATE UTILITY LOCATION FIRM TO CONFIRM THE LOCATION OF ON-SITE UNDERGROUND UTILITY IN THE PROJECT AREA

- ANTICIPATED CONSTRUCTION SEQUENCE
- a. MARK BOAT LAUNCH, LOT LIMITS, TOILET BUILDINGS, DRAINAGE FEATURE LOCATIONS, DRIVE LIMITS, AND CLEARING LIMITS.
 - b. INSTALL GEOTEXTILE SILT FENCE (GSF), AS NECESSARY, BETWEEN THE PROJECT AREA AND THE CLEARING LIMITS.
 - c. INLET PROTECTION AND CONSTRUCTION ENTRANCE.
 - d. LOCATE SOIL STOCKPILE AREA AWAY FROM CONSTRUCTION ACTIVITIES. INSTALL GEOTEXTILE SILT FENCE AROUND STOCKPILE.

- e. SELECTIVELY REMOVE FALLEN TREES, STUMPS AND CLEAR AND GRUB VEGETATION IMPACTING THE PROPOSED WORK AREAS AND STOCKPILE OR DISPOSE OFF-SITE.
- f. PERFORM SAWCUTTING AND/OR MILL EXISTING PAVEMENT AS SHOWN ON PLAN.
- g. PERFORM ROUGH GRADING FOR BOAT LAUNCH, LOT, SIDEWALKS, TOILET BUILDINGS, DRAIN SWALES, AND ACCESS DRIVE.
- h. INSTALL BOAT LAUNCH.
- i. INSTALL TRENCH DRAIN AND FLOATING DOCKS.
- j. INSTALL PROPOSED TOILET BUILDINGS.
- m. INSTALL SUBBASE FOR LOT LIMITS AND ACCESS DRIVE, THEN PERFORM FINAL GRADING AND COMPACT.
- n. INSTALL CONCRETE SIDE WALK AROUND LOT LIMITS AND ACCESS DRIVE
- o. INSTALL DRAINAGE SWALE NORTH AND SOUTH OF PROPOSED LOT.
- p. INSTALL PAVEMENT BINDER COURSE AND CURBING
- q. INSTALL FINAL PAVEMENT COURSE
- r. PERFORM LINE TRIPPING AS INDICATED ON THE PLANS.
- s. INSTALL SIGNAGE, CONCRETE WHEEL STOPS AND PAINTED SYMBOLS.
- t. INSTALL SEEDING.

- GENERAL NOTES
- a. AS CONSTRUCTION PROGRESSES, ADDITIONAL SILT FENCE SHOULD BE INSTALLED DOWNSTREAM OF ANY DISTURBED AREAS TO INTERCEPT AND RETAIN SEDIMENT.
 - b. MAINTENANCE OF STABILIZATION AND STRUCTURAL PRACTICES ON THE SITE SHOULD BE PERFORMED IN ACCORDANCE WITH THE GUIDELINES.
 - c. IF ADDITIONAL MAINTENANCE AND/OR MEASURES ARE REQUIRED TO PROTECT THE WATERS OF THE STATE, THE MEASURES WILL BE AMENDED AS NECESSARY.

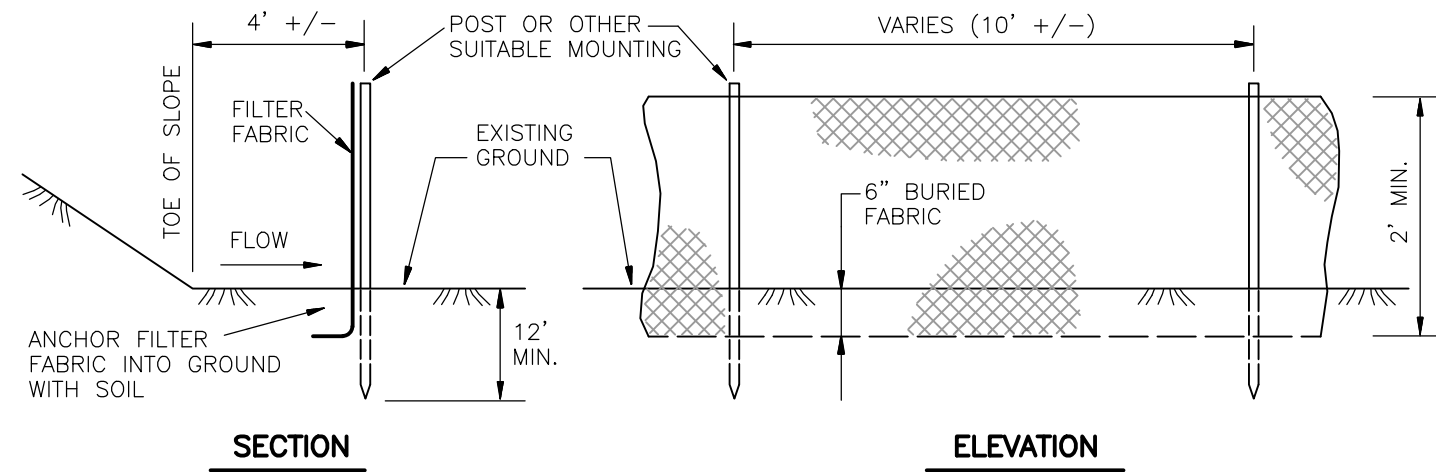


NOTE: POST SPACING AND EMBEDMENT VARIES BASED ON THE FABRIC MANUFACTURER'S REQUIREMENTS.

SILT FENCE SHALL BE AMOCO "SILT STOP" OR EQUIVALENT.


SILT FENCE

NOT TO SCALE

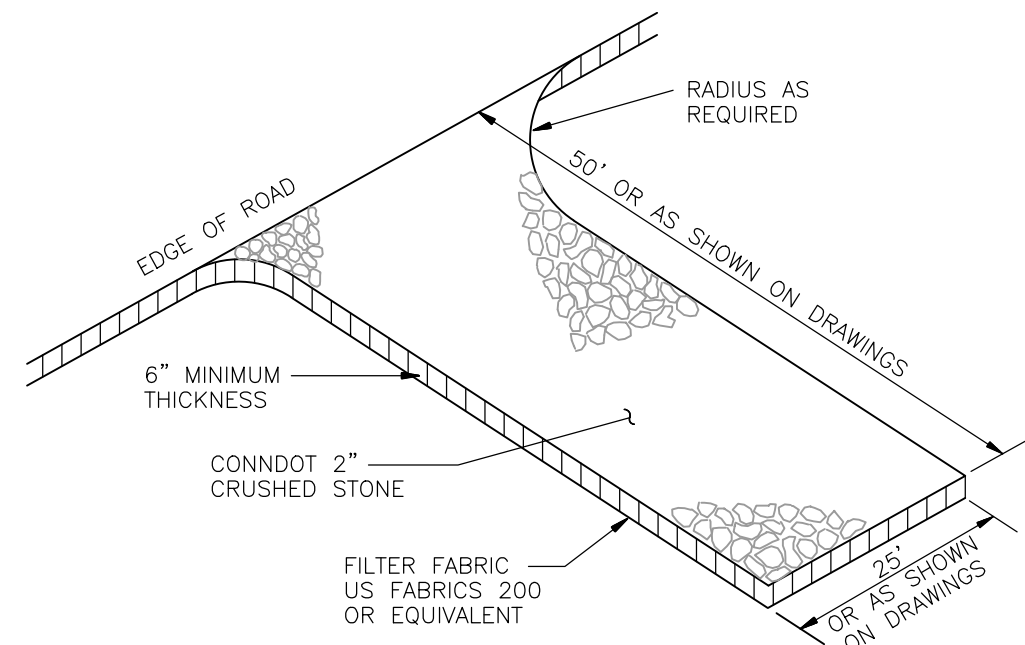


CONSTRUCTION ENTRANCE DETAIL

NOT TO SCALE

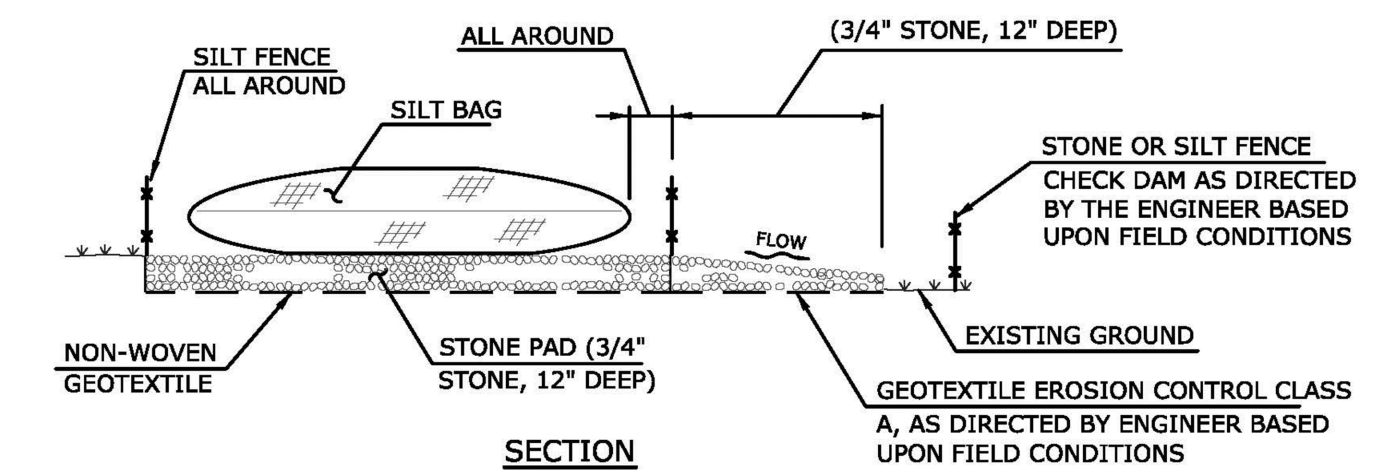


SECTION

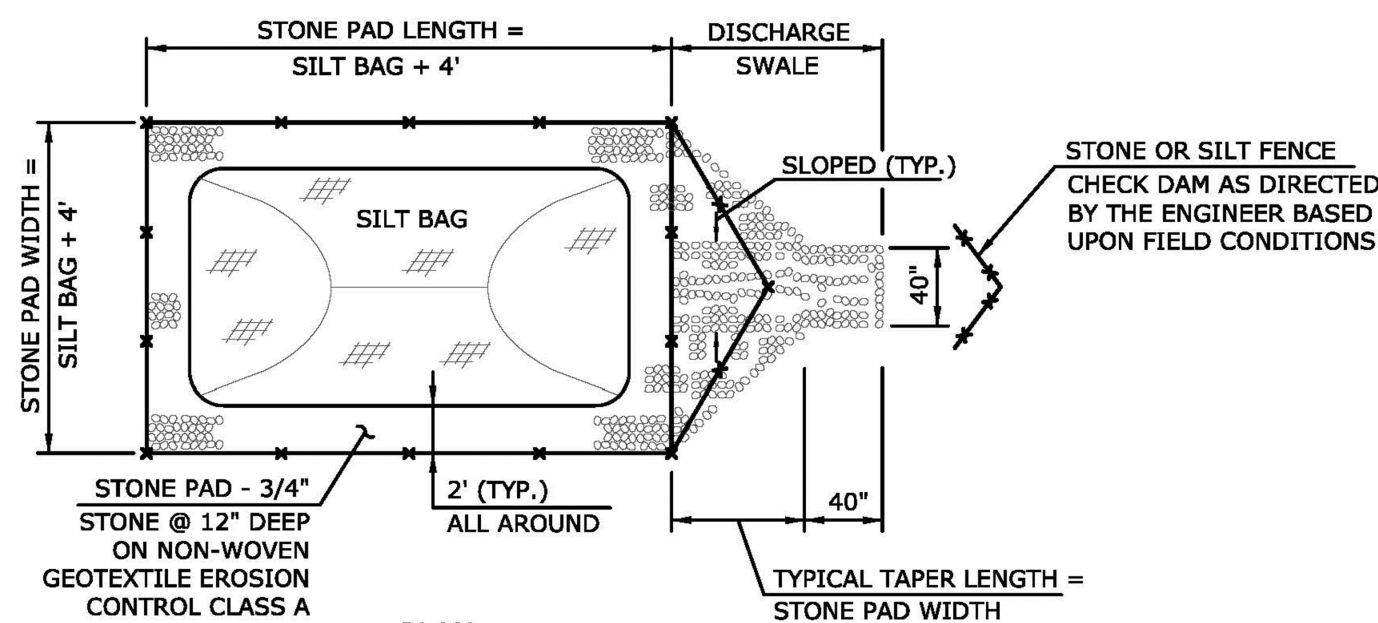

PLAN


SILT BAG INSTALLATION

NOT TO SCALE

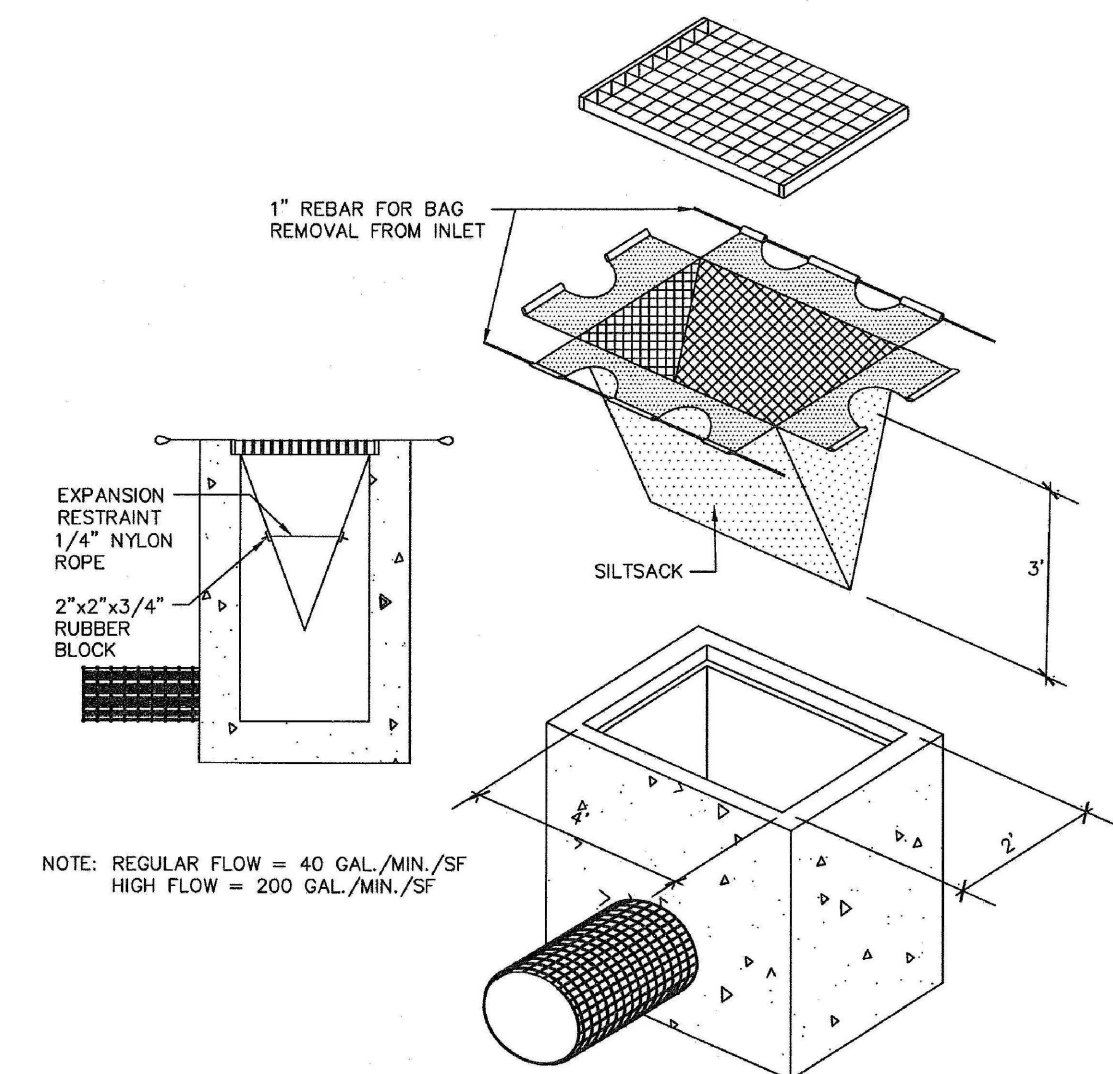


SILTSACK DETAIL

NOT TO SCALE

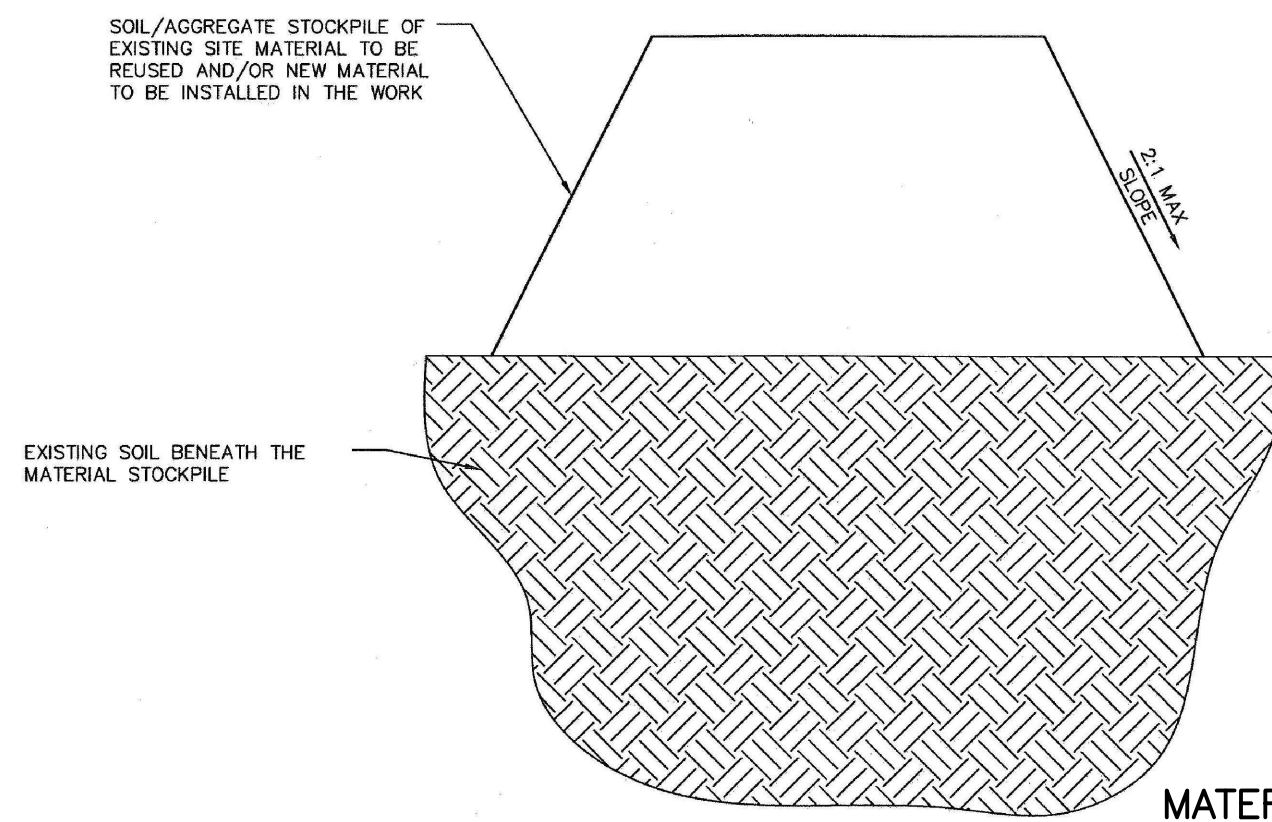


MATERIALS STOCKPILE DETAIL

NOT TO SCALE

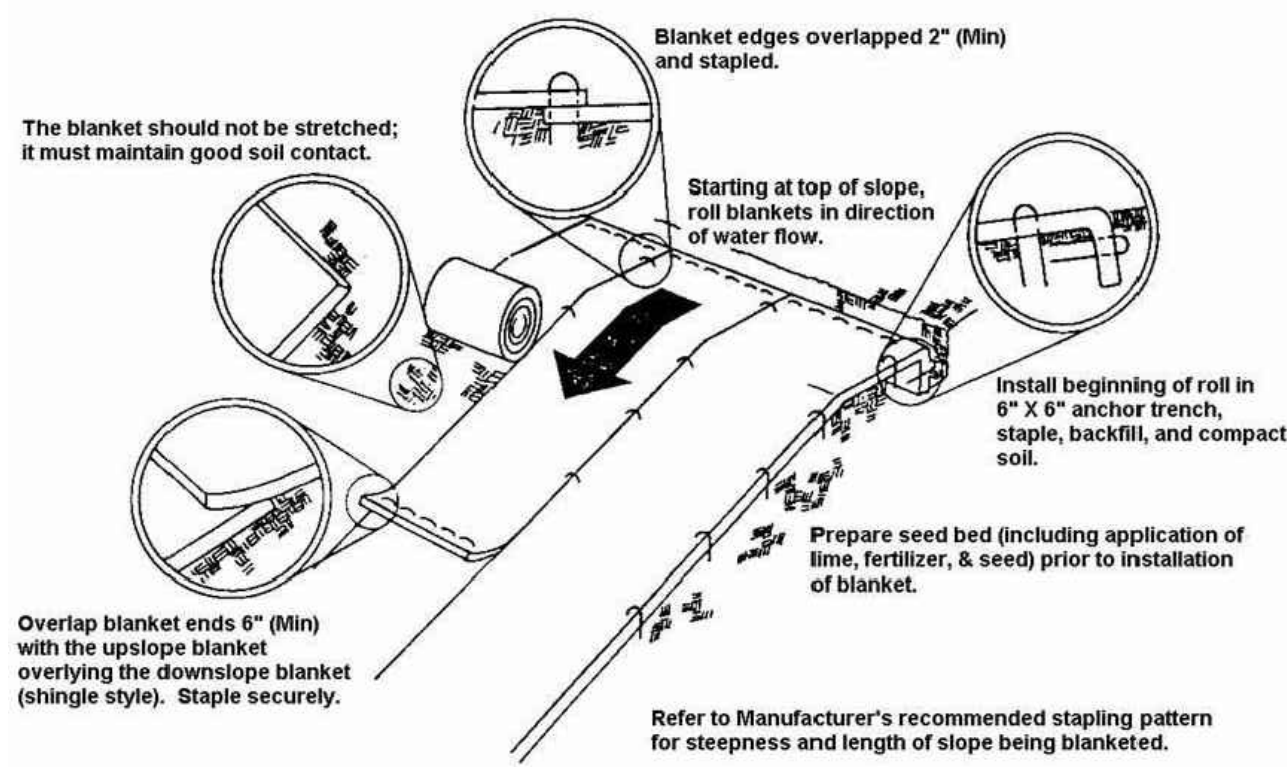

EROSION CONTROL MATTING

NOT TO SCALE

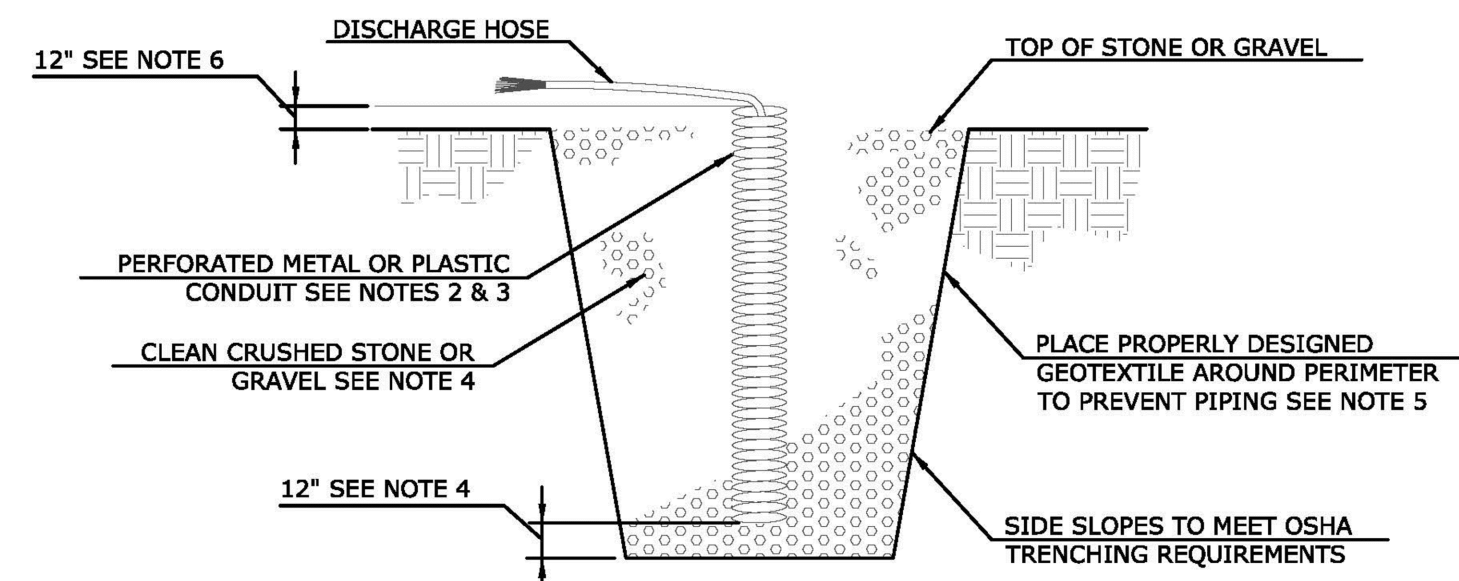

REFER TO PAGE 5-13-3 "CONNECTICUT GUIDELINES FOR SOIL EROSION AND SEDIMENTATION CONTROL".

- NOTE:
1. OVERALL SUMP PIT DIMENSIONS SHALL BE COMPATIBLE WITH ANTICIPATED SEEPAGE RATES AND PUMP SIZE TO BE USED.
 2. THE STANDPIPE DIAMETER AND NUMBER OF PERFORATIONS SHALL BE COMPATIBLE WITH THE PUMP SIZE BEING USED.
 3. PERFORATIONS IN THE STANDPIPE SHALL BE EITHER CIRCULAR OR SLOTS. PERFORATION SIZE SHALL NOT EXCEED 1/2" IN DIAMETER.
 4. CRUSHED STONE OR GRAVEL SHALL BE NO SMALLER THAN CT DOT #8 SIZE NOR LARGER THAN CT DOT #3 SIZE. CRUSHED STONE SHALL EXTEND A MINIMUM OF 12" BELOW THE BOTTOM OF THE STANDPIPE.
 5. IF EXCESSIVE MOVEMENT OF FINE SOIL PARTICLES FROM THE SURROUNDING EXISTING SOILS IS ANTICIPATED, A PROPERLY DESIGNED GEOTEXTILE SHALL BE PLACED BETWEEN THE EXISTING SOILS AND THE CRUSHED STONE OR GRAVEL BACKFILL.
 6. THE STANDPIPE SHALL EXTEND A MINIMUM OF 12" ABOVE THE SURROUNDING GROUND.

PUMP INTAKE
TYPICAL SECTION OF SUMP PIT

NOT TO SCALE

REV.	DESCRIPTION	APP'D	DATE
--	--	--	--

Table 1 – Soil Erosion and Sedimentation Control Measure Maintenance Schedule

E&S Measure	Maintenance Items	Frequency
Roller Erosion Control Product (RECP) or Silt Fence (SF)	• Inspect controls for displacement, damage, or bypass. • Remove sediment, or install a secondary barrier upgradient of the original control when deposits reach approximately half of the height of the control.	Inspect Weekly and after a Storm Event Greater than 0.5"
Inlet Protection (RECP or SF)	• Inspect the measure for damage, displacement, bypass or surface ponding. • Remove sediment, or install a secondary barrier upgradient of the original control when deposits reach approximately half of the height of the control.	Inspect Weekly and after a Storm Event Greater than 0.5"
Soil Stockpile (RECP or SF)	• See Above for RECP or SF	Inspect Weekly and after a Storm Event Greater than 0.5"
Dewatering (if required)	• Inspect for damage, excessive pump rate, discharge quality • Maintain measure as necessary.	Inspect Daily During Dewatering Operations
Construction Entrance (if required)	• Inspect for effectiveness (tracking of sediment out of construction area) • Install top dressing with additional aggregate, as required. • Remove immediately sediment spilled, dropped, or washed onto public right-of-ways must be removed immediately.	Inspect Weekly and after a Storm Event Greater than 0.5"
Washout (if required)	• Inspect containers/pits to ensure structural integrity, adequate holding capacity, and to check for leaks or overflows • Remove hardened concrete waste when the waste has accumulated to a height of half of the washout, or as necessary to avoid overflows	Inspect Weekly and after a Storm Event Greater than 0.5"
Temporary Seeding (if required)	• Erosion, poor seedling emergence • Reseed, as necessary to stabilize	Inspect Weekly and after a Storm Event Greater than 0.5"

TRITON ENVIRONMENTAL
A TRUE ENVIRONMENTAL COMPANY

385 Church Street, Suite 201 • Guilford, Connecticut 06437 • 203.458.7200

C9.0
SOIL EROSION AND SEDIMENT DETAILS AND NOTES

SQUANTZ COVE BOAT LAUNCH
PROJECT #DEPA00013203701

CONNECTICUT DEEP
210 ROUTE 39 (SHERMAN ROAD)
NEW FAIRFIELD, CONNECTICUT

DRAWN BY: FSM
DATE: 6/11/26

APPROVED BY: SJB
SCALE: AS NOTED
FILE No.:R25-00007-BLD-14

SEAL & SIGNATURE



FIGURE 5
FEMA Floodplain Map

National Flood Hazard Layer FIRMMette



73°28'27"W 41°30'42"N



0 250 500 1,000 1,500 2,000 Feet

1:6,000

73°27'49"W 41°30'15"N

Basemap: USGS National Map: Orthoimagery: Data refreshed October, 2020

Legend

SEE FIS REPORT FOR DETAILED LEGEND AND INDEX MAP FOR FIRM PANEL LAYOUT

SPECIAL FLOOD HAZARD AREAS		Without Base Flood Elevation (BFE) Zone A, V, A99
		With BFE or Depth Zone AE, AO, AH, VE, AR
		Regulatory Floodway
OTHER AREAS OF FLOOD HAZARD		0.2% Annual Chance Flood Hazard, Areas of 1% annual chance flood with average depth less than one foot or with drainage areas of less than one square mile Zone X
		Future Conditions 1% Annual Chance Flood Hazard Zone X
		Area with Reduced Flood Risk due to Levee. See Notes. Zone X
		Area with Flood Risk due to Levee Zone D
OTHER AREAS		NO SCREEN Area of Minimal Flood Hazard Zone X
		Effective LOMRs
GENERAL STRUCTURES		Area of Undetermined Flood Hazard Zone D
OTHER FEATURES		Channel, Culvert, or Storm Sewer
		Levee, Dike, or Floodwall
MAP PANELS		Cross Sections with 1% Annual Chance Water Surface Elevation
		Coastal Transect
		Base Flood Elevation Line (BFE)
		Limit of Study
		Jurisdiction Boundary
		Coastal Transect Baseline
		Profile Baseline
		Hydrographic Feature
		Digital Data Available
		No Digital Data Available
		Unmapped



The pin displayed on the map is an approximate point selected by the user and does not represent an authoritative property location.

This map complies with FEMA's standards for the use of digital flood maps if it is not void as described below. The basemap shown complies with FEMA's basemap accuracy standards

The flood hazard information is derived directly from the authoritative NFHL web services provided by FEMA. This map was exported on **3/20/2023 at 3:03 PM** and does not reflect changes or amendments subsequent to this date and time. The NFHL and effective information may change or become superseded by new data over time.

This map image is void if the one or more of the following map elements do not appear: basemap imagery, flood zone labels, legend, scale bar, map creation date, community identifiers, FIRM panel number, and FIRM effective date. Map images for unmapped and unmodernized areas cannot be used for regulatory purposes.

FIGURE 6

Soils Map

Soil Map—State of Connecticut, Western Part (Squantz Cove Soils Map)



Soil Map—State of Connecticut, Western Part
(Squantz Cove Soils Map)

MAP LEGEND

Area of Interest (AOI)

 Area of Interest (AOI)

Soils

 Soil Map Unit Polygons

 Soil Map Unit Lines

 Soil Map Unit Points

Special Point Features



Blowout



Borrow Pit



Clay Spot



Closed Depression



Gravel Pit



Gravelly Spot



Landfill



Lava Flow



Marsh or swamp



Mine or Quarry



Miscellaneous Water



Perennial Water



Rock Outcrop



Saline Spot



Sandy Spot



Severely Eroded Spot



Sinkhole



Slide or Slip



Sodic Spot



Spoil Area



Stony Spot



Very Stony Spot



Wet Spot



Other



Special Line Features

Water Features



Streams and Canals

Transportation



Rails



Interstate Highways



US Routes



Major Roads



Local Roads

Background



Aerial Photography

MAP INFORMATION

The soil surveys that comprise your AOI were mapped at 1:12,000.

Warning: Soil Map may not be valid at this scale.

Enlargement of maps beyond the scale of mapping can cause misunderstanding of the detail of mapping and accuracy of soil line placement. The maps do not show the small areas of contrasting soils that could have been shown at a more detailed scale.

Please rely on the bar scale on each map sheet for map measurements.

Source of Map: Natural Resources Conservation Service

Web Soil Survey URL:

Coordinate System: Web Mercator (EPSG:3857)

Maps from the Web Soil Survey are based on the Web Mercator projection, which preserves direction and shape but distorts distance and area. A projection that preserves area, such as the Albers equal-area conic projection, should be used if more accurate calculations of distance or area are required.

This product is generated from the USDA-NRCS certified data as of the version date(s) listed below.

Soil Survey Area: State of Connecticut, Western Part

Survey Area Data: Version 6, Sep 16, 2025

Soil map units are labeled (as space allows) for map scales 1:50,000 or larger.

Date(s) aerial images were photographed: Oct 21, 2022—Oct 27, 2022

The orthophoto or other base map on which the soil lines were compiled and digitized probably differs from the background imagery displayed on these maps. As a result, some minor shifting of map unit boundaries may be evident.

Map Unit Legend

Map Unit Symbol	Map Unit Name	Acres in AOI	Percent of AOI
90B	Stockbridge loam, 3 to 8 percent slopes	2.8	60.4%
90C	Stockbridge loam, 8 to 15 percent slopes	1.8	39.6%
Totals for Area of Interest		4.6	100.0%

FIGURE 7

Historic Places Screening Map

ConnCRIS, CT State Historic Preservation Office



Appendix A

Stormwater Pollution Control Plan Certifications

REGISTRANT/PREPARER CERTIFICATION

CONNECTICUT DEPARTMENT OF ENERGY AND ENVIRONMENTAL PROTECTION

I hereby certify that I am making this certification in connection with an application under the General Permit for the Discharge of Stormwater from Construction Activities (general permit), submitted to the Commissioner by Connecticut Department of Energy and Environmental Protection for an activity located at 210 Route 39 in New Fairfield, Connecticut, and that all terms and conditions of the general permit are being met all discharges which will be initiated and such activity is eligible for authorization under such permit. I further certify that a system is in place to ensure that all terms and conditions of this general permit will continue to be met for all discharges authorized by this general permit at the site. I certify that the application filed pursuant to this general permit is on complete and accurate forms as prescribed by the Commissioner without alteration of their text. I certify that I have personally examined and am familiar with the information that provides the basis for this certification, including but not limited to all information described in Section 2.2.13.1 of such general permit, and I certify, based on reasonable investigation, including my inquiry of those individuals responsible for obtaining such information, that the information upon which this certification is based is true, accurate and complete to the best of my knowledge and belief. I certify that I have made an affirmative determination in accordance with Section 2.2.13.2 of this general permit. I understand that the application filed in connection with such general permit is submitted in accordance with and shall comply with the requirements of Section 22a-430b of Conn. Gen. Stat. I also understand that knowingly making any false statement in the submitted information and in this certification may be punishable as a criminal offense, including the possibility of fine and imprisonment, under Section 53a-157b of the Conn. Gen. Stat. and any other applicable law.

Signature of Registrant

Alex Curry, PE
Name of Registrant

Date

Civil Engineer II
Title (if applicable)

Signature of Preparer

Stephen Benben, PE
Name of Preparer

Date

Vice President (Triton Environmental)
Title (if applicable)

PROFESSIONAL ENGINEER CERTIFICATION

CONNECTICUT DEPARTMENT OF ENERGY AND ENVIRONMENTAL PROTECTION

I hereby certify that I am a professional engineer licensed in the State of Connecticut. I am making this certification in connection with an application under the General Permit for the Discharge of Stormwater from Construction Activities (general permit), submitted to the commissioner by the Connecticut Department of Energy and Environmental Protection for an activity located at 210 Route 39 in New Fairfield, Connecticut. I certify that I have thoroughly and completely reviewed the Stormwater Pollution Control Plan for the project or activity covered by this certification. I further certify, based on such review and on the standard of care for such projects, that the Stormwater Pollution Control Plan has been prepared in accordance with the Connecticut Guidelines for Soil Erosion and Sediment Control, as amended, the Stormwater Quality Manual, as amended, and the conditions of the general permit, and that the controls required for such SPCP are appropriate for the site. I further certify, based on reasonable investigation, including my inquiry of those individuals responsible for obtaining such information, that the information upon which this certification is based is true, accurate and complete to the best of my knowledge and belief. I also understand that knowingly making any false statement in this certification may subject me to sanction by the Department and/or be punishable as a criminal offense, including the possibility of fine and imprisonment, under Section 53a-157b of the Conn. Gen. Stat. and any other applicable law.

Signature of Professional Engineer

Date

Stephen J. Benben, PE
Name of Professional Engineer

24952
License Number

(SUB)CONTRACTOR CERTIFICATION STATEMENT CERTIFICATION

CONNECTICUT DEPARTMENT OF ENERGY AND ENVIRONMENTAL PROTECTION

I certify under penalty of the law that I have read and understand the terms and conditions of the General Permit for the Discharge of Stormwater from Construction Activities and the site-specific Stormwater Pollution Control Plan ("SPCP"). I understand that as a contractor or subcontractor at the site, I must comply with the terms and conditions of this general permit and the SPCP.

Contractor 1:

Name/Title

Signature

Name of Company

Address of Company

Date

Contractor 3:

Name /Title

Signature

Name of Company

Address of Company

Date

Contractor 2:

Name/Title

Signature

Name of Company

Address of Company

Date

Contractor 4:

Name/Title

Signature

Name of Company

Address of Company

Date



Check box if additional page(s) required

Appendix B

NDDB Determination Letter

Generated by eNDDDB on:
11/26/2024

Alexander Fortin
TRITON COASTAL CONSULTANTS, LLC
385 Church St
Guilford, CT 06437
afortin@tritoncoastal.com

Subject: Filing # 121739
Boat Launch Replacement Squantz Cove Boat Launch
NDDDB – New Determination Number: 202411714
210 Route 39 (Sherman Road)
New Fairfield

Expiration Date: 11/26/2026

Based on current data maintained by the Natural Diversity Database (NDDDB) and housed in the DEEP ezFile portal, negative impacts to populations of Federal or State Endangered, Threatened, or Special Concern species (RCSA Sec. 26-306) are not anticipated from the proposed Docks/Piers/Boat Launches and Aquaculture / Boat Launch repair/modification, Boat Launch Replacement Squantz Cove Boat Launch.

This NDDDB – New determination may be utilized to fulfill the Endangered and Threatened Species requirements for state-issued permit applications, licenses, registration submissions, and authorizations. However, please be aware of the following limitations and conditions:

- This determination does not preclude the possibility that listed species may be encountered on site. Should this occur, a report must be submitted to the Natural Diversity Database promptly and additional action may be necessary to remain in compliance with certain state permits. Please fill out the [appropriate survey form](#) and follow the instructions for submittal.
- If your project involves preparing an Environmental Impact Assessment, this NDDDB consultation and determination should not be substituted for conducting biological field surveys assessing on-site habitat and species presence.
- This determination applies only to the project as described in the submission and summarized at the end of this letter. Please re-submit an updated Request for Review if the project's scope of work and/or timeframe changes, including if work has not begun by 11/26/2026.

The NDDDB – New determination for the Boat Launch Replacement Squantz Cove Boat Launch at 210 Route 39 (Sherman Road), New Fairfield as described in the submitted information and summarized at the end of this document is valid for two years from the date on this letter.

Natural Diversity Database information includes all information regarding listed species available to us at the time of the request. This information is a compilation of data collected over the years by the Department of Energy and Environmental Protection's Natural History Survey and cooperating units of DEEP, land owners, private conservation groups and the scientific community. This information is not necessarily the result of comprehensive or site-specific field investigations. Current research projects and new contributors continue to identify additional populations of species and locations of habitats of concern, as well as, enhance existing data. Such new information is incorporated into the Database and accessed through the ezFile portal as it becomes available.

This letter is computer generated and carries no signature. If however, any clarification is needed, or if you have further questions, please contact the following:


CT DEEP Bureau of Natural Resources
Wildlife Division
Natural Diversity Database
79 Elm Street, 6th floor
Hartford, CT 06106-5127
(860) 424-3011
deep.nddbrequest@ct.gov

Please reference the Determination Number provided in this letter when you e-mail or write. Thank you for submitting your project through DEEP's ezFile portal for Natural Diversity Database reviews.


Application Details:

Project involves federal funds or federal permit:	Yes
Project involves state funds, state agency action, or relates to CEPA request:	Yes
Project requires state permit, license, registration, or authorization:	Yes
DEEP enforcement action related to project:	
Project Type:	Docks/Piers/Boat Launches and Aquaculture
Project Sub-type:	Boat Launch repair/modification
Project Name:	Boat Launch Replacement Squantz Cove Boat Launch
Project Description:	

Boat Launch Replacement Squantz Cove Boat Launch Map

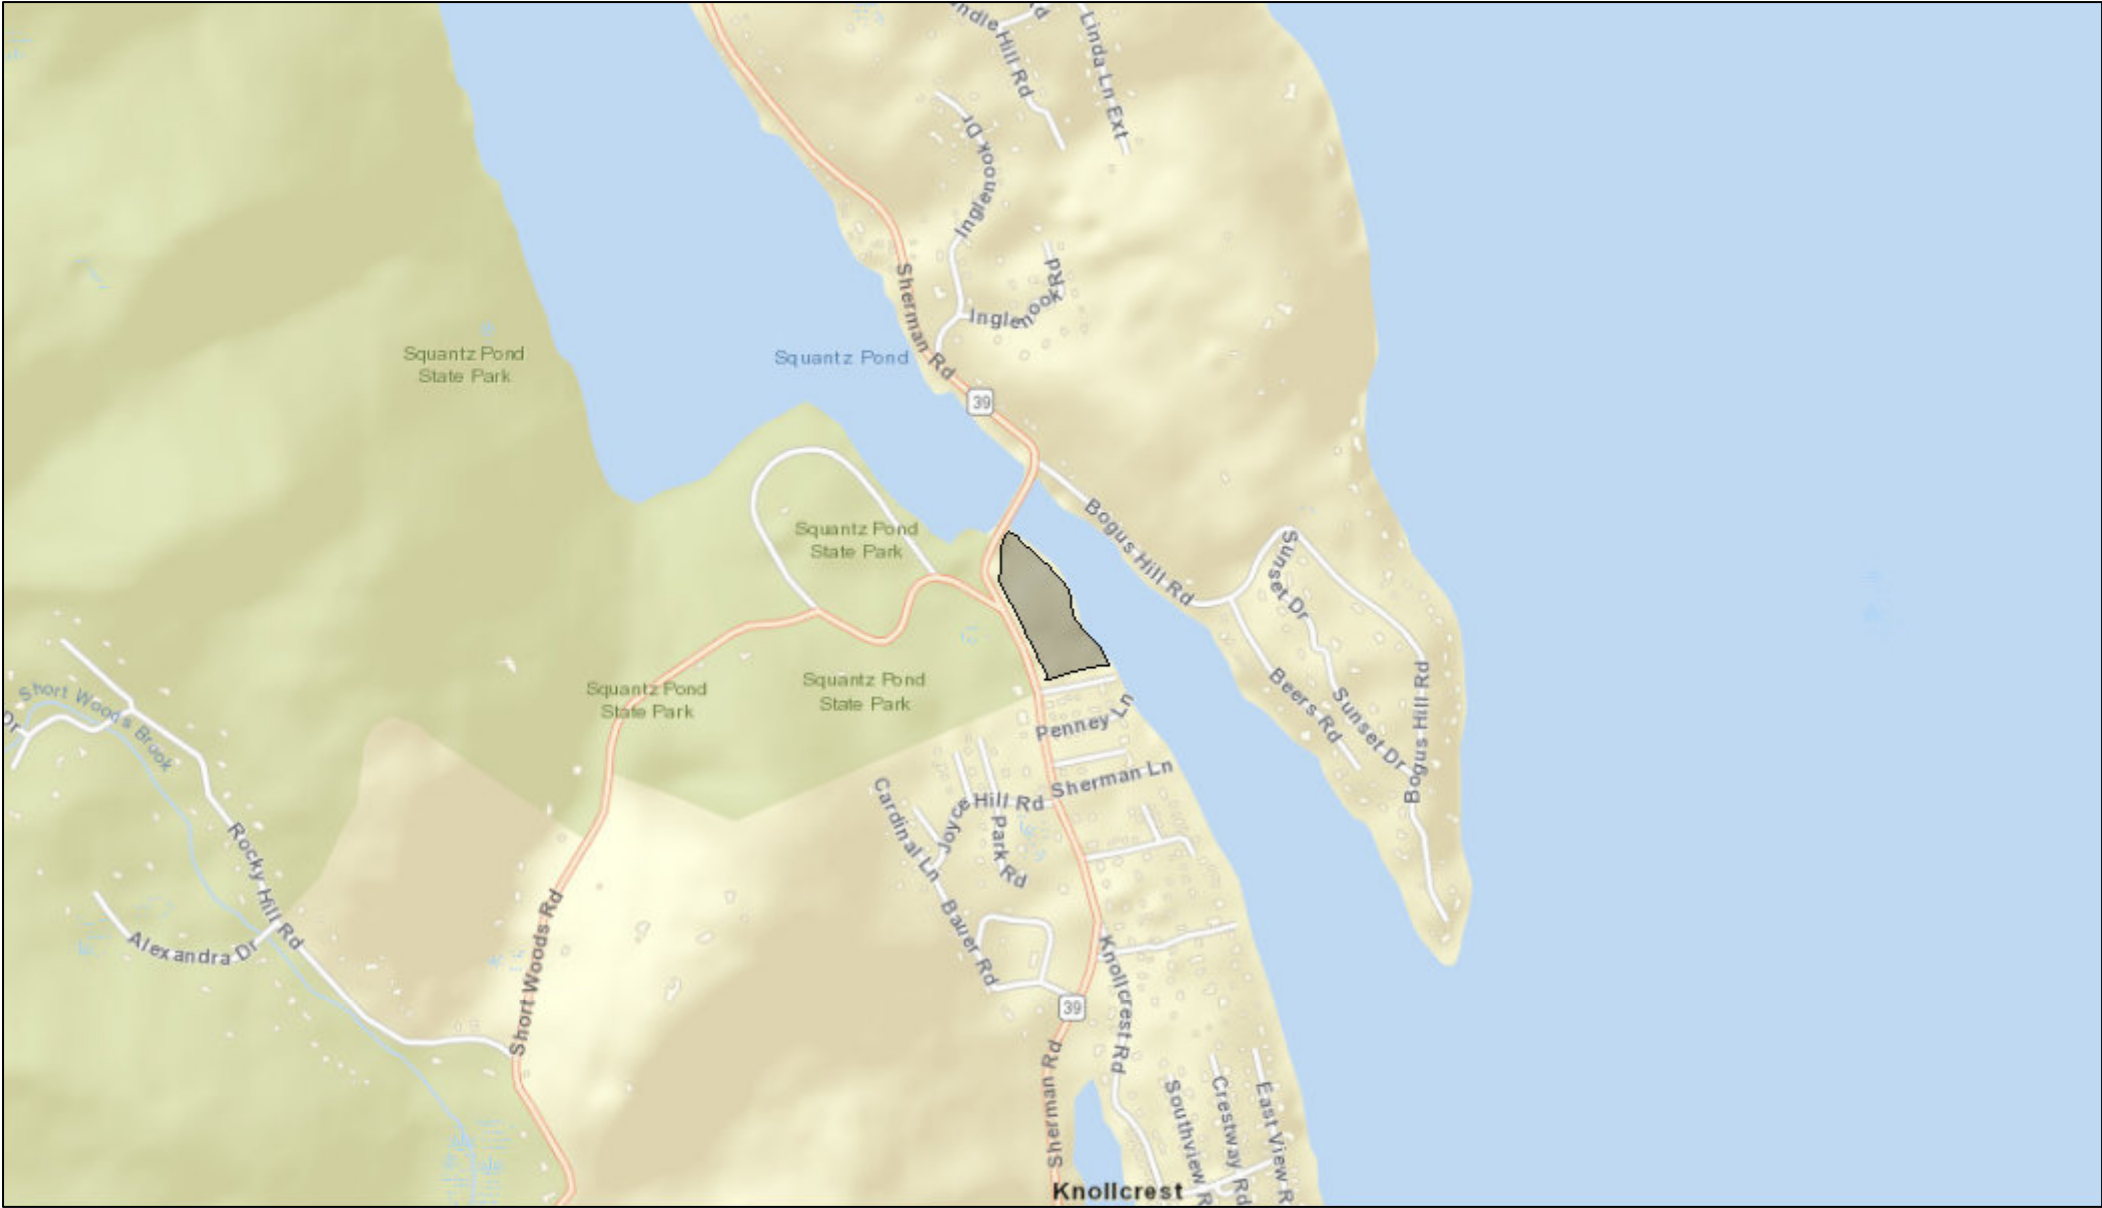

November 26, 2024



Appendix C

Wetland and Soil Report

JMM WETLAND CONSULTING SERVICES, LLC

**23 Horseshoe Ridge Road
Newtown, CT 06482**

Phone: 203-364-0345
Mobile: 203-994-3428
james@jmmwetland.com
jmmwetland.com

December 9, 2019

Triton Environmental, Inc.
385 Church Street, Suite 201
Guilford, CT 06437

ATTN: Mr. Robert B. Soden

RE: ***Wetlands Assessment & Wetland Delineations***
Candlewood State Boat Launch
Squantz Pond State Park, New Fairfield, CT

JMM Job # 19-2507-NFR-4

Dear Mr. Soden:

At your request, **JMM Wetland Consulting Services, LLC** (JMM), is providing this *Wetlands Assessment/Wetlands Delineations* report for the above-referenced study area.

Wetlands were delineated pursuant to both State and Federal Statutes and guidelines within the study area on October 17th, and 28th, 2019. The site is located on the east side of Route 39, and consists of a Connecticut State Park with an existing boat launch, while the study area is a roughly 5.4 acre segment of the overall park. Under current conditions it consists of gravel parking areas and drives, maintained lawn, scattered trees and shrubs, picnic areas, the existing boat launch, a section of Candlewood Lake, and a lake edge lined with mature trees and shrubs (see photos 1-6, attached).

Description of Regulated Resource Areas

JMM delineated the regulatory/jurisdictional wetland boundaries within the study area with wetland boundary markers JMM-1A to JMM-1K tied to JMM-1 to JMM-18. We note that at this site the State and Federal wetland boundaries are coincident. This wetland system within the study area is comprised of the near shore portion of Lake Candlewood, and a narrow forested/scrub shrub fringe. The wetland boundary begins at the northeastern portion of the study area, continuing southerly along an abrupt slope to the edge of lake.

Per the National Wetlands Inventory (NWI) classification system the delineated resource is predominately classified as a *lacustrine, limnetic, unconsolidated bottom, permanently flooded/diked/impounded* (L1UBHh). Within the delineated area the soils were found to be poorly drained.

Typical vegetation observed within this regulated wetlands, at the edge of the lake, include such species as red maple, oaks, sweet birch, sycamore, cottonwood, white ash, gray birch, speckled alder, silky dogwood, willows, and poison ivy, to name a few.

The Army Corps of Engineers Wetland Determination Data Forms that verify the delineation of the jurisdictional wetlands at the study are attached.

3.0 Soils

The soil types were found to be both undisturbed and disturbed. Any disturbed soils were noted mainly within the upland areas of the study area. The undisturbed soils are derived from glacial till (i.e. unstratified sand, silt, and rock) deposits. The undisturbed “upland type” soils are comprised of the well-drained Stockbridge (90) soil series and the moderately well drained Georgia/Amenia (48) soil series complex.

Stockbridge loam (90). This series consists of very deep, well drained soils formed in loamy calcareous till. They are nearly level to very steep soils on till plains, smooth hills, low ridges and drumloidal landforms. Slope ranges from 0 to 60 percent. Permeability is moderate in the surface layer and subsoil and moderately slow or slow in the substratum.

Georgia silt loam (48). This series consists of very deep, moderately well drained soils on glaciated uplands. They formed in loamy till. Permeability is moderate in the solum and slow in the substratum. Saturated hydraulic conductivity is moderately high or high in the solum and moderately low or moderately high in the substratum. Slope ranges from 0 to 60 percent.

Amenia silt loam (48). This series consists of very deep, moderately well drained soils formed in till. They are on uplands of till plains. Slope ranges from 0 to 25 percent. Saturated hydraulic conductivity is moderately high to high in the mineral surface layer and subsoil and low to moderately high in the substratum.

The disturbed upland soils were mapped as the Udorthents (308) mapping unit.

Udorthents (308). This soil mapping unit consists of well drained to moderately well drained soils that have been altered by cutting, filling, or grading. The areas either have had two feet or more of the upper part of the original soil removed or have more than two feet of fill material on top of the original soil. *Udorthents* or Made Land soils can be found on any soil parent material but are typically fluvial on glacial till plains and outwash plains and stream terraces.

The undisturbed “wetland-type” soils are identified as the poorly drained Mudgepond (7) soil series.

Mudgepond silt loam (7). This series consists of very deep, poorly drained soils in depressions and drainageways on till plains. They are nearly level to strongly sloping soils that formed in till dominated by siliceous rocks with some limestone. Slope ranges from 0 to 8 percent. Permeability is moderate or moderately rapid in the solum and moderate in the substratum.

Any disturbed wetland soils were mapped as the Aquents (308w) soil mapping unit.

Aquents (308w). This soil map unit consists of poorly drained and very poorly drained disturbed land areas. They are most often found on landscapes, which have been subject to prior filling and/or excavation activities. In general, this soil map unit occurs where two or more feet of the original soil surface has been filled over, graded or excavated. The *Aquents* are characterized by a seasonal to prolonged high ground water table and either support or are capable of supporting wetland vegetation. *Aquents* are recently formed soils, which have an aquic moisture regime. An aquic moisture regime is associated with a reducing soil environment that is virtually free of dissolved oxygen because the soil is saturated by groundwater or by water of the capillary fringe. The key feature is the presence of a ground water table at or very near to the soil surface for a period of fourteen days or longer during the growing season.

Mr. Robert Soden

Candlewood Lake Boat Launch, Squantz State Park, New Fairfield, CT

December 9, 2019


Page 4

JMM

Please call us if you have any questions on the above or need further assistance.

Respectfully submitted,

JMM WETLAND CONSULTING SERVICES, LLC

A handwritten signature in black ink, appearing to read "James M. McManus", with a long horizontal flourish extending to the right.

James M. McManus, MS, CPSS

Certified Professional Soil Scientist (No. 15226)

Attachments: Figure 1, Photos 1-6, NRCS Web Soil Survey Map, USACE Wetland Determination Data
Forms

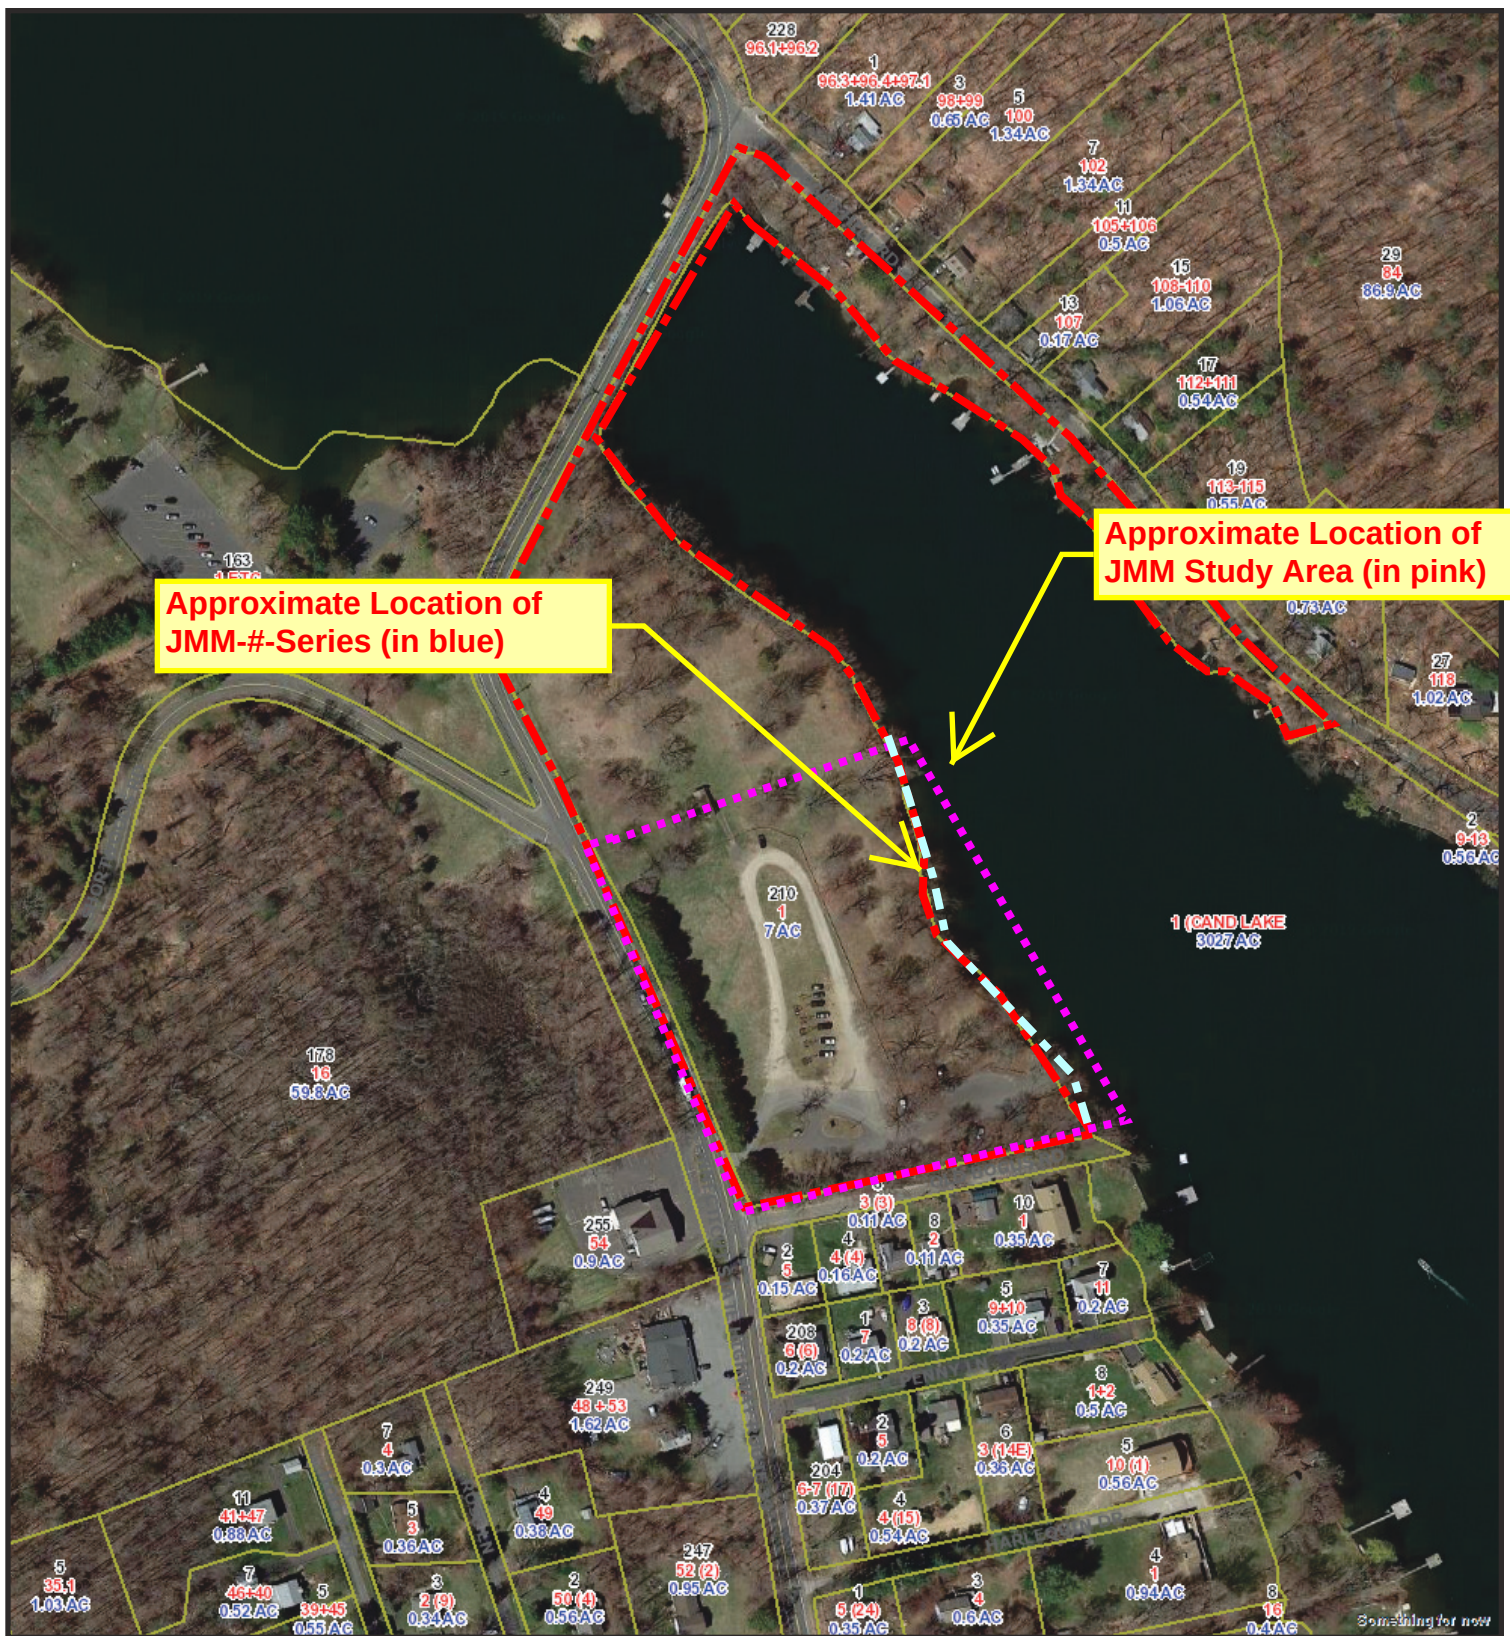


FIGURE 1

12/9/2019 1:24:24 PM

Scale: 1"=250'

Scale is approximate

The information depicted on this map is for planning purposes only. It is not adequate for legal boundary definition, regulatory interpretation, or parcel-level analyses.





Photo 1: View of fringe wetland within southeastern part of study area
(JMM photo taken 10/17/19); facing southeasterly



Photo 2: View of fringe wetland within southeastern part of study area
(JMM photo taken 10/17/19); facing southwesterly



Photo 3: View of upland/wetland edge along study area (JMM photo taken 10/17/19); facing northeasterly



Photo 4: View of boat launch within southeastern part of study area (JMM photo taken 10/17/19); facing easterly



Photo 5: View of Candlewood Lake (JMM photo taken 10/17/19); facing northeasterly



Photo 6: View of upland area within study area (JMM photo taken 10/17/19); facing northwesterly

Soil Map—State of Connecticut
(Squantz Pond State Park, New Fairfield, CT)



Soil Map may not be valid at this scale.

Map Scale: 1:6,240 if printed on A landscape (11" x 8.5") sheet.

0 50 100 200 300 Meters

0 300 600 1200 1800 Feet

Map projection: Web Mercator Corner coordinates: WGS84 Edge tics: UTM Zone 18N WGS84



Natural Resources
Conservation Service

Web Soil Survey
National Cooperative Soil Survey

3/28/2019
Page 1 of 3

Soil Map—State of Connecticut
(Squantz Pond State Park, New Fairfield, CT)

MAP LEGEND

Area of Interest (AOI)

 Area of Interest (AOI)

Soils

 Soil Map Unit Polygons

 Soil Map Unit Lines

 Soil Map Unit Points

Special Point Features



Blowout



Borrow Pit



Clay Spot



Closed Depression



Gravel Pit



Gravelly Spot



Landfill



Lava Flow



Marsh or swamp



Mine or Quarry



Miscellaneous Water



Perennial Water



Rock Outcrop



Saline Spot



Sandy Spot



Severely Eroded Spot



Sinkhole



Slide or Slip



Sodic Spot



Spoil Area



Stony Spot



Very Stony Spot



Wet Spot



Other



Special Line Features

Water Features



Streams and Canals

Transportation



Rails



Interstate Highways



US Routes



Major Roads



Local Roads

Background



Aerial Photography

MAP INFORMATION

The soil surveys that comprise your AOI were mapped at 1:12,000.

Warning: Soil Map may not be valid at this scale.

Enlargement of maps beyond the scale of mapping can cause misunderstanding of the detail of mapping and accuracy of soil line placement. The maps do not show the small areas of contrasting soils that could have been shown at a more detailed scale.

Please rely on the bar scale on each map sheet for map measurements.

Source of Map: Natural Resources Conservation Service

Web Soil Survey URL:

Coordinate System: Web Mercator (EPSG:3857)

Maps from the Web Soil Survey are based on the Web Mercator projection, which preserves direction and shape but distorts distance and area. A projection that preserves area, such as the Albers equal-area conic projection, should be used if more accurate calculations of distance or area are required.

This product is generated from the USDA-NRCS certified data as of the version date(s) listed below.

Soil Survey Area: State of Connecticut

Survey Area Data: Version 18, Dec 6, 2018

Soil map units are labeled (as space allows) for map scales 1:50,000 or larger.

Date(s) aerial images were photographed: Dec 31, 2009—Oct 5, 2016

The orthophoto or other base map on which the soil lines were compiled and digitized probably differs from the background imagery displayed on these maps. As a result, some minor shifting of map unit boundaries may be evident.

Map Unit Legend

Map Unit Symbol	Map Unit Name	Acres in AOI	Percent of AOI
3	Ridgebury, Leicester, and Whitman soils, 0 to 8 percent slopes, extremely stony	2.2	1.1%
4	Leicester fine sandy loam	7.5	3.7%
48B	Georgia and Amenia silt loams, 2 to 8 percent slopes	4.9	2.5%
73C	Charlton-Chatfield complex, 0 to 15 percent slopes, very rocky	1.7	0.9%
73E	Charlton-Chatfield complex, 15 to 45 percent slopes, very rocky	12.8	6.4%
75C	Hollis-Chatfield-Rock outcrop complex, 3 to 15 percent slopes	9.5	4.8%
75E	Hollis-Chatfield-Rock outcrop complex, 15 to 45 percent slopes	39.1	19.6%
76E	Rock outcrop-Hollis complex, 3 to 45 percent slopes	8.3	4.2%
90B	Stockbridge loam, 3 to 8 percent slopes	41.3	20.7%
90C	Stockbridge loam, 8 to 15 percent slopes	7.9	4.0%
91C	Stockbridge loam, 8 to 15 percent slopes, very stony	19.3	9.7%
91D	Stockbridge loam, 15 to 35 percent slopes, very stony	0.5	0.2%
290B	Stockbridge-Urban land complex, 3 to 8 percent slopes	3.3	1.6%
306	Udorthents-Urban land complex	0.6	0.3%
W	Water	40.3	20.2%
Totals for Area of Interest		199.4	100.0%

WETLAND DETERMINATION DATA FORM – Northcentral and Northeast Region

Project/Site: Candlewood Lake Boat Launch, Squantz State Park City/County: New Fairfield Sampling Date: 10-17-19
Applicant/Owner: Triton Environmental State: CT Sampling Point: W1
Investigator(s): James McManus Section, Township, Range: _____
Landform (hillside, terrace, etc.): terrace Local relief (concave, convex, none): Concave Slope (%): 2-5%
Subregion (LRR or MLRA): LRR R, MLRA 144B Lat: 41.508154 Long: -73.469741 Datum: NWImapper
Soil Map Unit Name: Aquents NWI classification: PFO1, PSS1

Are climatic / hydrologic conditions on the site typical for this time of year? Yes X No _____ (If no, explain in Remarks.)
Are Vegetation N, Soil N, or Hydrology N significantly disturbed? Are "Normal Circumstances" present? Yes X No _____
Are Vegetation N, Soil N, or Hydrology N naturally problematic? (If needed, explain any answers in Remarks.)

SUMMARY OF FINDINGS – Attach site map showing sampling point locations, transects, important features, etc.

Hydrophytic Vegetation Present?	Yes <u>X</u> No _____	Is the Sampled Area within a Wetland? Yes <u>X</u> No _____ If yes, optional Wetland Site ID: _____
Hydric Soil Present?	Yes <u>X</u> No _____	
Wetland Hydrology Present?	Yes <u>X</u> No _____	
Remarks: (Explain alternative procedures here or in a separate report.) 		

HYDROLOGY

Wetland Hydrology Indicators: <u>Primary Indicators (minimum of one is required; check all that apply)</u> <u>X</u> Surface Water (A1) _____ Water-Stained Leaves (B9) <u>X</u> High Water Table (A2) _____ Aquatic Fauna (B13) <u>X</u> Saturation (A3) _____ Marl Deposits (B15) <u>X</u> Water Marks (B1) _____ Hydrogen Sulfide Odor (C1) _____ Sediment Deposits (B2) _____ Oxidized Rhizospheres on Living Roots (C3) _____ Drift Deposits (B3) _____ Presence of Reduced Iron (C4) _____ Algal Mat or Crust (B4) _____ Recent Iron Reduction in Tilled Soils (C6) _____ Iron Deposits (B5) _____ Thin Muck Surface (C7) _____ Inundation Visible on Aerial Imagery (B7) _____ Other (Explain in Remarks) _____ Sparsely Vegetated Concave Surface (B8)		<u>Secondary Indicators (minimum of two required)</u> _____ Surface Soil Cracks (B6) <u>X</u> Drainage Patterns (B10) _____ Moss Trim Lines (B16) _____ Dry-Season Water Table (C2) _____ Crayfish Burrows (C8) _____ Saturation Visible on Aerial Imagery (C9) _____ Stunted or Stressed Plants (D1) <u>X</u> Geomorphic Position (D2) _____ Shallow Aquitard (D3) _____ Microtopographic Relief (D4) _____ FAC-Neutral Test (D5)
Field Observations: Surface Water Present? Yes <u>X</u> No _____ Depth (inches): <u>5</u> Water Table Present? Yes <u>X</u> No _____ Depth (inches): <u>5</u> Saturation Present? Yes <u>X</u> No _____ Depth (inches): <u>surface</u> (includes capillary fringe)	Wetland Hydrology Present? Yes <u>X</u> No _____	
Describe Recorded Data (stream gauge, monitoring well, aerial photos, previous inspections), if available: 		
Remarks: Wetland boundary follows an abrupt slope to the edge of lake. 		

VEGETATION – Use scientific names of plants.

Sampling Point: W1

	Absolute % Cover	Dominant Species?	Indicator Status																	
Tree Stratum (Plot size: <u>30' radius</u>)				Dominance Test worksheet: Number of Dominant Species That Are OBL, FACW, or FAC: <u>2</u> (A) Total Number of Dominant Species Across All Strata: <u>4</u> (B) Percent of Dominant Species That Are OBL, FACW, or FAC: <u>50.0%</u> (A/B)																
1. <u>Betula lenta</u>	<u>2</u>	<u>Yes</u>	<u>FACU</u>																	
2. <u>Populus deltoides</u>	<u>5</u>	<u>Yes</u>	<u>FAC</u>																	
3. _____	_____	_____	_____																	
4. _____	_____	_____	_____																	
5. _____	_____	_____	_____																	
6. _____	_____	_____	_____																	
7. _____	_____	_____	_____																	
			<u>7</u> =Total Cover																	
Sapling/Shrub Stratum (Plot size: <u>15' radius</u>)																				
1. <u>Alnus incana</u>	<u>10</u>	<u>Yes</u>	<u>FACW</u>	Prevalence Index worksheet: <table style="width: 100%;"> <tr> <th style="width: 50%;">Total % Cover of:</th> <th style="width: 50%;">Multiply by:</th> </tr> <tr> <td>OBL species <u>0</u></td> <td>x 1 = <u>0</u></td> </tr> <tr> <td>FACW species <u>10</u></td> <td>x 2 = <u>20</u></td> </tr> <tr> <td>FAC species <u>10</u></td> <td>x 3 = <u>30</u></td> </tr> <tr> <td>FACU species <u>17</u></td> <td>x 4 = <u>68</u></td> </tr> <tr> <td>UPL species <u>0</u></td> <td>x 5 = <u>0</u></td> </tr> <tr> <td>Column Totals: <u>37</u> (A)</td> <td><u>118</u> (B)</td> </tr> <tr> <td colspan="2">Prevalence Index = B/A = <u>3.19</u></td> </tr> </table>	Total % Cover of:	Multiply by:	OBL species <u>0</u>	x 1 = <u>0</u>	FACW species <u>10</u>	x 2 = <u>20</u>	FAC species <u>10</u>	x 3 = <u>30</u>	FACU species <u>17</u>	x 4 = <u>68</u>	UPL species <u>0</u>	x 5 = <u>0</u>	Column Totals: <u>37</u> (A)	<u>118</u> (B)	Prevalence Index = B/A = <u>3.19</u>	
Total % Cover of:	Multiply by:																			
OBL species <u>0</u>	x 1 = <u>0</u>																			
FACW species <u>10</u>	x 2 = <u>20</u>																			
FAC species <u>10</u>	x 3 = <u>30</u>																			
FACU species <u>17</u>	x 4 = <u>68</u>																			
UPL species <u>0</u>	x 5 = <u>0</u>																			
Column Totals: <u>37</u> (A)	<u>118</u> (B)																			
Prevalence Index = B/A = <u>3.19</u>																				
2. <u>Cornus amomum</u>	<u>15</u>	<u>Yes</u>	<u>FACU</u>																	
3. <u>Populus deltoides</u>	<u>5</u>	<u>No</u>	<u>FAC</u>																	
4. _____	_____	_____	_____																	
5. _____	_____	_____	_____																	
6. _____	_____	_____	_____																	
7. _____	_____	_____	_____																	
			<u>30</u> =Total Cover																	
Herb Stratum (Plot size: <u>5' radius</u>)																				
1. _____	_____	_____	_____	Hydrophytic Vegetation Indicators: <u>1</u> - Rapid Test for Hydrophytic Vegetation <u>2</u> - Dominance Test is >50% <u>3</u> - Prevalence Index is ≤3.0 ¹ <u>4</u> - Morphological Adaptations ¹ (Provide supporting data in Remarks or on a separate sheet) <u>X</u> Problematic Hydrophytic Vegetation ¹ (Explain) ¹ Indicators of hydric soil and wetland hydrology must be present, unless disturbed or problematic.																
2. _____	_____	_____	_____																	
3. _____	_____	_____	_____																	
4. _____	_____	_____	_____																	
5. _____	_____	_____	_____																	
6. _____	_____	_____	_____																	
7. _____	_____	_____	_____																	
8. _____	_____	_____	_____																	
9. _____	_____	_____	_____																	
10. _____	_____	_____	_____																	
11. _____	_____	_____	_____																	
12. _____	_____	_____	_____																	
			_____ =Total Cover																	
Woody Vine Stratum (Plot size: <u>30' radius</u>)																				
1. _____	_____	_____	_____	Definitions of Vegetation Strata: Tree – Woody plants 3 in. (7.6 cm) or more in diameter at breast height (DBH), regardless of height. Sapling/shrub – Woody plants less than 3 in. DBH and greater than or equal to 3.28 ft (1 m) tall. Herb – All herbaceous (non-woody) plants, regardless of size, and woody plants less than 3.28 ft tall. Woody vines – All woody vines greater than 3.28 ft in height.																
2. _____	_____	_____	_____																	
3. _____	_____	_____	_____																	
4. _____	_____	_____	_____																	
			_____ =Total Cover																	

Remarks: (Include photo numbers here or on a separate sheet.)
 Jurisdictional area is a narrow fringe wetland along the edge of the lake.

SOIL

Sampling Point: W1

[illegible]

WETLAND DETERMINATION DATA FORM – Northcentral and Northeast Region

Project/Site: Candlewood Lake Boat Launch, Squantz State Park City/County: New Fairfield Sampling Date: 10-17-19
Applicant/Owner: Triton Environmental State: CT Sampling Point: U1
Investigator(s): James McManus Section, Township, Range: _____
Landform (hillside, terrace, etc.): terrace Local relief (concave, convex, none): convex Slope (%): 1-2%
Subregion (LRR or MLRA): LRR R, MLRA 144B Lat: 41.508154 Long: -73.469741 Datum: NWImapper
Soil Map Unit Name: Udorthents NWI classification: _____

Are climatic / hydrologic conditions on the site typical for this time of year? Yes X No _____ (If no, explain in Remarks.)
Are Vegetation N, Soil N, or Hydrology N significantly disturbed? Are "Normal Circumstances" present? Yes Y No _____
Are Vegetation N, Soil N, or Hydrology N naturally problematic? (If needed, explain any answers in Remarks.)

SUMMARY OF FINDINGS – Attach site map showing sampling point locations, transects, important features, etc.

Hydrophytic Vegetation Present? Yes _____ No <u>X</u>	Is the Sampled Area within a Wetland? Yes _____ No <u>X</u> If yes, optional Wetland Site ID: _____
Hydric Soil Present? Yes _____ No <u>X</u>	
Wetland Hydrology Present? Yes _____ No <u>X</u>	
Remarks: (Explain alternative procedures here or in a separate report.)	

HYDROLOGY

Wetland Hydrology Indicators:		Secondary Indicators (minimum of two required)
<u>Primary Indicators (minimum of one is required; check all that apply)</u>		
☐ Surface Water (A1)	☐ Water-Stained Leaves (B9)	☐ Surface Soil Cracks (B6)
☐ High Water Table (A2)	☐ Aquatic Fauna (B13)	☐ Drainage Patterns (B10)
☐ Saturation (A3)	☐ Marl Deposits (B15)	☐ Moss Trim Lines (B16)
☐ Water Marks (B1)	☐ Hydrogen Sulfide Odor (C1)	☐ Dry-Season Water Table (C2)
☐ Sediment Deposits (B2)	☐ Oxidized Rhizospheres on Living Roots (C3)	☐ Crayfish Burrows (C8)
☐ Drift Deposits (B3)	☐ Presence of Reduced Iron (C4)	☐ Saturation Visible on Aerial Imagery (C9)
☐ Algal Mat or Crust (B4)	☐ Recent Iron Reduction in Tilled Soils (C6)	☐ Stunted or Stressed Plants (D1)
☐ Iron Deposits (B5)	☐ Thin Muck Surface (C7)	☐ Geomorphic Position (D2)
☐ Inundation Visible on Aerial Imagery (B7)	☐ Other (Explain in Remarks)	☐ Shallow Aquitard (D3)
☐ Sparsely Vegetated Concave Surface (B8)		☐ Microtopographic Relief (D4)
		☐ FAC-Neutral Test (D5)
Field Observations:		Wetland Hydrology Present? Yes _____ No <u>X</u>
Surface Water Present? Yes _____ No <u>X</u> Depth (inches): _____	Water Table Present? Yes _____ No <u>X</u> Depth (inches): _____	
Saturation Present? Yes _____ No <u>X</u> Depth (inches): _____ (includes capillary fringe)		
Describe Recorded Data (stream gauge, monitoring well, aerial photos, previous inspections), if available:		
Remarks:		

VEGETATION – Use scientific names of plants.

Sampling Point: U1

Tree Stratum (Plot size: <u>30' radius</u>)	Absolute % Cover	Dominant Species?	Indicator Status																	
1. <u>Acer rubrum</u>	2	No	FAC	Dominance Test worksheet: Number of Dominant Species That Are OBL, FACW, or FAC: <u>0</u> (A) Total Number of Dominant Species Across All Strata: <u>1</u> (B) Percent of Dominant Species That Are OBL, FACW, or FAC: <u>0.0%</u> (A/B)																
2. _____	_____	_____	_____																	
3. _____	_____	_____	_____																	
4. _____	_____	_____	_____																	
5. _____	_____	_____	_____																	
6. _____	_____	_____	_____																	
7. _____	_____	_____	_____																	
	2	=Total Cover		Prevalence Index worksheet: <table style="width: 100%;"> <tr> <th style="width: 50%;">Total % Cover of:</th> <th style="width: 50%;">Multiply by:</th> </tr> <tr> <td>OBL species _____</td> <td>x 1 = _____</td> </tr> <tr> <td>FACW species _____</td> <td>x 2 = _____</td> </tr> <tr> <td>FAC species _____</td> <td>x 3 = _____</td> </tr> <tr> <td>FACU species _____</td> <td>x 4 = _____</td> </tr> <tr> <td>UPL species _____</td> <td>x 5 = _____</td> </tr> <tr> <td>Column Totals: _____</td> <td>(A) _____ (B) _____</td> </tr> <tr> <td colspan="2" style="text-align: center;">Prevalence Index = B/A = _____</td> </tr> </table>	Total % Cover of:	Multiply by:	OBL species _____	x 1 = _____	FACW species _____	x 2 = _____	FAC species _____	x 3 = _____	FACU species _____	x 4 = _____	UPL species _____	x 5 = _____	Column Totals: _____	(A) _____ (B) _____	Prevalence Index = B/A = _____	
Total % Cover of:	Multiply by:																			
OBL species _____	x 1 = _____																			
FACW species _____	x 2 = _____																			
FAC species _____	x 3 = _____																			
FACU species _____	x 4 = _____																			
UPL species _____	x 5 = _____																			
Column Totals: _____	(A) _____ (B) _____																			
Prevalence Index = B/A = _____																				
Sapling/Shrub Stratum (Plot size: <u>15' radius</u>)																				
1. _____	_____	_____	_____																	
2. _____	_____	_____	_____																	
3. _____	_____	_____	_____																	
4. _____	_____	_____	_____																	
5. _____	_____	_____	_____																	
6. _____	_____	_____	_____																	
7. _____	_____	_____	_____																	
		=Total Cover																		
Herb Stratum (Plot size: <u>5' radius</u>)																				
1. <u>Poa sp.</u>	80	Yes	UPL	Hydrophytic Vegetation Indicators: <u>1</u> - Rapid Test for Hydrophytic Vegetation <u>2</u> - Dominance Test is >50% <u>3</u> - Prevalence Index is ≤3.0 ¹ <u>4</u> - Morphological Adaptations ¹ (Provide supporting data in Remarks or on a separate sheet) <u> </u> Problematic Hydrophytic Vegetation ¹ (Explain) ¹ Indicators of hydric soil and wetland hydrology must be present, unless disturbed or problematic.																
2. <u>Plantago major</u>	10	No	FAC																	
3. <u>Trifolium repens</u>	2	No	FAC																	
4. _____	_____	_____	_____																	
5. _____	_____	_____	_____																	
6. _____	_____	_____	_____																	
7. _____	_____	_____	_____																	
8. _____	_____	_____	_____																	
9. _____	_____	_____	_____																	
10. _____	_____	_____	_____																	
11. _____	_____	_____	_____																	
12. _____	_____	_____	_____																	
	92	=Total Cover																		
Woody Vine Stratum (Plot size: <u>30' radius</u>)																				
1. _____	_____	_____	_____																	
2. _____	_____	_____	_____																	
3. _____	_____	_____	_____																	
4. _____	_____	_____	_____																	
		=Total Cover																		

Definitions of Vegetation Strata:

Tree – Woody plants 3 in. (7.6 cm) or more in diameter at breast height (DBH), regardless of height.

Sapling/shrub – Woody plants less than 3 in. DBH and greater than or equal to 3.28 ft (1 m) tall.

Herb – All herbaceous (non-woody) plants, regardless of size, and woody plants less than 3.28 ft tall.

Woody vines – All woody vines greater than 3.28 ft in height.

Hydrophytic Vegetation Present? Yes No X


Remarks: (Include photo numbers here or on a separate sheet.)

SOIL

Sampling Point: U1

[illegible]

Candlewood Lake Boat Launch
Squantz State Park
New Fairfield, CT

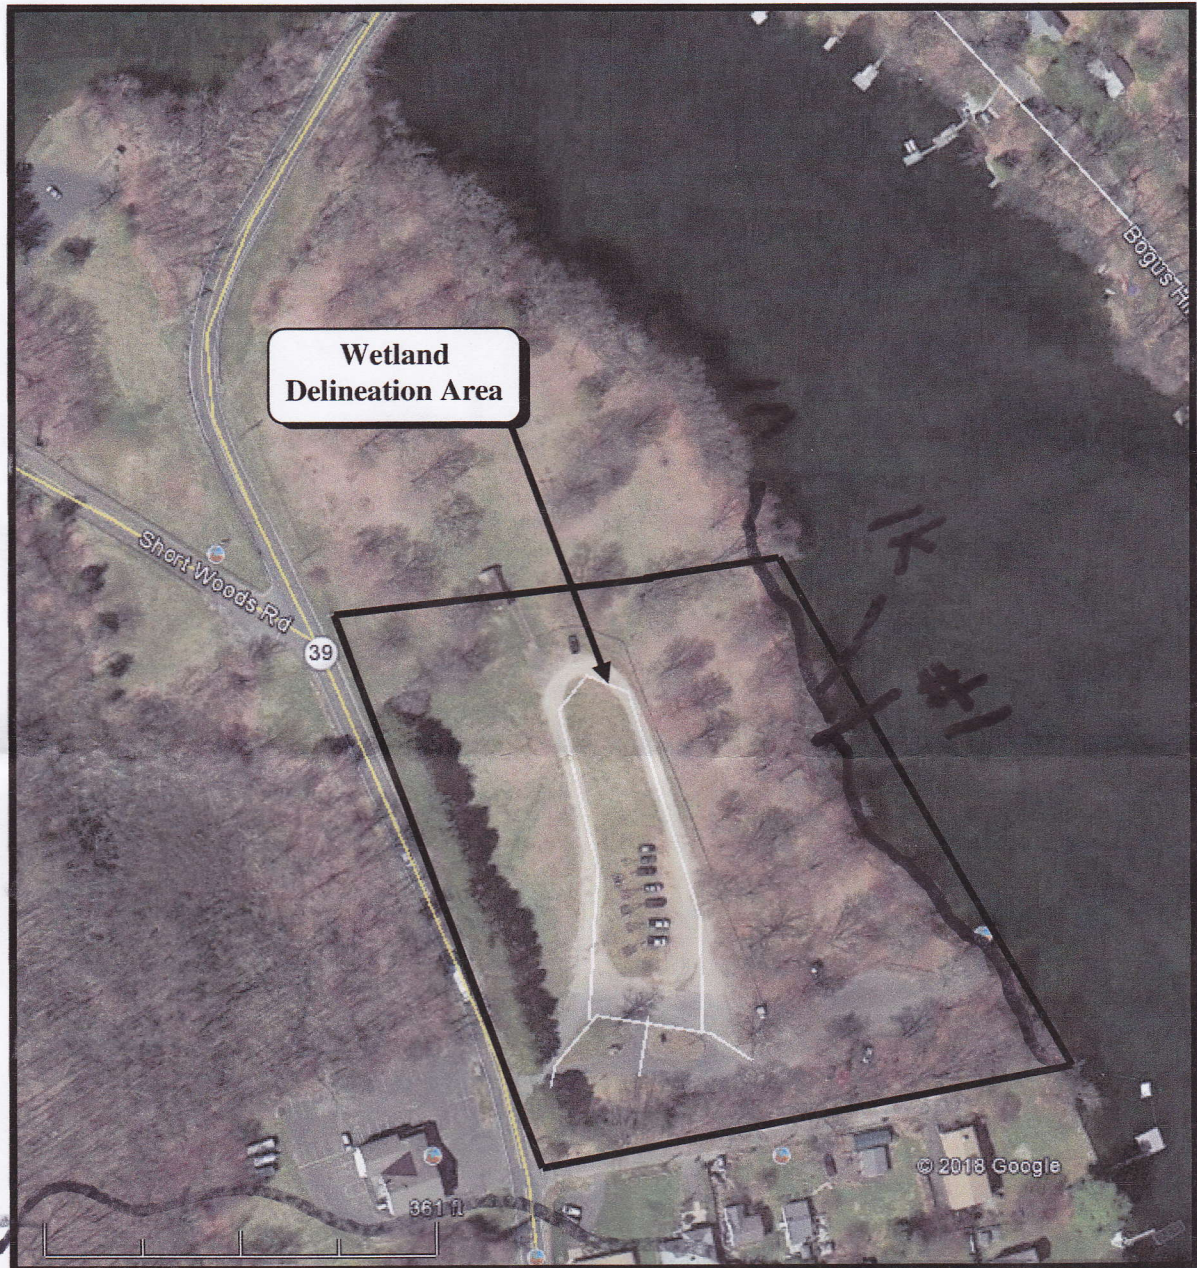

Jim Fingers: 10/28/19

1A-1K - tie to #1

Appendix D

Sample Forms

- Weekly/Rainfall Event Inspection Log
- Corrective Action Form

FIELD INSPECTION FORM

CT DEEP General Permit for the Discharge of Stormwater and Dewatering Wastewaters from Construction Activities

Squantz Cove Boat Construction – New Fairfield, CT

Project Name: _____

Location: _____

Date of Inspection: _____ Start Time: _____ AM/PM End Time: _____ AM/PM

Inspector's Name: _____

Inspector's Title: _____

Inspector's Phone: _____

Describe present phase of construction: _____

Type of ☐ Plan Implementation ☐ Routine ☐ Post-Storm Event

Inspection: ☐ Post-Construction Final Stabilization ☐ Termination

WEATHER INFORMATION

Has there been a storm event since the last inspection? ☐ Yes ☐ No

If yes, provide: _____

Storm Start Date: _____ Start Time: _____ AM/PM Storm Duration: _____ hours

Approximate Amount of Precipitation: _____ inches

Weather at time of this ☒ Clear ☐ Cloudy ☐ Windy ☐ Fog ☐ Rain

inspection? ☐ Sleet ☐ Snow ☐ Other: _____ Temperature _____ °F

DISCHARGE INFORMATION

Have any discharges occurred since the last inspection ☐ Yes ☐ No

If yes, describe: _____

Are there any discharges at the time of inspection? ☐ Yes ☐ No

If yes, describe: _____

CERTIFICATION STATEMENT

I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information is, to the best of my knowledge and belief, true, accurate and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

I have personally examined and am familiar with the information submitted in this document and all attachments thereto, and I certify that, based on reasonable investigation, including my inquiry of those individuals responsible for obtaining the information, the submitted information is true, accurate and complete to the best of my knowledge and belief. I understand that a false statement made in this document or its attachments may be punishable as a criminal offense, in accordance with Section 22a-6 of the Connecticut General Statutes, pursuant to Section 53a-157b of the Connecticut General Statutes, and in accordance with any other applicable statute.

In my professional judgment as the qualified inspector, the site is in ☐ out ☐ of compliance with the terms and conditions of the Plan and permit.

Inspector Signature: _____ Inspector Name: _____ Title: _____ Date: _____

OBSERVED SITE ISSUES			
BMP/ACTIVITY	IMPLEMENTED	MAINTENANCE REQUIRED	CORRECTIVE ACTION FORM REQUIRED
1. All disturbed ground surfaces have been stabilized.	Yes ☐ No ☐	Yes ☐ No ☐	Yes ☐ No ☐
2. Are perimeter controls (silt fence/filter socks) installed per plan and maintained (no undercutting, overtopping, gaps)?	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐
3. Are stockpiles contained with perimeter controls and covered when inactive?	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐
4. Are storm drain protection/catch basin inserts properly installed and maintained (free of sediment buildup)?	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐
5. Is the construction entrance stable and preventing sediment from being tracked into the street?	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐
6. Are adjacent waters and tidal wetlands protected?	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐
7. Are stockpiles, demolition debris, or hazardous materials properly stored and contained or removed from property?	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐
8. Is trash/litter from work areas collected and placed in covered dumpsters?	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐
9. Is accumulated water controlled and discharged through approved filtration method?	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐
10. Are vehicle and equipment fueling, cleaning, and maintenance areas free of spills, leaks, or any other deleterious material?	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐
11. Are materials that are potential stormwater contaminants stored inside or under cover?	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐
12. Are discharges from dewatering properly controlled and not causing sedimentation or erosion?	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐
13. (Other)	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐
	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐
	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐ N/A ☐	Yes ☐ No ☐

CORRECTIVE ACTION FORM

CT DEEP General Permit for the Discharge of Stormwater and Dewatering Wastewaters from Construction Activities

Squantz Cove Boat Construction – New Fairfield, CT

Date of Associated Inspection Report: _____

SESC Measure Deficiency: _____

Deficiency Identified During Current Inspection? ☐ Yes ☐ No

If No, Date Originally Identified: _____

Location of Deficiency Within Project Area: _____

Corrective Action Required: _____

Inspector Name: _____

Date of Associated Inspection Report: _____

SESC Measure Deficiency: _____

Deficiency Identified During Current Inspection? ☐ Yes ☐ No

If No, Date Originally Identified: _____

Location of Deficiency Within Project Area: _____

Corrective Action Required: _____

Inspector Name: _____

Date of Associated Inspection Report: _____

SESC Measure Deficiency: _____

Deficiency Identified During Current Inspection? ☐ Yes ☐ No

If No, Date Originally Identified: _____

Location of Deficiency Within Project Area: _____

Corrective Action Required: _____

Inspector Name: _____

☐ Check box if additional page(s) required

Appendix E
Inspector Qualifications



STEPHEN J. BENBEN, PE

Vice President of Engineering



CAREER SUMMARY

Mr. Benben is the Vice President of Engineering at Triton Environmental, LLC (Triton) Managing and supporting civil and environmental engineering projects throughout the company. Mr. Benben is a Professional Engineer with approximately eighteen years of experience in the consulting field. Prior to joining Triton in 2011, Mr. Benben was a project manager at BL Companies.

Mr. Benben's primary responsibilities at Triton include providing technical expertise and project management of local and state regulatory permitting and compliance, and assessment and remediation projects.

EDUCATION

University of Rhode Island, B.S., Civil Engineering,

2000

ADDITIONAL TRAINING

Professional Engineer in CT, MA, NH and PA

PROFESSIONAL MEMBERSHIPS

Prestressed Concrete Institute (PCI): Chairman of the Subcommittee on Integral Bridges

PROFESSIONAL EXPERIENCE

Engineering Projects & Storm Water Management

Steve has designed site layout plans, site grading and drainage plans, stormwater collection and conveyance systems and above and below ground detention systems in various states and has experience with Low Impact Design (LID) methods. Steve has evaluated existing stormwater deficiencies, and designed and instituted stormwater retrofits for compliance related issues. Steve has experience with designing septic disposal systems, designing and implementing soil erosion and sedimentation controls and conducting and evaluating geotechnical investigations. His work has included stormwater control system design for numerous commercial, industrial and residential facilities in various states. He is thoroughly familiar with the latest technologies for stormwater treatment units including physical separation and advanced treatment, and has specified this equipment in recent design systems. Steve has designed and instituted construction stormwater discharge BMP's as well as Post-Construction Stormwater Management plans.

Regulatory Compliance and Wastewater Engineering Projects

As a Senior Project Manager and Engineer, Steve is involved with stormwater and wastewater compliance and permitting at Triton. Specifically, he has experience with State and Federal NPDES/SPDES programs, General Permits, Multi-Sector General Permit regulations and permits. He reviews, provides technical support, and certifications for Spill Prevention Control and Countermeasure (SPCC) Plans and Stormwater Pollution Plans (SWP3). In addition, Steve has contributed to projects involving amendment and development of regulatory compliance plans for industrial facilities such as CT DEEP, MassDEP, Illinois EPA, NJ DEP Stormwater Pollution Prevention Plans; EPA Spill Prevention Control and Countermeasure (SPCC) Plans; and Integrated Contingency

Years with the Firm

14

Years Total



STEPHEN J. BENBEN, PE

Vice President of Engineering

Plans (ICPs). In addition, Steve has been involved in assisting facilities with annual environmental training, as required by BPDES Construction Stormwater General Permit.

PREVIOUS EXPERIENCE

Prior to joining Triton in 2011, Mr. Benben was a project manager at BL Companies.

Appendix F

Record of Plan Amendments

RECORD OF PLAN AMENDMENTS

STORMWATER POLLUTION CONTROL PLAN

CONNECTICUT DEPARTMENT OF ENERGY AND ENVIRONMENTAL PROTECTION

Form Instructions:

1. *The Amendment Table below should be completed in accordance with Section 7.0 of the Plan, including whenever there is a change in contractors or subcontractors at the site; a change in design, construction, operation, or maintenance at the site which has the potential for the discharge of pollutants to the waters of the state and which has not otherwise been addressed in the Plan, or; if the actions required by the Plan fail to prevent pollution.*

NO.	DATE	PLAN AMENDMENT DESCRIPTION	Initials

Appendix G
Grading and Drainage Plans


REV.	DESCRIPTION	APP'D	DATE
1			
2			
3			
4			
5			
6			
7			
8			
9			
10			
11			
12			
13			
14			
15			
16			
17			
18			
19			
20			
21			
22			
23			
24			
25			
26			
27			
28			
29			
30			
31			
32			
33			
34			
35			
36			
37			
38			
39			
40			
41			
42			
43			
44			
45			
46			
47			
48			
49			
50			
51			
52			
53			
54			
55			
56			
57			
58			
59			
60			
61			
62			
63			
64			
65			
66			
67			
68			
69			
70			
71			
72			
73			
74			
75			
76			
77			
78			
79			
80			
81			
82			
83			
84			
85			
86			
87			
88			
89			
90			
91			
92			
93			
94			
95			
96			
97			
98			
99			
100			

LEGEND

---	PROPERTY LINE
---	PROPOSED CLEARING LIMIT
WF #JMM12	INLAND WETLAND FLAG
---	EXISTING CONTOUR
---	EXISTING SPOT ELEVATION
---	PROPOSED CONTOUR
---	PROPOSED SPOT ELEVATION
● B7	SOIL BORING
---	PROPOSED INTERLOCKING CONCRETE BLOCKS
---	RIPRAP
---	PROPOSED CONCRETE
---	PROPOSED BUILDING
---	STORMWATER PIPE
---	PERFORATED STORMWATER PIPE
---	PROPOSED FLOWAGE RIGHTS TO BE GRANTED TO FIRSTLIGHT POWER

NOTES:

1. THE LOCATION OF ALL STRUCTURES, EQUIPMENT, DELINEATIONS AND OTHER FEATURES PRESENTED ON THIS DRAWING SHOULD BE CONSIDERED APPROXIMATE. THIS DRAWING SHOULD ONLY BE USED FOR GENERAL PRESENTATION PURPOSES AND SHOULD NOT BE USED FOR CONSTRUCTION PURPOSES. TRITON MAKES NO WARRANTY AS TO THE CORRECTNESS OR THE COMPLETENESS OF THE INFORMATION CONTAINED IN THIS DRAWING, AND THE USER ASSUMES ALL RISK OF LOSS TO PERSONS AND PROPERTY FROM RELIANCE THEREON.
2. THE MAXIMUM AND MINIMUM SUMMER WATER ELEVATIONS FOR CANDLEWOOD LAKE WERE DETERMINED USING THE FIRSTLIGHT POWER "CONNECTICUT SHORELINE MANAGEMENT MANUAL, TABLE 1 - PROJECT BOUNDARY AND OPERATING ELEVATIONS (FEET) NOW" AND CONVERTED TO NAVD83.
3. BASE MAP INFORMATION IS FROM A "TOPOGRAPHIC SURVEY" PREPARED BY GESICK & ASSOCIATES, P.C., DATED: NOVEMBER 6, 2019; SCALE: 1"=30', "FATHOMETRIC SURVEY" PREPARED BY HYDROGRAPHIC SURVEYS; DATED: NOVEMBER 20, 2019; SCALE: 1"=20'. A "TOPOGRAPHIC SURVEY" PREPARED BY GODFREY, HOFFMAN, HODGE; DATED: MARCH 24, 2026; SCALE: 1"=30', AND A "HYDROGRAPHIC SURVEY PLAN" PREPARED BY MATRIX NEW WORLD; DATED: APRIL 16, 2026; SCALE: 1"=20'.



TRITON ENVIRONMENTAL
A TRUE ENVIRONMENTAL COMPANY

385 Church Street, Suite 201 • Guilford, Connecticut 06437 • 203.458.7200


C3.0
GRADING, DRAINAGE, AND UTILITY PLAN

SQUANTZ COVE BOAT LAUNCH
PROJECT #DEPA00013203701

CONNECTICUT DEEP
210 ROUTE 39 (SHERMAN ROAD)
NEW FAIRFIELD, CONNECTICUT

DRAWN BY: FSM	APPROVED BY: SJB
DATE: 6/11/26	SCALE: 1"=30' FILE No.: R25-00007-BLD-14

SEAL & SIGNATURE



EARTHWORK ESTIMATE

MILLINGS GENERATED ONSITE FOR REUSE = 569 C.Y.
MATERIAL GENERATED ONSITE NOT SUITABLE FOR REUSE (BOAT LAUNCH) = 269 C.Y.
MATERIAL IMPORTED FROM OFFSITE = 6,485 C.Y.
(PAVEMENT, CONCRETE, PRECAST CONCRETE, STONE, AND BIOMATERIAL)
SURPLUS SOIL FOR REUSE/DISPOSAL = 20,357 C.Y.

NOTES:
1. SOIL REUSE VOLUME ESTIMATE HAS NOT CONSIDERED GEOTECHNICAL OR ENVIRONMENTAL SUITABILITY.

ACCESS ROAD PROFILE

NOT TO SCALE

PROPOSED 20'x6'x18" THICK MODIFIED RIPRAP OUTLET PROTECTION
TOP OF STONE AT PIPE INVERT=434.0'
TOP OF STONE 4' DOWNSTREAM OF INVERT=432.0'
TOP OF STONE 6' DOWNSTREAM=433.0'

Candlewood Lake
(Water Elevation = 425.4')
(11/5/2019) (NAVD 1988)

OPERATING ELEVATION LINE
ELEV= 427.30' (NAVD 1988)

PROPOSED STORMWATER QUALITY
SWALE W/ UNDERDRAIN
(SEE EAST SWALE DETAIL)

400 LF OF 6" PERFORATED PVC
INSTALL CLEANOUT AT UPSTREAM
LIMIT AND 100' O.C.

50' LF OF SOLID 6" PVC
INV=434.92'

PROPOSED 24"x12"
QUAZITE BOX

PROPOSED 24"x12"
QUAZITE BOX

PROPOSED 24"x12"
QUAZITE BOX

PROPOSED 24"x12"
QUAZITE BOX

PROPOSED 24"x12"
QUAZITE BOX

PROPOSED 24"x12"
QUAZITE BOX

PROPOSED 24"x12"
QUAZITE BOX

PROPOSED 24"x12"
QUAZITE BOX

PROPOSED 24"x12"
QUAZITE BOX

Appendix H

**CT DEEP National Pollutant Discharge Elimination System General Permit
for the Discharge of Stormwater from Construction Activities (effective
January 2026)**



National Pollutant Discharge Elimination System General Permit for the Discharge of Stormwater from Construction Activities

Permit No.: CTR100000

This National Pollutant Discharge Elimination System *General Permit for the Discharge of Stormwater from Construction Activities* is issued in accordance with Section 22a-430 of Chapter 446k, Connecticut General Statutes (“Conn. Gen. Stat.”), and Regulations of Connecticut State Agencies (“Regs. Conn. State Agencies”) adopted thereunder, as amended, and Section 402(b) of the Clean Water Act (“CWA”), as amended, 33 USC 1251, et. seq., and pursuant to an approval dated September 26, 1973, by the Administrator of the United States Environmental Protection Agency for the State of Connecticut to administer a NPDES permit program. Persons shall comply with all conditions of this permit.

This permit becomes effective January 1, 2026. This permit and the authorization to discharge shall expire sixty (60) months (five (5) years) from the effective date. This permit expires on December 31, 2030.

Issued: January 1, 2026

Emma Cimino
Deputy Commissioner

This page is intentionally left blank.

Table of Contents

Section 1	Authority	5
Section 2	Authorization Under This General Permit	5
2.1	Eligible Activities	5
2.2	Requirements for Authorization.....	6
2.3	Geographic Area	14
2.4	Effective Date and Expiration Date of this General Permit	14
2.5	Effective Date of Authorization	14
2.6	Transition to and from an Individual Permit.....	16
Section 3	Application Requirements	17
3.1	Who Must File an Application.....	17
3.2	Scope of Application	17
3.3	Application Requirements	17
3.4	Contents of Application	19
3.5	Notice of Change	22
3.6	New Application Required	22
3.7	Change of Permittee.....	22
3.8	Additional Information	23
3.9	Where to File an Application and Stormwater Construction Pollution Plan.....	23
3.10	Availability of Application and Stormwater Pollution Control Plan	23
3.11	Actions by Commissioner.....	24
Section 4	Termination Requirements.....	26
4.1	Notice of Termination.....	26
4.2	Termination Requirements.....	26
4.3	Where to File a Termination Form.....	27
Section 5	Conditions of this General Permit	28
5.1	General Conditions	28
5.2	Stormwater Pollution Control Plan.....	30
5.3	Reporting and Record Keeping Requirements.....	44
Section 6	Duty to Correct, Record, and Report Violations	46
6.1	Corrective Actions	46
6.2	Reporting Violations.....	46
Section 7	Regs. Conn. State Agencies Incorporated into this General Permit	48
7.1	Section 22a-430-3.....	48
7.2	Section 221-430-4.....	48
Section 8	Standard Conditions	49
8.1	Inspection and Entry	49
8.2	Reliance on Application.....	49
8.3	Submission of Documents	49
8.4	Violations.....	49
8.5	Enforcement.....	49
8.6	Need to Halt or Reduce Activity Not a Defense.....	49
8.7	No Assurance.....	49
8.8	Relief	49
8.9	Duty to Provide Information.....	49
8.10	Duty to Comply	50
8.11	Duty to Mitigate.....	50
8.12	Sludge Disposal	50
8.13	Resource Conservation	50

8.14	Spill Prevention and Control.....	50
8.15	Duty to Reapply.....	50
8.16	Equalization	51
8.17	Effect of an Upset	51
8.18	Bypass.....	51
8.19	Proper Operation and Maintenance.....	52
8.20	Instrumentation, Alarms, and Flow Records.....	52
8.21	Signatory Requirements.....	52
8.22	Date of Filing.....	53
8.23	False Statements	53
8.24	Correction of Inaccuracies	54
8.25	Transfer of Authorization	54
8.26	Other Applicable Law.....	54
8.27	Duty to Reapply.....	54
8.28	Other Rights.....	54
8.29	Effect of a Permit.....	54
Section 9	Commissioner’s Powers	55
9.1	Abatement of Violations	55
9.2	General Permit Revocation, Suspension, or Modification	55
9.3	Filing of an Individual Permit Application	55
Section 10	Definitions	56
Section 11	Appendices	63
11.1	Appendix A – Endangered and Threatened Species	63
11.2	Appendix B – RESERVED	63
11.3	Appendix C – Aquifer Protection Guidance Information	63
11.4	Appendix D – Coastal Management Act Determination Form.....	63
11.5	Appendix E & F – Memoranda of Agreement Between DEEP and Conservation Districts.....	63
11.6	Appendix G – Historic Preservation Review	63
11.7	Appendix H – Wild & Scenic Rivers Guidance.....	63
11.8	Appendix I – Stormwater Management at Solar Array Construction Projects	63
11.9	Appendix J – CT DEEP Financial Assurance Irrevocable Letter of Credit.....	63

General Permit for the Discharge of Stormwater from Construction Activities

Section 1 Authority

This general permit is issued under the authority of Section 22a-430b of the Connecticut General Statutes (“Conn. Gen. Stat.”).

Section 2 Authorization Under This General Permit

2.1 Eligible Activities

This general permit authorizes the discharge of stormwater from construction activities, as defined in this general permit as “any activity and discharges associated with construction at a site or the site’s preparation for construction including, but not limited to, clearing, grubbing, pile driving, soil disturbance, soil compaction by construction equipment, staging and stockpiling, storage, cleaning and washout, grading, excavation, and dewatering,” with a total disturbance of one (1) or more acres of land area for the entire project regardless of project phasing to waters of the State of Connecticut provided the requirements of this section are satisfied and the activity is conducted in accordance with this permit.

In the case of a larger plan of development (such as a subdivision), the estimate of total acres of site disturbance shall include, but is not limited to, road and utility construction, individual lot construction (e.g. house, driveway, septic system, etc.), and all other construction associated with the overall plan, regardless of the individual parties responsible for construction of these various elements.

2.1.1 Allowable non-stormwater discharges

The following non-stormwater discharges associated with the construction activity are authorized under this permit provided that, with the exception of water used to control dust and to irrigate vegetation in stabilized areas, these discharges are not routed to areas of exposed soil on the site, are included in the Stormwater Pollution Control Plan, and the Permittee complies with the applicable requirements of Section 5.2:

- uncontaminated discharges from construction dewatering operations in accordance with requirements of Section 5.2.2.8.
- uncontaminated and non-turbid discharges from natural springs or naturally occurring groundwater.
- foundation or footing drains where flows are not contaminated with process materials such as solvents or contaminated ground water.
- discharges from emergency fire-fighting activities.
- landscape irrigation.
- water used to control dust.
- potable water including uncontaminated water line or fire hydrant flushing.
- uncontaminated air conditioning or compressor condensate.

All other non-stormwater discharges except those specifically listed are not authorized by this permit. Such discharges to surface water must be authorized under a different permit issued by the Commissioner (pursuant to Section 22a-430 or 22a-430b of the Conn. Gen. Stat.).

2.1.2 Emergency Construction Activity Exception

The general permit authorizes short-term discharges of stormwater from construction activities in response to a public emergency as determined by the Commissioner (e.g., mud slides, earthquake, extreme flooding conditions, widespread disruption in essential public services), when the related work requires immediate authorization to avoid imminent endangerment to human health, public safety, or the environment, or to reestablish essential public services.

2.2 Requirements for Authorization

This general permit authorizes the discharge of stormwater from construction activity and associated discharges listed in the Section 2.1 “Eligible Activities” of this general permit provided the following conditions are met:

2.2.1 Limitations of Coverage

2.2.1.1 Prohibited discharges

The following discharges are prohibited:

- wastewater from washout of concrete, unless managed in accordance with Section 5.2.2.11.b of this general permit and the Connecticut Guidelines for Soil Erosion and Sediment Control (“the Guidelines”).
- wastewater from washout and/or cleanout of stucco, paint, form release oils, curing compounds, and other construction materials.
- fuels, oils, or other pollutants used in vehicle and equipment operation and maintenance.
- soaps, solvents, or detergents used in vehicle and equipment washing or external building washdown.
- toxic or hazardous substances from a spill or other release.
- discharges from dewatering activities, including discharges from dewatering of trenches and excavations, are prohibited unless managed by appropriate Control Measures.
- discharges containing or resulting in a visible oil sheen, floating solids, or foam.
- discharge of litter, debris, building materials, hardened concrete waste, or similar materials from the site.
- process wastewater as defined by 40 Code of Federal Regulations (“CFR”) 122.2.
- slurry materials and waste from shaft drilling, including process wastewater from shaft drilling for construction of building, road, and bridge foundations unless managed to prevent discharge to surface water.
- wheel wash wastewater, unless managed in accordance with Section 5.2.2.11.c of this general permit and the Guidelines.
- discharges of water, substance, or material into the waters of the State other than eligible discharges specified in this general permit.
- eligible discharges to publicly or privately owned storm sewers or conveyances without notification being provided to the owner.
- the stormwater discharge resulting from an activity classified by the Standard Industrial Classification 10 and 12 through 14 (the mining industry) is not eligible to be authorized by this general permit and is regulated under the General Permit for the Discharge of Stormwater Associated with Industrial Activity.
- discharges of dewatering waters known to contain pollutants other than sediment.
- discharges of polychlorinated biphenyl (“PCB”) compounds.
- discharges of mercury compounds.

2.2.2 Complete Application

A complete application pursuant to Section 3 of this general permit shall be filed with the Commissioner.

2.2.3 Coastal Management Act

Such construction activity must be consistent with all applicable goals and policies in Section 22a-92 of the Conn. Gen. Stat. and must not cause adverse impacts to coastal resources as defined in Section 22a-93(15) of the Conn. Gen. Stat. Please refer to the Appendix D for additional guidance.

2.2.4 Endangered and Threatened Species

Such construction activity must not threaten the continued existence of any species listed pursuant to Section 26-306 of the Conn. Gen. Stat. as endangered or threatened and must not result in the destruction or adverse modification of habitat designated as essential to such species. See Appendix A for permit terms and conditions.

2.2.5 Aquifer Protection Areas

Such construction activity, if it is located within an aquifer protection area as mapped under Section 22a-354b of the Conn. Gen. Stat., must comply with regulations adopted pursuant to Section 22a-354i of the Conn. Gen. Stat. Please refer to the Appendix C for guidance. For any construction activity regulated pursuant to the Aquifer Protection Regulations in Sections 22a-354i-8(c) and 9(b) of the Regs. Conn. State Agencies, the Stormwater Pollution Control Plan (“SPCP”) must provide sufficient information to assure that stormwater discharge generated from the construction activity is (i) managed in a manner so as to prevent pollution of groundwater, and (ii) complies with all the requirements of this general permit.

2.2.6 Conservation and Preservation Restrictions

Such construction activity, if located within a conservation or preservation restriction area, complies with Section 47-42d of the Conn. Gen. Stat., by providing the following documentation to the Commissioner: proof of written notice to the holder of such restriction of the proposed activity’s application pursuant to this general permit or a letter from the holder of such restriction verifying that the proposed activity is in compliance with the terms of the restriction.

2.2.7 Historic Preservation

Such construction activity, in accordance with the criteria in Appendix G, complies with state Historic Preservation statutes, regulations, and policies including identification of any potential impacts on property listed or eligible for listing on the Connecticut Register of Historic Places. A review conducted for an Army Corps of Engineers Section 404 wetland permit would meet this qualification. Refer to Appendix G for guidance on conducting the required review.

2.2.8 Wild and Scenic Rivers Act

Such construction activity must be consistent with the Wild and Scenic Rivers Act (16 U.S.C. 1271-1287) for those river components and tributaries which have been designated as Wild and Scenic by the United States Congress. Further, such construction activities must not have a direct and adverse effect on the values for which such river designation was established. Please refer to Appendix H for guidance.

2.2.9 Antidegradation

2.2.9.1 New or Increased Discharges to High Quality Waters

Any new or increased discharge of stormwater to a High Quality Water (as identified by the Commissioner consistent with the Water Quality Standards shall be discharged in accordance with the Connecticut Anti-Degradation Implementation Policy in the Water Quality Standards regulation (Section 22a-426 of the Regs. Conn. State Agencies). Before commencing any new or increased discharge, the Permittee must identify in its Stormwater Pollution Control Plan (“SPCP”), the Control

Measures it will implement to ensure compliance with anti-degradation provisions and the terms of this permit. At a minimum, the Permittee shall evaluate and implement measures and practices consistent with Best Available Technology Economically Achievable (“BAT”) that will prevent the discharge of the Water Quality Volume (“WQV”) to a surface water body or other practices necessary to protect and maintain designated uses and meet standards and criteria contained in the Water Quality Standards.

2.2.9.2 Discharges to Impaired Waters

For any portion of the site that discharges stormwater into a waterbody that is listed as impaired for sediment or a sediment-related impairment in the State’s Integrated Water Quality Report as of the effective date of this general permit, the Permittee shall comply with the requirements of Section 5.2.3 of this permit. Additionally, the Commissioner may require new or enhanced Control Measures or outfall monitoring, as necessary to protect instream water quality standards. These Control Measures may include those necessary for the stormwater discharge to be consistent with the assumptions of any available load allocation in any applicable TMDL or Watershed Action Plan.

2.2.9.3 For discharges to other impaired waters or waters with an established TMDL

If the Permittee discharges stormwater into a waterbody that is impaired for a parameter other than a sediment or sediment-related parameter, the Commissioner may inform the Permittee if any additional measures are necessary for the discharge to be controlled as necessary to protect the instream water quality standards. These Control Measures may include those necessary for the discharge to be consistent with the assumptions of any available load allocation in any applicable TMDL or Watershed Action Plan. In addition, the Commissioner may require the Permittee to apply for and obtain coverage under an individual permit.

2.2.10 Cold Water Stream Habitat

Unless otherwise authorized in writing by the Commissioner, a Permittee shall maintain a one-hundred (100) foot buffer of undisturbed soil and well-established vegetation between any construction activity and any stream, river, or tributary that is included within a cold water stream habitat as defined in regulation and accessible on DEEPs website here: <https://portal.ct.gov/DEEP/Water/Inland-Water-Monitoring/Cold-Water-Stream-Habitat-Map>.

2.2.11 Discharge to POTW

The stormwater is not discharged to a privately or Publicly Owned Treatment Works (“POTW”).

2.2.12 Discharge to Groundwater

The stormwater is not discharged entirely to groundwater.

2.2.13 Certification Requirements for Applicants and other Individuals

As part of the application for this general permit, the applicant and any other individual or individuals responsible for preparing the application submits to the Commissioner a written certification which, at a minimum, complies with the following requirements:

2.2.13.1 Review

The applicant and any other individual or individuals responsible for preparing the application and signing the certification has completely and thoroughly reviewed, at a minimum, this general permit and the following regarding the activities to be authorized under such general permit:

- a. All application information provided in accordance with Section 3.3 of this general permit.
- b. The project site, based on a site inspection.

- c. The Stormwater Pollution Control Plan.
- d. Any plans and specifications and any Department approvals regarding such Stormwater Pollution Control Plan.

2.2.13.2 Affirmative Determination

The applicant and any other individual or individuals responsible for preparing the application and signing the certification pursuant to this general permit has, based on the review described in Section 2.2.13.1 of this general permit, made an affirmative determination to:

- a. Comply with the terms and conditions of this general permit.
- b. Maintain compliance with all plans and documents prepared pursuant to this general permit including, but not limited to, the Stormwater Pollution Control Plan.
- c. Properly implement and maintain the elements of the Stormwater Pollution Control Plan.
- d. Properly operate and maintain all stormwater management systems in compliance with the terms and conditions of this general permit to protect the waters of the State from pollution.

2.2.13.3 The applicant and any other individual or individuals responsible for preparing the application certifies to the following statement:

"I hereby certify that I am making this certification in connection with an application under the General Permit for the Discharge of Stormwater from Construction Activities (general permit), submitted to the Commissioner by [INSERT NAME OF APPLICANT] for an activity located at [INSERT ADDRESS OF PROJECT OR ACTIVITY] and that all terms and conditions of the general permit will be met for all discharges which will be initiated and such activity is eligible for authorization under such permit. I further certify that a system is in place to ensure that all terms and conditions of this general permit will continue to be met for all discharges authorized by this general permit at the site. I certify that the application filed pursuant to this general permit is on complete and accurate forms as prescribed by the Commissioner without alteration of their text. I certify that I have personally examined and am familiar with the information that provides the basis for this certification, including but not limited to all information described in Section 2.2.13.1 of such general permit, and I certify, based on reasonable investigation, including my inquiry of those individuals responsible for obtaining such information, that the information upon which this certification is based is true, accurate and complete to the best of my knowledge and belief. I certify that I have made an affirmative determination in accordance with Section 2.2.13.2 of this general permit. I understand that the application filed in connection with such general permit is submitted in accordance with and shall comply with the requirements of Section 22a-430b of Conn. Gen. Stat. I also understand that knowingly making any false statement in the submitted information and in this certification may be punishable as a criminal offense, including the possibility of fine and imprisonment, under Section 53a-157b of the Conn. Gen. Stat. and any other applicable law."

2.2.14 Designing Professional Engineer or Landscape Architect Certification

The applicant submitted to the Commissioner a written certification by a professional engineer or, where appropriate, a landscape architect licensed in the State of Connecticut for the preparation, planning and design of the Stormwater Pollution Control Plan ("SPCP") and stormwater management systems.

The professional engineer or landscape architect shall certify to the following statement:

"I hereby certify that I am a [professional engineer] [landscape architect] licensed in the State of Connecticut. I am making this certification in connection with a application under the General Permit for the Discharge of Stormwater from Construction Activities (general permit), submitted to the Commissioner by [INSERT NAME OF APPLICANT] for an activity located at [INSERT ADDRESS OF PROJECT OR ACTIVITY]. I certify that I have thoroughly and completely reviewed the Stormwater Pollution Control Plan for the project or activity covered by this certification. I further certify, based on such review and on the standard

of care for such projects, that the Stormwater Pollution Control Plan has been prepared in accordance with the Connecticut Guidelines for Soil Erosion and Sediment Control, as amended, the Stormwater Quality Manual, as amended, and the conditions of the general permit, and that the controls required for such SPCP are appropriate for the site. I further certify, based on reasonable investigation, including my inquiry of those individuals responsible for obtaining such information, that the information upon which this certification is based is true, accurate and complete to the best of my knowledge and belief. I also understand that knowingly making any false statement in this certification may subject me to sanction by the Department and/or be punishable as a criminal offense, including the possibility of fine and imprisonment, under Section 53a-157b of the Conn. Gen. Stat. and any other applicable law."

2.2.15 Stormwater Pollution Control Plan Review and Certification by a District for Locally Approvable Projects

For Locally Approvable Projects, any Stormwater Pollution Control Plan ("SPCP" or "Plan") not reviewed in accordance with Section 2.2.16 below, the applicant has submitted to the Commissioner a written certification by the appropriate regional Soil and Water Conservation District ("District"), as defined in this general permit, for the review of the Stormwater Pollution Control Plan pursuant to Appendix E, which, at a minimum, complies with the following requirements:

2.2.15.1 Plan Review Certification

The Plan Review Certification must be signed by an authorized representative of the District. Information on the District review process is outlined in the Memorandum of Agreement provided in Appendix E. In cases where the District is unable to complete the review of the SPCP within the time limits specified in the Memorandum of Agreement in Appendix E, a notice to that effect signed by an authorized representative of the District may be submitted in lieu of the certification.

2.2.15.2 Stormwater Pollution Control Plan

The Stormwater Pollution Control Plan has been prepared in accordance with the requirements of Section 5.2 of the general permit.

2.2.16 Stormwater Pollution Control Plan Review and Certification by a Qualified Professional for Locally Approvable Projects

For the purposes of this section, a "Qualified Professional" is either a Qualified Soil Erosion and Sediment Control Professional or a Qualified Professional Engineer licensed in the state of Connecticut and in good standing.

2.2.16.1 Qualified Professional Criteria

a. Projects with an engineered stormwater management system

For projects with an engineered stormwater management system, if the SPCP is not reviewed in accordance with Section 2.2.15 above, the applicant shall submit to the Commissioner a signed certification by a Qualified Professional engineer.

b. Projects without an engineered stormwater management system

For projects without an engineered stormwater management system, if the SPCP is not reviewed in accordance with Section 2.2.15 above, the applicant shall submit to the Commissioner a written certification by a qualified soil erosion and sediment control professional or Qualified Professional engineer.

2.2.16.2 Certification by Qualified Professional

All projects shall submit a signed certification by a Qualified Professional to the Commissioner in accordance with the following requirements:

- a. For projects disturbing more than one acre and less than twenty (20) acres, such Qualified Professional:
 - i. Is not an employee, as defined by the Internal Revenue Service in the Internal Revenue Code of 1986, of the applicant.
 - ii. Has no ownership interest or monetary investment of any kind in the project for which the application is being submitted.
- b. For projects disturbing twenty (20) acres or more, such Qualified Professional:
 - i. Is not an employee, as defined by the Internal Revenue Service in the Internal Revenue Code of 1986, of the applicant.
 - ii. Has no ownership interest or monetary investment of any kind in the project for which the application is being submitted.
 - iii. Did not engage in any activities associated with the preparation, planning, designing or engineering of such plan for soil erosion and sediment control or plan for stormwater management systems on behalf of such applicant.
 - iv. Is not under the same employ as any person who engaged in any activities associated with the preparation, planning, designing or engineering of such plans and specifications for soil erosion and sediment control or plans and specifications for stormwater management systems on behalf of such applicant.

2.2.16.3 The Qualified Professional signing the certification has, at a minimum, completely and thoroughly reviewed this general permit and the following regarding the discharges to be authorized under such general permit:

- a. All application information provided in accordance with Section 3.3 of this general permit.
- b. The site, based on a site inspection.
- c. The Stormwater Pollution Control Plan.
- d. The Guidelines.
- e. The Stormwater Quality Manual, if applicable.
- f. All non-engineered and engineered stormwater management systems, including any plans and specifications and any approvals by the Commissioner regarding such stormwater management systems.

2.2.16.4 Affirmative Determination

- a. Qualified Soil Erosion & Sediment Control Professional

The qualified soil erosion and sediment control professional signing the certification must have made an affirmative determination, based on the review described in Section 2.2.13.1 of this general permit that:

- i. The Stormwater Pollution Control Plan prepared and certified pursuant to the application is adequate to assure that the project or activity authorized under this general permit, if implemented in accordance with the Stormwater Pollution Control Plan, will comply with the terms and conditions of such general permit.
- ii. All non-engineered stormwater management systems:
 - have been designed to control pollution using measures that reflect the Best Available Technology economically achievable (“BAT”), and that conform to the Guidelines and the Stormwater Quality Manual.

- will function properly as designed and constructed.
- are adequate to ensure compliance with the terms and conditions of this general permit.
- will not cause or contribute to violations of the instream water quality standards and protect the waters of the State from pollution.

iii. There are no engineered stormwater management systems for the site.

b. Qualified Professional Engineer

The Qualified Professional engineer, licensed in the state of Connecticut and in good standing, signing the certification must have made an affirmative determination, based on the review described in Section 2.2.13.1 of this general permit that:

- The Stormwater Pollution Control Plan prepared and certified pursuant to the application is adequate to assure that the activity authorized under this general permit, if implemented in accordance with the Stormwater Pollution Control Plan, will comply with the terms and conditions of such general permit.
- All non-engineered and engineered stormwater management systems:
 - have been designed to control pollution to the BAT and that conform to those in the Guidelines and the Stormwater Quality Manual.
 - will function properly as designed.
 - are adequate to ensure compliance with the terms and conditions of this general permit. and
 - will protect the waters of the State from pollution.

2.2.16.5 The Qualified Professional shall, provided it is true and accurate, certify to the following statement:

“I hereby certify that I am a Qualified Professional engineer licensed in the state of Connecticut and in good standing or a qualified soil erosion and sediment control professional, or both, as defined in the General Permit for Discharge of Stormwater from Construction Activities (general permit) and as further specified in Sections 2.2.16.1.a and 2.2.16.1.b of the general permit. I am making this certification in connection with an application under such general permit, submitted to the Commissioner by [INSERT NAME OF APPLICANT] for an activity located at [INSERT ADDRESS OF PROJECT OR ACTIVITY]. I have personally examined and am familiar with the information that provides the basis for this certification, including but not limited to all information described in Section 2.2.16.3 of such general permit, and I certify, based on reasonable investigation, including my inquiry of those individuals responsible for obtaining such information, that the information upon which this certification is based is true, accurate and complete to the best of my knowledge and belief. I further certify that I have made the affirmative determination in accordance with Sections 2.2.13.2 and 2.2.16.4 of this general permit. I understand that this certification is part of an application submitted in accordance with Section 22a-430b of Conn. Gen. Stat. and is subject to the requirements and responsibilities for a Qualified Professional in such statute. I also understand that knowingly making any false statement in this certification may be punishable as a criminal offense, including the possibility of fine and imprisonment, under Section 53a-157b of the Conn. Gen. Stat. and any other applicable law.”

2.2.17 Plan Review and Certification for Projects Conducted by State Agencies

For construction activity owned or operated by a state of Connecticut agency (e.g. Department of Transportation (CTDOT), Department of Administrative Services (DAS), etc.), the applying agency has submitted to the Commissioner a signed certification by a Qualified Professional in accordance with the following requirements:

- 2.2.17.1 The applying agency or another state agency has developed a process to establish a list of Qualified Professionals for which the process to qualify has been approved in writing by the Commissioner.
- 2.2.17.2 The Qualified Professional reviewing and certifying the SPCP is included on the list prepared by a state agency and for which the process to establish the list has been approved by the Commissioner pursuant to Section 2.2.17.1, above.
- 2.2.17.3 The Qualified Professional signing the certification has, at a minimum, completely and thoroughly reviewed this general permit and the following regarding the discharges to be authorized under such general permit:
- a. All application information provided in accordance with Section 3.3 of such general permit.
 - b. The site, based on a site inspection.
 - c. The Stormwater Pollution Control Plan.
 - d. The Guidelines.
 - e. The Stormwater Quality Manual, if applicable.
 - f. All non-engineered and engineered stormwater management systems, including any plans and specifications and any Department approvals regarding such stormwater management systems.
- 2.2.17.4 Affirmative Determination
- a. A qualified soil erosion and sediment control professional signing the certification must have made an affirmative determination, based on the review described in Section 2.2.13.1 of this general permit that:
 - i. The Stormwater Pollution Control Plan prepared and certified pursuant to the application is adequate to assure that the project or activity authorized under this general permit, if implemented in accordance with the Stormwater Pollution Control Plan, will comply with the terms and conditions of such general permit.
 - ii. All non-engineered stormwater management systems:
 - have been designed to control pollution to the BAT and that conform to those in the Guidelines and the Stormwater Quality Manual.
 - will function properly as designed.
 - are adequate to ensure compliance with the terms and conditions of this general permit.
 - will protect the waters of the State from pollution.
 - iii. There are no engineered stormwater management systems for the site.
 - b. A Qualified Professional engineer signing the certification must have made an affirmative determination, based on the review described in Section 2.2.13.1 of this general permit that:
 - i. The Stormwater Pollution Control Plan prepared and certified pursuant to the application is adequate to assure that the activity authorized under this general permit, if implemented in accordance with the Stormwater Pollution Control Plan, will comply with the terms and conditions of such general permit.
 - ii. All non-engineered and engineered stormwater management systems:
 - have been designed to control pollution to the BAT and that conform to those in the Guidelines and the Stormwater Quality Manual.
 - will function properly as designed.

- are adequate to ensure compliance with the terms and conditions of this general permit.
- will protect the waters of the State from pollution.

2.2.17.5 The Qualified Professional shall, provided it is true and accurate, certify to the following statement:

"I hereby certify that I am a Qualified Professional engineer licensed in the state of Connecticut and in good standing or qualified soil erosion and sediment control professional, or both, as defined in the General Permit for Discharge of Stormwater from Construction Activities and as further specified in Sections 2.2.16.1.a and 2.2.16.1.b of such general permit. I am making this certification in connection with an application under such general permit, submitted to the Commissioner by [INSERT NAME OF APPLICANT] for an activity located at [INSERT ADDRESS OF PROJECT OR ACTIVITY]. I have personally examined and am familiar with the information that provides the basis for this certification, including but not limited to all information described in Section 2.2.17.3 of such general permit, and I certify, based on reasonable investigation, including my inquiry of those individuals responsible for obtaining such information, that the information upon which this certification is based is true, accurate and complete to the best of my knowledge and belief. I further certify that I have made the affirmative determination in accordance with Sections 2.2.13.2 and 2.2.17.4 of this general permit. I understand that this certification is part of an application submitted in accordance with Section 22a-430b of Conn. Gen. Stat. and is subject to the requirements and responsibilities for a Qualified Professional in such statute. I also understand that knowingly making any false statement in this certification may be punishable as a criminal offense, including the possibility of fine and imprisonment, under Section 53a-157b of the Conn. Gen. Stat. and any other applicable law."

2.2.17.6 Applications for construction activities conducted by a state agency under this subparagraph may be submitted in accordance with the requirements in Sections 3.3.2.

2.2.18 Solar Arrays

For constructions activities associated with the development of a Solar Array that is categorized as Locally Exempt, as defined in Section 10 of this general permit, the applicant shall also comply with the requirements in Appendix I.

2.3 Geographic Area

This general permit applies throughout the State of Connecticut.

2.4 Effective Date and Expiration Date of this General Permit

This general permit is effective on the date it is issued by the Commissioner and expires five (5) years from such date. The general permit may be administratively continued in effect until the Department has reissued the permit in accordance with the Conn. Gen. Stat. and Regs. Conn. State Agencies. If the permit is administratively continued, Permittees are required to comply with all permit terms and conditions, including the monitoring requirements and submittal of reports at the original frequency during the continuance of the permit.

2.5 Effective Date of Authorization

2.5.1 Authorization to Discharge for Existing Permittees

Upon the effective date of this general permit, Permittees that had existing authorization to discharge under the *General Permit for the Discharge of Stormwater and Dewatering Wastewaters from Construction Activities*, issued December 31, 2020, ("Existing Permittees") shall have continued authorization to discharge under the terms and conditions of this general permit, provided the Permittee is in compliance with the terms and conditions of this general permit and a complete application for this general permit is submitted to the Commissioner in accordance with Section 3 of this general permit on or before ninety (90) days after the effective date of this general permit until the Commissioner makes a final determination regarding such application.

If the Existing Permittee does not submit an appropriate, complete, and accurate application requesting authorization to discharge under this general permit or a Notice of Termination, if applicable, on or before ninety (90) days following the effective date of this permit, authorization under this permit will terminate on such due date. The Permittee must then submit a new application in compliance with the full terms and conditions of this permit. The Commissioner will review and approve, reject, or deny such applications in writing.

2.5.2 Emergency Construction Activity Exception

For emergency construction activities (pursuant to Section 2.1.2) resulting in short-term discharges of stormwater from construction activities in response to a public emergency (e.g., mud slides, earthquake, extreme flooding conditions, widespread disruption in essential public services), when the related work requires immediate authorization to avoid imminent endangerment to human health, public safety, or the environment, or to reestablish essential public services, the date of authorization is the day the discharge initiated.

2.5.3 Locally Approvable Small Construction Activity

No application or SPCP review is required for Small Construction Locally Approvable Projects that will disturb an area equal to or greater than one (1) and less than five (5) acres, regardless of phasing, provided a land-use commission of the municipality (i.e. planning/zoning, wetland, conservation, etc.) reviews and issues a written approval of the proposed erosion and sediment Control Measures, pursuant to the requirements of Section 22a-329 of the Conn. Gen. Stat. The owner or operator shall adhere to the erosion and sediment control land use regulations of the municipality in which the construction activity is conducted, as well as the Guidelines and the Stormwater Quality Manual. The date of authorization is the day written approval is obtained.

In the absence of a municipal commission to review and approve such activity, the Permittee shall apply with the DEEP under the requirements for a “Locally Exempt Project” and comply with all applicable conditions of this general permit.

2.5.4 Authorization to Discharge for New Permittees

2.5.4.1 A new construction activity that has never been authorized to discharge under this general permit (“New Permittee”) is authorized to discharge in accordance with the terms and conditions of this general permit upon submittal of a complete application and after receiving a Notice of Coverage from the Commissioner in accordance with the following timelines:

a. Standard Authorization Timelines:

- i. For Locally Approvable Projects: sixty (60) days after submission of a complete application form.
- ii. For Locally Exempt Projects with a total disturbed area of under twenty (20) acres: sixty (60) days after submission of a complete application form.
- iii. For Locally Exempt Projects with a total disturbed area equal to or more than twenty (20) acres: ninety (90) days after submission of a complete application form.

2.5.4.2 Exceptions to the Standard Authorization Timelines

If either of the criteria apply below, authorization timelines shall supersede those in Subsection 2.5.4.1 above:

- a. For sites where the application and the Stormwater Pollution Control Plan (SPCP) availability and review provisions in Section 3.10 of this general permit are fulfilled prior to the expiration of the authorization timelines referenced in Subsection 2.5.4.1.a above, the Commissioner may grant authorization to discharge upon completion of those requirements.
- b. For sites where conditions of Section 2.2.4, 2.2.9 or Section 5.1.2 of the general permit apply, the construction activity is authorized only upon the date of the Commissioner's affirmative determination and/or Notice of Coverage.
- c. For Locally Exempt Projects conducted by a state agency, the construction activity may be authorized sixty (60) days after submission of a complete application form, regardless of the total disturbed area.

2.6 Transition to and from an Individual Permit

No person shall operate or conduct an activity authorized by both this general permit and an individual permit or an alternative general permit issued by the Commissioner. The requirements for transitioning authorization are as follows:

2.6.1 Transition from an Individual Permit to Authorization Under this General Permit

If an activity meets the requirements of authorization of this general permit and such operation or activity is presently authorized by an individual permit, the Permittee may seek a modification to the individual permit to exclude such operation or activity from that permit. If the operation or activity is the sole operation or activity authorized by such permit, the Permittee shall surrender its permit in writing to the Commissioner. In either event, such Permittee's individual permit shall continue to apply and remain in effect until authorization of such operation or activity under this general permit takes effect.

2.6.2 Transition from Authorization Under this General Permit to an Individual Permit

If an activity or operation is authorized under this general permit and the Commissioner subsequently issues an individual permit for the same activity, then on the date any such individual permit is issued by the Commissioner, the authorization issued under this general permit shall automatically expire.

Section 3 Application Requirements

3.1 Who Must File an Application

An application form is not required for an Emergency Construction Activity (Section 2.5.2) or “Small Construction Locally Approvable Activities” (Section 2.5.3).

For all other eligible construction activities, any person, municipality, or state agency that initiates, creates, originates, or maintains a discharge of stormwater from or associated with construction activities that disturb one (1) or more acres shall file with the Commissioner an application form that meets the requirements of this Section of this general permit. Such form shall be submitted along with the applicable fee within the timeframes and in the amounts specified in this Section.

3.2 Scope of Application

An applicant shall submit one (1) application for all discharges taking place at the site for which the application seeks authorization under this general permit. Discharges or activities taking place at more than one (1) site may not be consolidated on one (1) application form.

3.2.1 Application Fees

3.2.1.1 For Existing Permittees, construction activities that were authorized to discharge under the previous iteration of the general permit, the renewal fee shall be \$1,250.

3.2.1.2 For new Locally Approvable projects and Locally Exempt projects conducted by a state agency, the application fee shall be \$1,250.

3.2.1.3 New Locally Exempt Projects

For new Locally Exempt projects the application fee shall be as follows:

- a. For sites with total disturbance of one (1) or more acres, but less than twenty (20) acres, the fee shall be \$3,000.
- b. For sites with total disturbance equal to or greater than twenty (20) acres and less than fifty (50) acres, the fee shall be \$4,000.
- c. For sites with total disturbance equal to or greater than fifty (50) acres, the fee shall be \$5,000.

3.2.1.4 The fees for municipalities shall be half of those indicated, pursuant to Section 22a-6(b) of the Conn. Gen. Stat. State and Federal agencies shall pay the full fees specified in this subsection.

3.2.1.5 The application fee shall be paid to the Department of Energy & Environmental Protection.

3.2.1.6 An application shall not be deemed complete, and no activity shall be authorized by this general permit unless the application fee has been paid in full.

3.2.1.7 The application fee is non-refundable.

3.3 Application Requirements

All applications must be electronically submitted, along with all required elements. Failure to submit a complete application form with all the required components of the application may result in the rejection of the application and/or significant delay in the processing of the application.

3.3.1 Permittees with Existing Authorization to Discharge

3.3.1.1 Permittees Authorized Under Previous General Permit

Upon the effective date of this general permit, existing Permittees authorized under the previous version of this general permit shall submit a complete application electronically for authorization to discharge under this general permit to the Commissioner in accordance with the requirements of this general permit on or before ninety (90) days after the effective date of this general permit. The Permittee submitting such application is not required to submit stormwater management design information included in Sections 5.2.1.2.g and 5.2.2.9. For such Permittees subject to Appendix I for solar projects, the Permittee will not be required to modify any existing Letters of Credit to meet the provisions of Section 1.0(8)(d)(ii) of Appendix I.

3.3.1.2 Permittees Submitting New Application for Change of Permittee

For permittees submitting a new application for a construction activity with existing coverage authorized after the effective date of this permit, pursuant to Section 3.7 (Change of Permittee), the new permittee shall submit a complete application electronically for authorization to discharge under this general permit to the Commissioner in accordance with the requirements of Section 3.7. The Notice of Termination of the previous permittee's authorization shall be submitted in accordance with Section 4.2.2. If the new application includes any change of construction activities from those authorized in the existing application, the new Permittee is not eligible for authorization under this Section and a complete application must be submitted in accordance with the requirements of Section 3.3.2. or 3.3.3, as appropriate.

3.3.1.3 Permittees Authorized Under a Site Preparation Phase Permit for a Design-Build Project

For state or federal agencies submitting an application for a Final Design Phase Permit to supersede a Site Preparation Phase Permit previously authorized for a design-build project, the permittee shall submit a complete application electronically for authorization to discharge under this general permit to the Commissioner in accordance with the requirements of this general permit at least thirty (30) days prior to the termination of the Site Preparation Phase Permit authorization pursuant to Section 4.2.3.

3.3.2 Applicants for New Locally Approvable Projects

For applications for new Locally Approvable projects and Locally Exempt projects conducted by a state agency, the application shall:

- 3.3.2.1 Be submitted to the Commissioner at least sixty (60) days prior to the planned commencement of the construction activity.
- 3.3.2.2 Include all of the information that may be required pursuant to Section 2.2, "Requirements for Authorization" of the general permit regarding compliance and/or consistency with the Coastal Management Act, NDDB Determination Letter, Discharges to Impaired Waters and TMDL requirements, Fisheries Consultation, and Aquifer Protection Areas. *Failure to include these components may result in the rejection of the Application.*
- 3.3.2.3 Include a copy of the Stormwater Pollution Control Plan. The electronic SPCP shall be in Adobe™ PDF format or similar publicly available format in common use. The SPCP should not include any pages or other material that do not pertain to stormwater management or erosion and sediment control (such as electrical and lighting plans, boundary or lot surveys, building plans, non-stormwater related detail sheets, etc.). *The submission of these additional pages in the SPCP will delay the Department's review of the Application.*
- 3.3.2.4 Include a Plan Review Certification in accordance with the plan review certification requirements of either Section 2.2.15, 2.2.16, or 2.2.17 of the general permit.

3.3.3 Applications for New Locally Exempt Projects

Applications for new Locally Exempt projects (except those projects conducted by a state agency pursuant to Section 3.3.2), shall:

- 3.3.3.1 Be submitted at least:
 - a. Sixty (60) days prior to the planned commencement of the construction activity if the site has a total disturbance of between one (1) and twenty (20) acres.
 - b. Ninety (90) days prior to the planned commencement of construction activity if the site:
 - i. Has a total disturbance greater than twenty (20) acres.
 - ii. Discharges to a tidal wetland (that is not a fresh-tidal wetland) within 500 feet of the discharge point.
 - iii. Or is subject to the impaired waters provisions of Section 2.2.9.2 of the general permit.
- 3.3.3.2 Include all of the additional information that may be required pursuant to Section 2.2 of the general permit, “Requirements of Authorization”, regarding compliance and/or consistency with the Coastal Management Act, NDDB Determination Letter, Discharges to Impaired Waters including TMDL requirements, Fisheries Consultation, Historic Preservation Review, Solar Array provisions, and Aquifer Protection.
- 3.3.3.3 Include an electronic copy of the Stormwater Pollution Control Plan (SPCP) for the Commissioner’s review. The electronic SPCP shall be in Adobe™ PDF format. The SPCP should not include any pages or other material that does not pertain to stormwater management or erosion and sediment control (such as electrical and lighting plans, A-2 boundary or similar lot surveys, building plans, non-stormwater related detail sheets, etc.). *The submission of these additional pages in the SPCP will delay the Departments review of the application.*

3.4 Contents of Application

3.4.1 Standard Application Form

Applications shall be filed electronically on forms prescribed and provided by the Commissioner and include the following:

- 3.4.1.1 Legal name, mailing address, email address, and telephone number of the applicant. If the applicant is a person as defined in this permit transacting business in Connecticut and is registered with the Connecticut Secretary of the State, provide the exact name as registered with the Connecticut Secretary of the State.
- 3.4.1.2 Name, address, telephone number, contact’s name, title, phone number, and email address for the following, if different than the applicant:
 - Owner of the property on which the construction activity will take place.
 - Primary contact for departmental correspondence and inquiries, if different from the applicant.
 - Developer of the property on which the construction activity is to take place.
 - General contractor(s) or other representative(s), if different from the developer (day and night).
 - Qualified Professionals, engineer(s) or landscape architect(s) retained by the Permittee to prepare the application and/or the Stormwater Pollution Control Plan.

- 3.4.1.3 Physical address or description of the site for which the application is filed. If the site does not have a mailing address, provide the nearest crossroads, mile markers, latitude/longitude, or permanent structures to identify the location.
- 3.4.1.4 For Existing Permittees, the previously issued permit number.
- 3.4.1.5 The estimated duration of the construction activity.
- 3.4.1.6 Indication of the normal working hours at the site.
- 3.4.1.7 A brief description of the construction activity, including, but not limited to
 - a. Total number of acres to be disturbed, regardless of phasing.
 - b. Indication or Narrative description that construction is in accordance with The Guidelines and Stormwater Quality Manual and local erosion and sediment control ordinances, where applicable.
 - c. Assurances

Assurance that the Stormwater Pollution Control Plan is consistent with the requirements of this general permit and the following provisions of state statutes and regulations, as appropriate:

- i. For sites in the Coastal Boundary, documentation that the DEEP Land and Water Resources Division or local governing authority has issued a coastal site plan approval or a determination that the project is exempt from coastal site plan review (see Appendix D) in accordance with Section 22a-92 and 22a-93(15) of the Conn. Gen. Stat.
- ii. Documentation that the construction activity will not threaten the continued existence of any species listed pursuant to Section 26-306 of the Conn. Gen. Stat. as endangered or threatened and will not result in the destruction or adverse modification of habitat designated as essential to such species (see Appendix A). For sites located within a “listed species” habitat, applications must include a valid National Diversity Database Determination Letter Identification number.
- iii. For sites discharging to impaired waters or waters that have a TMDL or specific load allocation for the site, as specified in Section 2.2.9.3 of the general permit, documentation that the construction activity meets the requirements of that section and Section 5.2.3 of the general permit for authorization under this general permit.
- iv. Indication or documentation to determine if the construction activity is located within an aquifer protection area (see Appendix C) as mapped under Section 22a-354b of the Conn. Gen. Stat. If the site is partially or wholly in an aquifer protection area or public water supply watershed, provide a copy of correspondence with the local water company demonstrating that the construction activity will comply with regulations adopted pursuant to Section 22a-354i of the Conn. Gen. Stat.
- v. Documentation that the proposed construction activity has been reviewed for consistency with state Historic Preservation statutes, regulations, and policies including identification of any potential impacts on property listed or property eligible for listing on the Connecticut Register of Historic Places. A review conducted for an Army Corps of Engineers Section 404 wetland permit would meet this qualification. Refer to Appendix G for guidance on conducting the required review.
- d. For a Locally Approvable project, a plan review certification from the appropriate and authorized District, qualified soil erosion and sediment control professional, and/or Qualified Professional engineer in accordance with Section 2.2.15.1 or Section 2.2.16.4.a or Section 2.2.16.4.b or a notice from the District that they were unable to complete the SPCP review within the time limits specified in the Memorandum of Agreement in Appendix E.

- e. For construction activities within one hundred (100) feet of any stream, river, or tributary that is included within a Cold Water Stream Habitat, as may be authorized by the Commissioner pursuant to Section 2.2.10 of this general permit, a completed Fisheries Consultation Form or, for projects conducted by state agencies, documentation of official interagency coordination between the Fisheries Division and other state agency staff. An email is not considered official coordination.

3.4.1.8 Stormwater discharge information

- a. Name and waterbody ID of receiving stream(s) or waterbody(ies) to which the construction activity discharges and indication of whether or not a receiving stream is listed as an impaired water with or without a TMDL, including identification of the impairment in the most recent State of Connecticut Integrated Water Quality Report or identification of the receiving stream as a high quality water in the Connecticut Water Quality Standards.
- b. Number, type (e.g., swale or pipe), material (e.g., concrete or metal pipe, grass swale), and size of all outfalls that convey stormwater runoff from the site.
- c. Unique identifier (001, 002) and location of all stormwater discharge(s) including latitude and longitude.
- d. If the discharge enters a private or publicly owned storm sewer system, provide the name of the owner of the system.
- e. Indication whether or not the site discharges within 500 feet of a tidal wetland (not a fresh tidal wetland).
- f. Type of structural and nonstructural treatment practice used at each outfall or upgradient from each outfall if one exists.

3.4.1.9 The total effective impervious cover for the site before and after the proposed construction activity.

3.4.1.10 Stormwater Pollution Control Plan

- a. An electronic copy of the Stormwater Pollution Control Plan. The electronic SPCP shall be in Adobe™ PDF format.

Provide an internet address (URL) where the Pollution Control Plan is accessible for public review. The internet address shall remain available and accessible during the term of the permit.
- b. The SPCP should not include any pages or other material that do not pertain to stormwater management or erosion and sediment control (such as electrical and lighting plans, boundary or lot surveys, building plans, non-stormwater related detail sheets, etc.). Also, the full calculation sheets for peak flow analysis (e.g. HydroCAD), other than sheets providing a brief summary of peak flow and Water Quality Volume analyses, should not be included in the SPCP. The full calculation sheets shall be available upon request by the Commissioner. *The submission of these additional pages in the SPCP will delay the Departments review of the application.*
- c. SPCPs submitted for application must comply with all requirements listed in Section 5.2.1.2 of this general permit.

3.4.1.11 Certifications

- a. The certification of the applicant and of the individual or individuals responsible for preparing the application, in accordance with Section 2.2.13 of the general permit.
- b. A design certification must be signed by a professional engineer or, where appropriate, a landscape architect in accordance with Section 2.2.14 of the general permit.
- c. For Locally Approvable projects a signed certification must be submitted by either:

- i. An authorized representative of the District in accordance with Section 2.2.15 of the general permit.
- ii. A qualified soil erosion and sediment control professional and/or Qualified Professional engineer in accordance with either Section 2.2.16 of the general permit.
- d. The training certification(s) obtained by the Qualified Inspector.

3.4.2 Application for State or Federal Agency Design-Build Projects

3.4.2.1 Application for Site Preparation Projects

For a state or federal agency submitting an application for Early Release Construction (ERC) work for the Site Preparation Phase of a design-build project, the Permittee shall include in their application all information included in Section 3.4.1, above, except the peak flow and Water Quality Volume analyses in Section 3.4.1.10.b. The Permittee shall also not be subject to the Post-Construction Performance Standards in Section 5.2.2.9.

3.4.2.2 Application for Final Design Projects

For a state or federal agency submitting an application for the Final Design Phase of a design-build project, the Permittee shall include in their application all information included in Section 3.4.1, including identification of the Site Preparation Phase Permit number pursuant to Section 3.4.1.4.

3.5 Notice of Change

The Permittee shall submit a Notice of Change to the Commissioner electronically to the Department at: DEEP.StormwaterConstruction@ct.gov if any of the following criteria are met:

- To correct inaccurate or misleading information previously submitted to DEEP.
- Change of contractor.
- Changes to name of the project or site.
- Changes to the disturbed area on the site that reduces the distance to impaired waters, high quality waters, cold water habitat, endangered or threatened species habitat, or aquifer protection areas from those in the original SPCP. For increases of the disturbed area, see Section 3.6.
- Changes to engineered or non-engineered construction or post-construction Control Measures that have the potential to increase the rate or volume of stormwater discharged.

The Notice of Change shall be submitted before any such increases or changes are implemented. Changes to the SPCP documented under this section as well as those not requiring notice under this section shall continue to follow the provisions of Section 5.2.5, Keeping Pollution Control Plans Current.

3.6 New Application Required

For sites that increase the amount of disturbed area by more than one (1) acre from the amount specified in the application approved by the Commissioner, a new application shall be submitted to the Commissioner in accordance with Section 3 of the general permit.

3.7 Change of Permittee

Permit coverage is **not transferable**. When there is a change to the site's Permittee, the new Permittee must submit a new application to the Commissioner in accordance with Section 3 of this general permit within thirty (30) days following the date of transfer and the previous Permittee must submit a Notice of Termination (NOT) in accordance with Section 4 of this general permit.

3.8 Additional Information

The Commissioner may require an applicant to submit additional information that the Commissioner reasonably deems necessary to evaluate the consistency of the subject activity with the requirements for authorization under this general permit. A response to the Commissioner's request for additional information shall be submitted to the Department within fifteen (15) days of the Commissioner's request.

3.9 Where to File an Application and Stormwater Construction Pollution Plan

An application (available at: www.ct.gov/deep/stormwater) shall be filed electronically with the Commissioner in accordance with Section 3.4 of the general permit. If a permittee is not capable of submitting electronically, contact the DEEP stormwater staff at DEEP.StormwaterConstruction@ct.gov.

3.10 Availability of Application and Stormwater Pollution Control Plan

3.10.1 Application Availability

The application shall be made available for public review and comments by both the Permittee and the Commissioner.

3.10.1.1 Availability by the Permittee

- a. No later than five (5) days after submitting an application to the Commissioner, the Permittee shall make their application available to the following parties:
 - i. For discharges authorized by this general permit to a privately or publicly owned separate storm sewer system, a copy of the application that was submitted to the Department shall also be submitted to the owner and operator of that system.
 - ii. For discharges authorized by this general permit to a CTDOT separate storm sewer system, a copy of the application and all attachments thereto shall also be submitted to the CTDOT.
 - iii. For discharges within a public drinking water supply watershed or aquifer protection area, a copy of the application and the SPCP described in Section 5.2 of this general permit shall be submitted to the water company.
 - iv. For discharges to river components and tributaries which have been designated as Wild and Scenic under the Wild and Scenic Rivers Act, a copy of the application and the SPCP described in 5.2 of this general permit shall be submitted to the applicable Wild and Scenic Coordinating Committee. Please refer to Appendix H for additional guidance.
- b. A completed application shall be provided to the following persons immediately upon request:
 - i. The municipal planning commission, zoning commission and/or inland wetlands agency, or its respective enforcement officer or designated agent.
- c. Following approval of the application by the Commissioner, the Permittee shall make a copy of the application available to the public pursuant to the Notice of Construction Activities requirements in Section 5.1.7.

3.10.1.2 Availability by the Commissioner

The Commissioner shall post on the DEEP website a list of applications submitted. SPCPs shall be posted electronically, or a link to such plans provided, with the corresponding application. On or before thirty (30) days from the date such application is accessible to the public through posting by the Commissioner, members of the public may review and comment on an application and/or SPCP. This provision shall not apply to Permittee's submitting a Permit renewal for sites applied under any previous version of this general permit and for which no Notice of Termination has been submitted pursuant to the "Termination Requirements" in Section 4 of the general permit.

3.10.2 Stormwater Pollution Control Plan Availability

The Stormwater Pollution Control Plan (“SPCP”) shall be made available for public review and comments by both the Permittee and the Commissioner.

3.10.2.1 Availability by the Permittee

The Stormwater Pollution Control Plan shall be provided to the following persons immediately upon request:

- a. The municipal planning commission, zoning commission and/or inland wetlands agency, or its respective enforcement officer or designated agent.
- b. If the stormwater discharges through a municipal separate storm sewer system, the municipal operator of the system.
- c. If the stormwater discharge is located within a public drinking water supply watershed or aquifer protection area, the water company or entity responsible for that water supply.
- d. Following approval of the application by the Commissioner, the Permittee shall make a copy of the SPCP available to the public for the duration of construction pursuant to the Notice of Construction Activities requirements of Section 5.1.7.

3.10.2.2 Availability by the Commissioner

- a. On or before thirty (30) days of receipt of an application and SPCP, the Commissioner shall post the SPCP on the DEEP website.
- b. On or before thirty (30) days from the date of posting of the list by the Commissioner, members of the public may submit written comments to the Commissioner. Comments shall be sent via email to DEEP.StormwaterConstruction@ct.gov with the subject line “Construction GP Comments [INSERT NAME OF PERMITTEE].”

3.11 Actions by Commissioner

3.11.1 Approval with Permit Conditions

The Commissioner may approve an application with reasonable permit conditions. If the Commissioner approves the application with conditions, the Permittee shall be bound by such conditions as if they are part of this general permit.

3.11.2 Rejection or Denial

The Commissioner may reject or deny without prejudice an application if it is determined that it does not satisfy the application requirements in Section 3 of this general permit, or if more than fifteen (15) days have elapsed since the Commissioner requested the Permittee submit additional information to determine eligibility for permit coverage for authorization to discharge under this general permit. Any application refiled after such a rejection shall be accompanied by the fee specified in Section 3.2.1 of this general permit.

3.11.3 Require Individual Permit

The Commissioner may require that a Permittee obtain an individual permit for any discharge authorized by this permit in accordance with Section 22a-430b(c) of the Conn. Gen. Statutes.

3.11.4 Activity Inconsistent with Authorization Requirements

The Commissioner may reject or deny an application if he or she finds that the subject activity is inconsistent with the “Requirements for Authorization” in Section 2.2 of this general permit, or for any other reason provided by law.

3.11.5 Notice to Applicant

Denial or rejection of an application under this subsection shall constitute notice to the applicant that the subject activity may not lawfully be conducted or maintained without the issuance of an individual permit in accordance with Section 22a-430 of Regs. Conn. State Agencies.

3.11.6 Notice in Writing

Rejection or denial of an application shall be provided to the applicant in writing and state the reasons for such rejection or disapproval.

Section 4 Termination Requirements

4.1 Notice of Termination

A Notice of Termination (NOT) must be submitted to the Commissioner on a prescribed form under the following conditions: at the completion of the construction project; or, for projects for which there is a Change of Permittee pursuant to Section 3.7, upon approval of a new permit authorized pursuant to Section 3.3.1.2; or for a state or federal agency with a Site Preparation Phase Permit authorized pursuant to Sections 3.3.2 and 3.4.2.1, upon approval of a Final Design Phase Permit authorized pursuant to Sections 3.3.2 and 3.4.2.2.

For Solar Array Projects, also refer to Appendix I for additional requirements.

4.2 Termination Requirements

4.2.1 Standard Termination

A project shall be considered complete after all post-construction measures have been installed, cleaned, functioning, inspected, and the site has achieved final stabilization as defined in Section 10 for all phases of construction for at least one (1) year following the Final Stabilization Inspection. The termination process for a project for which the Permittee has completed construction and is obtaining a Notice of Termination shall include the following information:

4.2.1.1 A Notice of Termination form shall include the following:

- The permit number as provided to the Permittee on the Notice of Coverage.
- The name of the Permittee as reported on the general permit application form.
- The address of the completed construction site.
- A description of the post-construction activities at the site.
- A copy of the Termination Inspection.

4.2.1.2 The dates when:

- Construction was completed.
- All storm drainage structures were cleaned of construction debris pursuant to the “Other Controls” in Section 5.2.2.11 of this general permit.
- The Post-Construction Inspection was completed pursuant to Section 5.2.4.3.
- The Final Stabilization Inspection was completed pursuant to Section 5.2.4.4.
- The Termination Inspection was completed pursuant to Section 5.2.4.5.

4.2.1.3 Certifications and Signatures for the following:

- The Permittee.
- The person who conducted the Post-Construction Inspection pursuant to Section 5.2.4.3 of the general permit.
- The person who conducted the Final Stabilization Inspection pursuant to Section 5.2.4.4 of the general permit.
- The person who conducted the Termination Inspection pursuant to Section 5.2.4.5 of the general permit.

4.2.2 Termination Upon Change of Permittee

For termination of a permit for which there is a change of Permittee (pursuant to Section 3.7), the original Permittee shall submit their Notice of Termination on or before thirty (30) days following the approval of an application filed by the new Permittee pursuant to Section 3.3.1.2. The original Permittee shall include the following information in their Notice of Termination:

4.2.2.1 A Notice of Termination form shall include the following:

- The permit number as provided to the original Permittee on their Notice of Coverage.
- The name of the original Permittee as reported on their general permit application form.
- The address of the construction site.
- The permit number as provided to the new Permittee on their Notice of Coverage.
- The name of the new Permittee as reported on their general permit application form.

4.2.2.2 The dates when:

- The date of transfer of ownership or assignment of the project to the new Permittee.
- The date the new Permittee obtained authorization as provided on their Notice of Coverage.

4.2.2.3 Certifications and Signatures for the following:

- The original Permittee.
- The new Permittee.

4.2.3 Termination of Site Preparation Phase for Design-Build Projects by a State or Federal Agency

For termination of a Site Preparation Phase Permit authorized pursuant to Sections 3.3.2 and 3.4.2.1, the original Permittee shall include the following information in their Notice of Termination following the approval of an application for a Final Design:

4.2.3.1 A Notice of Termination form shall include the following:

- The permit number as provided to the Permittee on the Notice of Coverage for the Site Preparation Phase Permit.
- The address of the construction site.
- The permit number as provided to the Permittee on the Notice of Coverage for the Final Design Phase Permit.

4.2.3.2 The date when the Permittee obtained authorization as provided on their Notice of Coverage for the Final Design Phase Permit.

4.2.3.3 Certifications and Signatures for the Permittee.

4.3 Where to File a Termination Form

A termination form shall be filed electronically with the Commissioner at the following address:

DEEP.StormwaterConstruction@ct.gov with the subject line “Construction GP Termination [INSERT NAME OF PERMITTEE].”

Section 5 Conditions of this General Permit

The Permittee shall, at all times, continue to meet the requirements for authorization set forth in this general permit. In addition, the Permittee shall ensure that authorized activities are conducted in accordance with the conditions in this section and the federal Effluent Limitation Guidelines 40 CFR§450—Construction and Development Point Source Category.

In the absence of information demonstrating otherwise, DEEP expects that compliance with the conditions in this permit will result in stormwater discharges being controlled as necessary to meet applicable water quality standards. If at any time the Permittee becomes aware, or DEEP determines, that discharges are not being controlled as necessary to meet applicable water quality standards, the Permittee must take corrective actions and document those actions. If during coverage under a previous permit, the Permittee was required to install and maintain stormwater controls specifically to meet the assumptions and requirements of an EPA-approved or established TMDL (for any parameter) or to otherwise control discharges to meet water quality standards, the Permittee must continue to implement such controls as part of their coverage under this permit. Failure to implement necessary corrective actions is considered a violation of this permit.

5.1 General Conditions

5.1.1 Structures and Dredging in Coastal and Tidal Areas

Any person or municipality who discharges stormwater into coastal tidal waters for which a permit is required under Section 22a-361 of the Conn. Gen. Stat. (structures and dredging) or Section 22a-32 of the Conn. Gen. Stat. (Tidal Wetlands Act), shall obtain such permit(s) from the Commissioner. A tidal wetland permit is required for any regulated activity conducted within a tidal wetland, including, but not limited to, the placement of any sediment upon a tidal wetland, whether it is deposited directly or indirectly.

5.1.2 Discharges to Tidal Wetlands

Any site which has a post-construction stormwater discharge to a tidal wetland (that is not a fresh-tidal wetland) where such discharge is within 500 feet of the tidal wetland, shall discharge such stormwater through a system designed to retain and infiltrate the Water Quality Volume (“WQV”), as defined in Section 10, on the site. If there are site constraints that would prevent retention of this volume on-site (e.g., brownfields, capped landfills, bedrock, elevated groundwater, etc.), documentation must be submitted, for the Commissioner’s review and written approval, explaining the site limitations and offering an alternative retention volume for consideration. In such cases, the portion of the WQV that cannot be retained must be provided with additional stormwater treatment to protect water quality. Any such treatment shall be designed, installed and maintained in accordance with the Stormwater Quality Manual.

For sites unable to comply with this section, the Commissioner, at the Commissioner’s sole discretion, may require the submission of an individual permit in lieu of authorization under this general permit.

5.1.3 Quality of Discharge

The discharge shall not contain visible floating scum, oil, trash, or other matter contained in the stormwater discharge.

5.1.4 Toxicity to Aquatic and Marine Life/Risk to Human Health

The discharge shall not result in pollution which may cause or contribute to acute or chronic toxicity to aquatic life, impair the biological integrity of aquatic or marine ecosystems, result in unacceptable bioaccumulation, risk to human health, or ecological communities.

5.1.5 Water Quality Standards

The stormwater discharge shall not cause or contribute to an exceedance of the applicable Water Quality Standards or Criteria in the receiving water.

5.1.6 Inspections and Certifications

The following initial inspections and certifications shall apply to all projects:

5.1.6.1 Pre-Construction Meeting

Prior to commencement of any construction activity, the Permittee shall conduct a pre-construction meeting with the Qualified Professional who designed the project, the Qualified Inspector who will be conducting inspections, and all site contractors and subcontractors to be involved in construction activity. Such meeting shall convey the design, stormwater Control Measures, erosion and sediment controls, plan implementation and routine site inspections, and contract requirements for the project prior to earth disturbance. Such a meeting shall also include a site walk of the project site.

- a. For Solar Arrays subject to Appendix I and any other project that may be reviewed and/or inspected by a representative of the District, the pre-construction meeting and site walk shall also include the appropriate District personnel.
- b. For State of CT Agencies, the CTDOT District Engineer, District Environmental Coordinator, or the designated employee of another state agency shall conduct the pre-construction inspection

The Permittee shall develop and retain in the SPCP a pre-construction meeting report. The report shall, at a minimum, include the date, time, names and titles of attendees, company names, phone and email addresses for each attendee and their signature confirming the Permittee held a pre-construction meeting and that they understand the design, stormwater Control Measures erosion and sediment controls, plan implementation, routine site inspections and contract requirements for the project.

5.1.6.2 Contractor Certifications

The Permittee shall obtain signed certifications for all contractors and subcontractors that will perform construction activities on the site and that have the potential to cause pollution of the waters of the State. Such signed certifications shall be retained in the SPCP. Contractors and subcontractors shall certify the following:

“I certify under penalty of the law that I have read and understand the terms and conditions of the General Permit for the Discharge of Stormwater from Construction Activities and the site-specific Stormwater Pollution Control Plan (“SPCP”). I understand that as a contractor or subcontractor at the site, I must comply with the terms and conditions of this general permit and the SPCP.”

5.1.6.3 Construction Inspections

All construction site inspections shall be conducted in accordance with Section 5.2.4 of this general permit.

5.1.7 Post Notice of Construction Activities

Upon commencement of construction activities, the Permittee shall post a sign of permit coverage at a safe, publicly accessible location in close proximity to the construction site. The sign must be at least two (2) feet by three (3) feet in dimension, weatherproof, and in English and Spanish, located so it is visible and legible from the public road nearest to the active part of the construction. The notice shall include:

- the name of the Permittee.
- the DEEP permit number.
- the site address.
- a contact name.

- contact email and phone number.
- the estimated start date and completion date.
- the Permittee-hosted website or email where the SPCP and application are available or can be obtained.
- the following statement: “If you observe indicators of stormwater pollutants in the discharge from this site or in the receiving water, please contact the CT DEEP through the link for Reporting Water Pollution at: www.ct.gov/deep/stormwater”.

For linear projects, such as roadways or utility rights-of-way, the Permittee shall post a sign at roadway crossings, public access points, and other areas where the public may reasonably view the notice.

The notice must be maintained on-site from the time construction activities begin until a Notice of Termination is approved.

5.2 Stormwater Pollution Control Plan

All Permittees shall develop and maintain on-site a Stormwater Pollution Control Plan (“SPCP”) for the discharge of stormwater for the construction activity authorized by this general permit. Once the construction activity begins, the Permittee shall perform all actions required by such SPCP and shall maintain compliance with the SPCP at all times. The Permittee shall ensure that the design and implementation of the SPCP minimizes: (1) soil erosion and sedimentation during and after construction; and (2) stormwater pollution from the site after construction is completed.

5.2.1 Development and Required Elements of the Plan

5.2.1.1 The SPCP shall consist of site plan drawings, selected Best Management Practices (“BMPs”), Control Measures and a narrative described in this section. The SPCP shall be prepared in accordance with sound engineering practices, and shall be consistent with the Guidelines, the Stormwater Quality Manual (available at <http://www.ct.gov/deep/stormwater>) and any applicable requirements of this general permit. The SPCP shall also be consistent with any remedial action plan, closure plan or other plan required by any other DEEP permit.

5.2.1.2 The SPCP shall, at a minimum, take into account and include the following items:

a. Account for the following factors in designing stormwater controls:

- The expected amount, frequency, intensity, and duration of precipitation.
- The nature of stormwater runoff (i.e., flow) and run-on at the site, including factors such as expected flow from impervious surfaces, slopes, and site drainage features.
- The proximity to wetlands, vernal pools, and surface waters.
- The Permittee must design stormwater controls to control stormwater volume, velocity, and peak flow rates to minimize discharges of pollutants in stormwater and to minimize channel and streambank erosion and scour in the immediate vicinity of discharge points.
- The soil type and range of soil particle sizes that are expected to be present on the site.

b. Project Description and Construction Sequencing

The SPCP shall provide a detailed description of the entire project, including the expected phasing or sequence of all construction activities on the site, names of corresponding erosion and sediment Control Measures for each phase of the project, and an estimated timeline for all construction activities. The timeline must be revised as necessary to keep the SPCP current. Wherever practicable, site construction activities shall be phased to avoid the disturbance of over five (5) acres at one time (or a lesser area of disturbance as required in Section 5.2.3 of the general permit regarding “Impaired Waters”). In addition, perimeter Control Measures and permanent

stormwater Control Measures, including, but not limited to, stormwater basins should be constructed in the early phases of the construction sequence prior to large-scale site disturbance. The SPCP shall clearly show the estimated limits of total disturbance for the construction activity and for each phase.

The SPCP shall provide a detailed description of how each phase of construction will be conducted, including, but not limited to:

- commencement of construction activities in each portion of the site, including clearing and grubbing, mass grading, demolition activities, site preparation (i.e., excavating, cutting and filling), final grading, and creation of soil and vegetation stockpiles requiring stabilization.
- temporary or permanent cessation of construction activities in each portion of the site.
- temporary or final stabilization of exposed areas for each portion of the site.
- removal of temporary stormwater controls and construction equipment or vehicles.
- the cessation of construction-related pollutant-generating activities.

c. Site Description, including, but not limited to:

- a narrative description of the nature of the construction activity.
- an estimate of the total area of the site and the total area of the site that is expected to be disturbed by construction activities.
- an estimate of the average runoff coefficient of the site after construction activities are completed.
- the name of the immediate receiving water(s) and the ultimate receiving water(s) of the discharges authorized by this general permit.
- extent of the wetland acreage on the site.

d. Site plan drawings indicating:

- drainage patterns and approximate slopes anticipated after major grading activities.
- areas of soil disturbance.
- the location of major structural and non-structural controls as specified in Subsection 5.2.2.
- the location of areas where stabilization practices are expected to occur.
- areas of existing vegetation.
- areas which will be vegetated following construction.
- the locations of test pits and infiltration tests for stormwater Control Measures.
- surface waters, impaired waters (identifying those with and without a TMDL), high quality waters, inland wetlands, tidal wetlands, fresh-tidal wetlands.
- discharge locations and serial numbers where stormwater will be discharged to surface water (both during and post-construction).
- other surface or subsurface conditions that may affect design considerations regarding potential environmental impact.

e. Pollutants of Concern

The SPCP shall include a list and description of all pollutant-generating activities on the site, include an inventory of pollutants or pollutant constituents (e.g., sediment, fertilizers, pesticides, paints, caulks, sealants, fluorescent light ballasts, contaminated substrates, solvents, fuels)

associated with that activity, which could be discharged in stormwater from the construction site. The Permittee shall address the need for proper containment and/or storage of such potential pollutants to minimize the potential for the discharge of such pollutants from the site. The Permittee must consider where potential spills and leaks could occur that contribute pollutants to stormwater discharges, and any known hazardous or toxic substances, such as PCBs and asbestos, that will be disturbed or removed during construction.

f. Control Measures

The SPCP shall include detailed descriptions of all the Control Measures that will be implemented at the site, both in a separate narrative and on the site plan drawings, to prevent and minimize the discharge of pollutants to the BAT. Control Measures shall be implemented in accordance with Section 5.2.2 of the general permit. In addition, the following information shall be provided in the narrative for each Control Measure:

- calculations supporting the design of sediment and floatables removal controls pursuant to Section 5.2.2.10.b of the general permit.
- calculations supporting the design of velocity dissipation controls pursuant to Section 5.2.2.10.c of the general permit.

g. Runoff Reduction and Low Impact Development (LID) Information

Where runoff reduction practices and/or LID measures are utilized, the following information shall be included in the site plan and narrative description:

- the location of the site's existing streams, floodplains, wetlands, riparian buffers, slopes 3:1 and steeper, and the vegetation identified for preservation and non-disturbance during construction such as forested areas, hay fields, and other old agricultural fields.
- natural drainage patterns, swales, and other drainage ways, that are not streams, floodplains, or wetlands.
- the location of all areas with soils suitable for infiltration and areas of the site best suited for infiltration for the siting of runoff reduction practices and LID design measures.
- the location of all areas unsuitable or least suitable for infiltration for the siting of areas of development/building.
- the location of all test pits and infiltration tests in accordance with the Stormwater Quality Manual.
- the location of all post-construction stormwater management measures, runoff reduction practices, and LID design measures developed pursuant to Subsection 5.2.2.10 of the general permit.
- identification of areas inappropriate for the infiltration of stormwater runoff from land uses with a significant potential for groundwater pollution (e.g. brownfields sites).
- a description of the nature, purpose, implementation, and long-term maintenance of the post-construction stormwater management measures, runoff reduction practices, and LID design measures. Identify who will be responsible for the management of the post-construction stormwater Control Measures and the timeline for such management.
- calculations, for Control Measures developed pursuant to Section 5.2.2.9 of the general permit, illustrating the retention of the Water Quality Volume or half the Water Quality Volume for the site, as applicable, including a discussion of the impact of any runoff reduction and/or LID practices on these calculations.
- a narrative description for all site constraints that may prevent retention of the required Water Quality Volume specified in Section 5.2.2.9 of the general permit including: site limitations;

a description of the runoff reduction practices implemented; a demonstration and explanation that the amount retained is the Best Available Technology; an alternative retention volume; and a description of the measures used to provide additional stormwater treatment for sediment, floatables, bacteria, nutrients and metals above the alternate volume up to the Water Quality Volume.

- calculations showing the proposed effective impervious cover for the site and, where required or proposed for linear projects pursuant to Section 5.2.2.9.b of the general permit, each outfall drainage area.

h. Site Inspections

All inspections shall comply with the requirements and conditions of Section 5.2.4 of the general permit.

i. Plan Implementation Inspections

The SPCP shall include the following information for all completed inspections:

- Plan Implementation Inspection Checklist.
- a schedule for conducting inspections.
- name, credentials, and responsibilities for each inspector.
- name, credentials, and responsibilities of the designing Qualified Professional (and District personnel, as appropriate) conducting such inspections, and required procedures pursuant to Section 5.2.4 of the general permit.
- inspection findings.
- corrective actions required.
- signature of the inspector.
- for additional inspection requirements for Solar Arrays Projects see Appendix I.

ii. Routine Inspections

The SPCP shall include the following information for all complete inspections:

- a routine inspection checklist.
- schedule for conducting inspections.
- identification and qualifications of the Qualified Inspector(s) conducting the routine inspections and their responsibilities and procedures pursuant to Subsection 5.2.4.2 of the general permit.
- inspection findings.
- corrective actions required.
- signature of the Qualified Inspector.
- For additional inspection requirements for Solar Arrays Projects see Appendix I.

i. Contractors

- i. The SPCP shall clearly identify each contractor and subcontractor that will perform construction activities on the site that have the potential to cause pollution of the waters of the State. The SPCP shall retain a signed and dated copy of each certification statement in accordance with Section 5.1.6.2 of the general permit.

ii. Subdivisions

Where individual lots in a subdivision or other common plan of development are conveyed or otherwise the responsibility of another person or municipality, the Permittee is responsible to ensure that those individual lot contractors comply with the provisions of this general permit and the Stormwater Pollution Control Plan, regardless of the lot size or disturbed area. In such cases, the Permittee shall provide a copy of the SPCP to each individual lot contractor, obtain their signed certification, and retain the documentation in the SPCP.

j. Impaired Waters

For construction activities that discharge to impaired waters, as specified in Section 2.2.9, the SPCP shall include a description of the provisions for controlling the preconstruction, active construction, and post-construction stormwater discharges to these waters pursuant to Section 5.2.3 below.

5.2.2 Stormwater Control Measures

Control Measures are required Best Management Practices (“BMPs”) that the Permittee must implement to prevent or minimize, as defined in this permit, the discharge of pollutants from the permitted activity. The Permittee shall comply with all of the BMPs in this section.

Control Measures shall be designed in accordance with the Guidelines, the Stormwater Quality Manual or the CTDOT Qualified Products List ([CTDOT QPL](#)). Use of Control Measures to comply with Section 5.2.2.1 of this general permit (“Erosion and Sediment Controls”), that are not included in such references must be approved by the Commissioner. The narrative and drawings of controls shall address the following minimum components:

5.2.2.1 Erosion and Sediment Controls

a. Soil Stabilization and Protection

The SPCP shall include a narrative description and drawings of interim and permanent soil stabilization practices for managing disturbed areas and soil stockpiles, including a schedule for implementing the practices. The Permittee shall ensure that existing vegetation is preserved to the BAT and disturbed portions of the site are minimized and stabilized throughout the duration of the construction activity at the site.

b. Erosion Control Barriers

In addition to requirements for erosion control barriers prescribed in the Guidelines, the Permittee shall ensure that two (2) rows of erosion control barriers are installed and maintained on sites with slopes equal to or greater than eight percent (8%) within the contributing drainage area to such barrier.

Notwithstanding the foregoing, use of two (2) rows of erosion control barriers shall not be required on the sites specified in this paragraph when:

- i. The Commissioner determines, for a limited section or portion of such erosion control barriers, that it is necessary to accommodate animal crossing or animal movement.
- ii. The Commissioner approves a SPCP that includes an erosion control system whose performance is equivalent to, or exceeds, two rows of erosion control barriers.
- iii. For linear projects, the Commissioner has determined that two rows of erosion control barriers, when compared to one row, will cause greater adverse impact to wetlands, waters, or other sensitive resources.

In such a situation the Commissioner may approve of a SPCP with one row of erosion control barriers or an alternative erosion control system. When implementing this paragraph, the Commissioner may consider the contributing disturbed area, drainage area, length of the slope,

flow conditions to maintain sheet flow, the efficacy of the proposed barrier, any adverse impacts and any other reasonable factor as determined by the Commissioner.

5.2.2.2 Soil Stabilization Timeline

Where construction activities have permanently ceased or when final grades are reached in any portion of the site, stabilization and protection practices as specified in the Guidelines or as approved by the Commissioner shall be initiated immediately and completed within seven (7) days. Notwithstanding any provisions of the Guidelines, areas that will remain disturbed but inactive for at least fourteen (14) calendar days shall receive temporary seeding or soil protection within seven (7) days in accordance with the Guidelines unless site conditions warrant shorter time periods for these provisions.

Areas that will remain disturbed beyond the seeding season as identified in the Guidelines, shall receive long-term, non-vegetative stabilization and protection sufficient to protect the site through the winter and spring when vegetative stabilization can resume. In all cases, stabilization and protection measures shall be implemented as soon as possible in accordance with the Guidelines or as approved by the Commissioner. In drought-stricken areas, alternative stabilization measures must be employed, as necessary, in accordance with the Guidelines.

5.2.2.3 Maintenance of Vegetation

To prevent erosion and soil compaction during construction activities, temporary or permanent vegetation or other ground cover shall be maintained at all times in all areas of the site, except those undergoing active disturbance. All new temporary and permanent vegetation shall consist of native plant species. With respect to such vegetation, the Permittee shall not use chemical fertilization, herbicides, or pesticides except as necessary to establish such vegetation in accordance with the manufactures label. The application of chemical pesticides and herbicides shall fully comply with all applicable laws and regulations. The Commissioner encourages the use of pollinator-friendly plant species and integrated pest management practices.

5.2.2.4 Slope Benches

A reverse slope bench is required for any slope steeper than 3:1 (horizontal: vertical) that exceeds 15 feet vertically, except when engineered slope stabilization structures or measures are included or a detailed soil mechanics analysis has been conducted to verify stability. Engineered analyses and measures must be designed by a Qualified Professional engineer with experience in geotechnical engineering or soil mechanics. The qualifications, engineered analysis, and measures shall be included in the SPCP.

5.2.2.5 Wetland Protection

The Commissioner encourages the use of a one hundred (100) foot buffer from any wetland or watercourse. Where site disturbance occurs within fifty (50) feet upgradient of a wetland or waters a double row of sediment barriers (e.g. hay bales, silt fence, wattles, etc.) shall be installed in accordance with the Guidelines between the disturbed area and any such downgradient wetland or waters.

5.2.2.6 Structural Measures

The SPCP shall include a narrative description and drawings of structural measures to divert flows away from exposed soils, store flows or otherwise limit runoff and minimize the discharge of pollutants from the site. Unless otherwise specifically approved in writing by the Commissioner, or if otherwise authorized by another State of Connecticut or federal permit, structural measures shall be installed on upland soil.

For points of discharge from disturbed sites with a total contributing drainage area of between two (2) to five (5) acres, a temporary sediment trap or temporary sediment basin shall be designed and installed in accordance with the Guidelines. For points of discharge from disturbed sites with a total contributing

drainage area greater than five (5) acres, a temporary sediment basin shall be designed and installed in accordance with the Guidelines. Such trap(s) or basin(s) shall utilize outlet structures that withdraw water from the surface (surface outlet), if feasible, and must be maintained until final stabilization of the contributing area.

The requirement for sediment traps or basins shall not apply to flows from off-site areas and flows from areas of the site that are either undisturbed or have undergone final stabilization, provided such flows are diverted around the temporary sediment trap or basin and are approved in writing by the Commissioner.

5.2.2.7 Maintenance

The SPCP shall include a narrative of the procedures to maintain, in good and effective operating condition, all erosion and sediment BMPs and Control Measures, including vegetation, and all other protective measures identified in the SPCP. Maintenance of all erosion and sediment controls shall be performed in accordance with the Guidelines, or more frequently as necessary.

5.2.2.8 Dewatering

- a. Dewatering shall be managed in accordance with the Guidelines. Stormwater discharged to surface waters shall be discharged in a manner that minimizes the discoloration of the receiving waters. The SPCP shall include a narrative description and identify in the drawings the operational and structural measures that will be used to ensure that dewatering waters will not cause scouring or erosion or contain suspended solids in amounts that could reasonably be expected to cause pollution of surface waters of the State or cause or contribute to instream water quality violations. Unless otherwise specifically approved in writing by the Commissioner, or if otherwise authorized by another state or federal permit, dewatering measures shall be installed on upland soil. If turbidity or discoloration or other pollutants are observed in the discharge from dewatering Control Measures, additional or alternate Control Measures or other corrective actions must be implemented in accordance with Section 5.2.4.2.c.i and the Guidelines. The Permittee shall document any corrective actions taken in their SPCP.

No discharge of stormwater shall contain or cause a visible oil sheen, turbidity, floating solids, debris, trash, or foaming in the receiving water.

- b. Turbidity Monitoring

For construction activities with dewatering operations, the Permittee shall carry out initial and weekly monitoring for turbidity from each dewatering discharge point for the duration of dewatering operations. Samples shall be taken after the dewatering water has been treated by any treatment device or control measure. The Permittee shall measure turbidity in accordance with 40 CFR 136. The Permittee shall take the first turbidity measurement within 30 minutes of initiating the dewatering discharge. Following this initial monitoring, the Permittee shall conduct weekly monitoring during the Routine Inspection pursuant to Section 5.2.4.2. A record of the turbidity monitoring results shall be kept on-site with the SPCP and submitted to the Commissioner pursuant to Section 5.3.2.2.

- c. In the absence of information demonstrating otherwise, DEEP expects that compliance with the conditions in this permit will result in stormwater discharges being controlled as necessary to meet applicable water quality standards. If the Permittee is aware of, or becomes aware of, or has reasonable suspicion of contamination onsite from historical activities or the site may have contaminated groundwater, or if any pollutants are known or believed present in the proposed dewatering discharge water, the applicant or Permittee shall apply for coverage under the appropriate permit for authorization to discharge to surface water, ground water, or a POTW. That permit will only cover the treatment and discharge of the contaminated water and will remain active until the cessation of dewatering activities.

- d. For the purposes of this condition, a pollutant may be verified as “known present” if measured above the analytical detection limit using a sufficiently sensitive test method in an environmental sample, and “believed present” if a pollutant has not been measured in an environmental sample but will be added or generated prior to discharge, such as through a treatment process. Consequently, a pollutant may be verified as “known absent” if measured as non-detect relative to the analytical detection limit using a sufficiently sensitive test method in an environmental sample, and “believed absent” if a pollutant has not been measured in an environmental sample but will not be added or generated prior to discharge and is not a parameter that applies to the applicable activity category for a site. If any pollutants are known or believed present in the proposed dewatering discharge water, the applicant shall test one sample of the proposed dewatering discharge water for the pollutants known or believed to be present.

5.2.2.9 Post-Construction Performance Standards

The SPCP shall include a narrative description and drawings of measures that will be installed during the construction process to minimize the discharge of pollutants in stormwater discharges that will occur after construction operations have been completed. Permittees are encouraged to consider the potential need for future resiliency measures to minimize impacts from stormwater discharges from major storm events such as hurricanes, storm surge, extreme/heavy precipitation, and flooding events. Post-construction stormwater management measures shall be designed and implemented in accordance with the Stormwater Quality Manual, the CTDOT Qualified Products List, or as approved by the Commissioner. Unless otherwise specifically provided by the Commissioner in writing, or authorized by another state or federal permit, structural measures shall be placed on upland soils. The SPCP shall include provisions to address the long-term maintenance of any postconstruction stormwater management measure installed.

The Permittee shall utilize runoff reduction practices as defined in Section 10 of this general permit to meet runoff volume requirements based on the conditions below.

a. Redevelopment

For sites that are currently developed with an effective impervious cover of forty percent or more and for which the Permittee is proposing redevelopment, the Permittee shall design the site in such a manner as to retain on-site half the water quality volume (as defined in Section 10 of the general permit) for the site and provide additional stormwater treatment without retention for discharges up to the full Water Quality Volume for sediment, floatables and nutrients to BAT. In cases where the Permittee is not able to retain half the Water Quality Volume (e.g., brownfields, capped landfills, bedrock, elevated groundwater, etc.), the Permittee shall design the redevelopment to retain a runoff volume to the BAT. In such cases, additional stormwater treatment up to the full Water Quality Volume is still required. Any such treatment shall be designed, installed and maintained in accordance with the Stormwater Quality Manual. If retention of half the Water Quality Volume is not achieved, the Permittee shall submit a report for the Commissioner’s review and written approval describing: the measures taken to maximize runoff reduction practices on the site; the reasons why those practices constitute the BAT; the alternative retention volume; and a description of the measures used to provide additional stormwater treatment above the alternate volume up to the Water Quality Volume.

For sites falling under this subsection, where redevelopment only impacts a portion of a previously developed site, the retention of half the Water Quality Volume shall be calculated based on the area of the site and stormwater management system that is disturbed as part of the redevelopment.

b. Linear Redevelopment

In the case of linear redevelopment projects (e.g. roadway reconstruction or widening or public utility rights of way) for the developed portion of the right of way: (1) for projects that may be unable to comply with the retention of the appropriate portion of the Water Quality Volume

specified in subparagraphs (a) and (c) of this subsection, the alternate retention and treatment provisions may also be applied as specified in such subparagraphs, or (2) for projects that will not increase the effective impervious cover within a given watershed, the Permittee shall implement the additional stormwater treatment measures referenced in Subsections (a) and (c) of this subsection, but will not be required to retain the appropriate portion of the Water Quality Volume specified in such paragraphs.

c. Other Development

The following performance standard applies to all sites that are currently undeveloped or are currently developed with less than forty percent effective impervious cover. For these sites, the Permittee shall design the site to retain the Water Quality Volume for the site. If there are site constraints that would prevent retention of this volume on-site (e.g., brownfields, capped landfills, bedrock, elevated groundwater, etc.), documentation must be submitted, for the Commissioner's review and written approval, which: explains the site limitations; provides a description of the runoff reduction practices implemented; provides an explanation of why this constitutes the BAT; offers an alternative retention volume; and provides a description of the measures used to provide additional stormwater treatment for sediment, floatables and nutrients above the alternate volume up to the Water Quality Volume. In the case of linear projects that do not involve impervious surfaces (e.g. electrical transmission rights-of-way or natural gas pipelines), retention of the Water Quality Volume is not required as long as the post-development runoff characteristics do not differ significantly from pre-development conditions.

For redevelopment sites falling under this subsection, where redevelopment only impacts a portion of a previously developed site, the retention of the Water Quality Volume shall be calculated based on the area of the site and stormwater management system that is disturbed as part of the redevelopment.

5.2.2.10 Post-Construction Control Measures

a. Runoff Reduction and Low Impact Development ("LID") Practices

The site design shall incorporate runoff reduction practices, low impact development ("LID") practices or other post-construction Control Measures to meet the performance standards in Section 5.2.2.9 above, promote groundwater recharge and minimize post-construction impacts to water quality.

b. Suspended Solids and Floatables Removal

The Permittee shall install post-construction stormwater Control Measures designed to minimize the discharge of suspended solids and floatables (e.g. oil and grease, other floatable liquids, floatable solids, trash, etc.) from stormwater. A goal of 80 percent removal of the annual sediment load from the stormwater discharge shall be used in designing and installing such stormwater Control Measures. The SPCP shall provide calculations supporting the capability of such measures in achieving this goal and any third-party verification, as applicable, of the sediment removal efficiencies of such measures. This goal is not intended to limit local approval authorities from requiring a higher standard pursuant to local requirements.

c. Velocity Dissipation

Velocity dissipation devices shall be placed at discharge locations and along the length of any outfall channel as necessary to provide a non-erosive velocity flow to receiving waters so that the natural physical and biological characteristics and functions of such waters are maintained and protected.

5.2.2.11 Other Controls

The following additional controls shall be implemented:

a. Waste Disposal

Best management practices shall be implemented to minimize the discharge of litter, debris, building materials, hardened concrete waste, or similar materials to waters of the State. The Permittee shall ensure that waste storage containers, including, but not limited to, dumpsters or tanks, be covered and leak proof to prevent stormwater from coming into contact with solid or liquid waste. A narrative of these practices shall be provided in the SPCP. In addition, the dumping of liquid wastes in storm sewers is prohibited.

b. Washout Areas

Washout of applicators, containers, vehicles and equipment for concrete, paint and other materials shall be conducted in a designated washout area. There shall be no surface discharge of washout wastewater from this area. Such a washout shall be conducted:

- outside of any buffers.
- as far away as possible, but at least fifty (50) feet, from any stream, wetland, storm drain inlet, or other sensitive resource.
- in an area directed into a leak-proof container or leak-proof and lined pit designed so no overflows can occur due to inadequate sizing or precipitation in accordance with 40 CFR 450.21(e).

The Permittee shall clearly flag off and designate areas to be used for washing and conduct such activities only in these areas. The Permittee shall direct all wash water into a container or pit designed such that no overflows can occur during rainfall or after snowmelt. At least once per week, the Permittee shall inspect all the containers or pits used for washout to ensure structural integrity, adequate holding capacity, and to check for leaks or overflows. If there are signs of leaks, holes or overflows in the containers or pits that could lead to discharge, the Permittee shall repair them prior to further use.

For concrete washout areas, the Permittee shall remove hardened concrete waste whenever the hardened concrete has accumulated to a height of $\frac{1}{2}$ of the container or pit or as necessary to avoid overflows. The Permittee shall remove and dispose of such hardened concrete waste in accordance with the practices developed for “Waste Disposal” (see Section 5.2.2.11.a of this general permit).

A narrative of maintenance procedures and a record of maintenance and inspections shall be included in the SPCP.

c. Off-site Vehicle Tracking & Dust Suppression

- i. Off-site vehicle tracking of sediments and the generation of dust shall be minimized. A construction entrance shall be installed and maintained in accordance with the Guidelines, including appropriately configured measures for vehicle washdown.
- ii. Where sediment has been tracked-out from the site onto paved roads, sidewalks, or other paved areas outside of the site, the Permittee shall remove the deposited sediment by the end of the same business day in which the track-out occurs or by the end of the next business day if track-out occurs on a non-business day. The Permittee shall remove the track-out by sweeping, shoveling, or vacuuming these surfaces, or by using other similarly effective means of sediment removal. The Permittee is prohibited from hosing or sweeping tracked-out sediment into any constructed or natural site drainage feature, storm drain inlet or receiving water.
- iii. Wet dust suppression shall be used, in accordance with Section 22a-174-18(c) of the Regs. Conn. State Agencies, for any construction activity that causes airborne particulates. The volume of water sprayed for controlling dust shall be minimized to prevent the runoff of water. No discharge of dust control water shall contain or cause a visible oil sheen, floating

solids, visible discoloration, or foaming agents in any receiving waters. Additionally, water used in dust suppression shall not contain contaminants that could violate water quality standards.

d. Cleaning

All post-construction stormwater structures shall be cleaned of construction sediment and any remaining silt fence shall be removed upon stabilization of the site.

e. Storage of Chemicals, Petroleum Products, and Other Potential Pollutant Sources

All chemical and petroleum product containers stored on the site (excluding those contained within vehicles and equipment) shall be stored within an impermeable containment system that is free of gaps and cracks, can contain any leaks or spills and accumulated precipitation until the collected materials are detected and removed, and which can hold at least 110% of the volume of the largest container, or 10% of the total volume of all containers in the area, whichever is larger, without overflow from the containment system. In addition, all chemicals and petroleum products shall be stored under a roofed area except for those chemicals stored in containers of 100-gallon capacity or more, in which case a roof is not required. Double-walled tanks satisfy the requirements of this paragraph for containment and roofing.

Covered storage shall be provided for all non-liquid potential pollutant sources such as fertilizers, pesticides, caulks, sealants, fluorescent light ballasts, contaminated substrates, solvents, and other potential pollutant sources stored on-site. For liquid pollutants, including, but not limited to, paints and solvents, containment shall be considered adequate if it meets the requirements for chemical and petroleum storage in the previous paragraph.

f. Emergency Spill Response

Spills of oil, grease, or other harmful chemicals must immediately be cleaned by the removal of and containment of contaminated soil or emergency spill kit. An emergency spill kit, or alternative proprietary device, must be present and accessible on site for emergency removal of oil, grease, or chemical spills. For reportable spills per Regs. Conn. State Agencies 22a-430-3 subsection (p), the Permittee shall call the DEEP Emergency Response Unit at (860)424-3338.

g. Cold Water Stream Habitat

For construction activities within one hundred (100) feet of any stream, river, or tributary that is included within a Cold Water Stream Habitat, as may be authorized by the Commissioner pursuant to Section 2.2.10 of this general permit, any mitigation strategies authorized by the Commissioner must be verified post-construction by the designing qualified professional.

5.2.3 Additional Conditions for Impaired Waters

For construction activities that discharge directly to impaired waters for sediment or sediment-related impairments, as specified in “Discharges to Impaired Waters” in Section 2.2.9.2 of this general permit, the SPCP shall include the following provisions:

- Where an applicable TMDL sets specific load allocations or requirements for discharges authorized by this permit, discharges shall be consistent with any specific load allocations or requirements established by the applicable TMDL.
- Where an applicable TMDL has been established, but no specific requirements have been identified, compliance with this permit will be assumed to be consistent with the approved TMDL.
- The SPCP shall document that Control Measures are in place to ensure there will be no discharge to the waterbody that may impact or exceed the allocations.

5.2.4 Inspections

All construction activities authorized by this general permit shall be inspected initially for SPCP implementation as describe in Section 5.1.6, and then routinely pursuant to Section 5.2.4.2. Upon project completion and prior to submission of a Notice of Termination, post-construction, final stabilization, and Termination Inspections shall also be conducted. For Solar Array inspections, see additional requirements in Appendix I.

5.2.4.1 Plan Implementation Inspections

Prior to commencement of each phase of the construction activity on the site, the Permittee shall contact the designing Qualified Professional and, for Locally Exempt projects including, but not limited to, Solar Arrays subject to Appendix I, the appropriate District, to ensure that all required inspections are conducted. For each phase of construction, the site shall be inspected at least once within the first thirty (30) days of construction activity and at least three times, with seven (7) or more days between inspections, within the first ninety (90) days of construction activity to confirm compliance with the general permit and proper initial implementation of all Control Measures designated in the SPCP for each phase of construction. The following conditions shall apply:

- a. For all projects not conducted by a state agency and which disturb more than one (1) acre, the inspector shall be someone who:
 - i. Is not an employee, as defined by the Internal Revenue Service in the Internal Revenue Code of 1986, of the applicant, and
 - ii. Has no ownership interest of any kind in the project for which the application is being submitted.
- b. For projects conducted by a state agency and which disturb more than one (1) acre, the inspector shall be someone who:
 - i. Meets the requirements in subparagraph (a), above, or
 - ii. Is included in the list of Qualified Professionals specified in Section 2.2.17.1 of the general permit.

5.2.4.2 Routine Inspections

The Permittee shall routinely inspect the site for compliance with the general permit, including, but not limited to, compliance with the SPCP for the site, until a Notice of Termination under Section 4 of the general permit has been submitted to the Commissioner. Inspection procedures for these routine inspections shall comply with the following:

- a. The Permittee shall maintain a rain gauge on-site to document rainfall amounts. At least once a week and within 24 hours of the end of a storm that generates a discharge, a Qualified Inspector (provided by the Permittee), shall inspect, at a minimum, the following: disturbed areas of the construction activity that have not been finally stabilized; site discharge outfalls; dewatering discharges; all erosion and sediment Control Measures; all structural Control Measures; all soil stockpile areas; all washout areas, and locations where vehicles enter or exit the site. If at all possible, the inspection shall be conducted during an active rain event. For storms that end on a weekend, holiday or other time after which normal working hours will not commence within 24 hours, a routine inspection is required within 24 hours only for storms that equal or exceed 0.5 inches. For storms of less than 0.5 inches, an inspection shall occur immediately upon the start of the subsequent normal working hours.

In areas of the site where temporary stabilization has been implemented, a routine inspection shall be conducted at least weekly until final stabilization has been achieved. Once all post-construction stormwater measures have been installed in accordance with the Post-Construction Stormwater Management and cleaned of any construction sediment or debris, a Post-Construction Inspection shall be conducted. For sites that have achieved final stabilization pursuant to Section 5.2.4.4, routine inspections shall then be conducted at least monthly.

- b. During each routine inspection the Qualified Inspector(s) shall, among other things, evaluate the effectiveness of erosion and sediment controls, structural controls, stabilization practices, and any other controls implemented to prevent pollution and determine if it is necessary to install, maintain, or repair such controls and/or practices to improve the quality of stormwater discharge(s). In addition, during each routine inspection, the site, including but not limited to, all of the areas noted in the preceding paragraph, shall be inspected for evidence of, or the potential for, the discharge of pollutants (such as sediment, discoloration, floatables, sheen, etc.) to waters or entering the drainage system, and impacts to the receiving waters. Turbidity monitoring pursuant to Section 5.2.2.8.b may also be conducted during these inspections. Locations where vehicles enter or exit the site shall also be inspected for evidence of off-site sediment tracking.
- c. The Qualified Inspector conducting routine inspections shall prepare a report on each inspection. Each such report shall be retained in the SPCP. This report shall summarize: the scope of the inspection; name(s) and qualifications of personnel conducting the inspection; the date(s) of the inspection; weather conditions including precipitation information; major observations relating to erosion and sediment controls and the implementation of the SPCP; a description of the stormwater discharge(s) from the site, including any evidence of pollutant discharge; and any water quality monitoring performed during the inspection.

The report shall be signed by the Permittee or his/her authorized representative in accordance with the Certification of Documents this general permit. The report shall include a statement that, in the judgment of the Qualified Inspector(s) conducting the site inspection, the site is either in compliance or out of compliance with the terms and conditions of the SPCP and permit. If the site inspection indicates that the site is out of compliance, the Permittee shall implement corrective actions pursuant to subsection i, below.

- i. Corrective Actions

If the site inspection indicates that the site is out of compliance, the inspection report shall include a summary of the corrective actions required to bring the site back into compliance. Non-engineered corrective actions (as identified in the Guidelines) shall be implemented on site within 24 hours and incorporated into a revised SPCP within three (3) calendar days of the date of inspection unless another schedule is specified in the Guidelines. Engineered corrective actions (as identified in the Guidelines) shall be implemented on site within seven (7) calendar days and incorporated into a revised SPCP within ten (10) calendar days of the date of inspection, unless another schedule is specified in the Guidelines or is approved by the Commissioner. During the period in which any corrective actions are being developed and have not yet been fully implemented, interim measures shall be implemented to minimize the potential for the discharge of pollutants from the site. If the Permittee must repeatedly (i.e., three (3) or more times) make the same routine maintenance fixes to the same control at the same location, even if the fix can be completed within the time periods prescribed above, the designing Qualified Professional shall investigate and develop a revised control measure to remedy the failure. A record of all corrective actions shall be maintained in the SPCP.

- d. For solar projects under Appendix I, or other projects at the Commissioner's request, a copy of each inspection report shall be submitted electronically to the Department at: DEEP.StormwaterConstruction@ct.gov
- e. Inspectors from DEEP and the appropriate District, where applicable, may inspect the site to verify compliance with this general permit at any time construction activities are ongoing, and upon completion of construction activities, until a Notice of Termination has been accepted by the Commissioner pursuant to Section 4 of the general permit.

5.2.4.3 Post-Construction Inspection

- a. For Locally Approvable projects, once all post-construction stormwater measures have been installed in accordance with Section 5.2.2.10 of the general permit, Post-Construction Stormwater

Management, and cleaned of any construction sediment or debris, the Permittee shall ensure that the appropriate Conservation District or a Qualified Professional, as appropriate, inspects the site to confirm site stabilization and compliance with the post-construction stormwater management requirements. The Permittee shall ensure that the person inspecting the site pursuant to this paragraph is not an employee, as defined by the Internal Revenue Service in the Internal Revenue Code of 1986, of the Permittee and that such person has no ownership interest of any kind in the project for which the site's application was submitted. A report shall be prepared and certified in accordance with Sections 4.2.2, 5.1.6, and 5.2.1.2.h of the general permit to indicate compliance with this requirement on the Notice of Termination form.

- b. For Locally Exempt Projects except those conducted by state agencies, once all post-construction stormwater measures have been installed in accordance with the Section 5.2.2.10 of the general permit, "Post-Construction Control Measures" and cleaned of any construction sediment or debris, the Permittee shall ensure that a qualified soil erosion and sediment control professional or a Qualified Professional Engineer inspects the site to confirm site stabilization and compliance with the post-construction stormwater management requirements of the general permit. A report shall be prepared and certified in accordance with Sections 4.2.2, 5.1.6, and 5.2.1.2.h of the general permit to indicate compliance with this requirement on the Notice of Termination form.
- c. For projects conducted by state agencies, once all post-construction stormwater measures have been installed in accordance with the Post-Construction Stormwater Management in Subsection 5.2.2.10 and cleaned of any construction sediment or debris, the CTDOT District Engineer or his/her designee and/or CTDOT District Environmental Coordinator, or the designated employee of another state agency, will inspect the site to confirm site stabilization and compliance with the post-construction stormwater management requirements of the general permit.

5.2.4.4 Final Stabilization Inspection

For all projects, once the site has achieved final stabilization, as defined in Section 10, the Permittee shall have the site inspected by a Qualified Professional Engineer (and, for Solar Array Projects subject to Appendix I, the appropriate District). This inspection shall confirm that all temporary erosion and sedimentation measures (silt fence, haybales, etc.) have been removed, all areas of the site are fully stabilized and vegetated, and that all post-construction stormwater management measures are implemented and functioning as designed. The inspection report shall include ground and/or aerial photographs to document final stabilization. All photographs must be clear and in focus, and in the original format and resolution; and include the date each photograph was taken, and a brief description of the area of the site captured by the photograph (e.g., photo shows full establishment of vegetation on northeast corner of site).

5.2.4.5 Termination Inspection

For all projects, except Solar Array Projects conducted pursuant to Appendix I, once the site has maintained final stabilization for at least one (1) year following the Final Stabilization Inspection, the Permittee shall have the site inspected by a Qualified Inspector to confirm such stabilization has been maintained. The inspection report shall include ground or aerial photographs to document final stabilization. All photographs must be clear and in focus, and in the original format and resolution; and include the date each photograph was taken, and a brief description of the area of the site captured by the photograph (e.g., photo shows application of seed and erosion control mats to remaining exposed surfaces on northeast corner of site). The Permittee shall submit the Termination Inspection report with the Notice of Termination form.

- a. No Termination Inspection is required for permits terminated by a Change of Permittee pursuant to Section 3.7 or for Site Preparation Phases authorized under a state or federal agency design-build project.

5.2.5 Keeping Pollution Control Plan Current

The Permittee is responsible for keeping the SPCP in compliance with this general permit at all times. This may involve any or all of the following:

5.2.5.1 The Permittee shall amend the SPCP if the actions required by the SPCP fail to prevent pollution or unauthorized discharges to the waters of the State or fail to comply with any other provision of this general permit. The SPCP shall also be amended whenever there is an addition of or change in contractors or subcontractors at the site, the designing Qualified Professional, District personnel, or a change in design, construction, operation, or maintenance at the site which has not otherwise been addressed in the SPCP. The Permittee shall comply with Section 3.5 if submission of a Notice of Change is required pursuant to that section.

5.2.5.2 The Commissioner may notify the Permittee at any time that the SPCP or the site does not meet one or more requirements of this general permit. Within seven (7) days of such notice, or such other time as the Commissioner may allow, the Permittee shall make the required changes to the SPCP and perform all actions required by such revised SPCP. Within fifteen (15) days of such notice, or such other time as the Commissioner may allow, the Permittee shall submit to the Commissioner a written certification that the requested changes have been made and implemented and such other information as the Commissioner requires. Any such certification or information shall be submitted in accordance with the ‘Duty to Provide Information’ and ‘Certification,’ Sections 8.9 and 8.21.4 of this general permit.

5.2.5.3 The Permittee shall ensure qualified persons maintain this SPCP at all times.

5.2.5.4 The Permittee shall retain as part of the SPCP all modifications, and any documentation associated with each modification, made under this section.

5.2.5.5 Failure to Prepare, Maintain or Update Plan

In no event shall failure to complete, maintain or update a SPCP, in accordance with the ‘Development and Required Elements of the Plan’ in Subsections 5.2.1 and 5.2.5 of this general permit, excuse non-compliance or relieve a Permittee of responsibility to implement any actions required to protect the waters of the State or comply with the requirements of this permit.

5.2.5.6 Plan Signature

The SPCP shall be signed and certified as follows:

- a. The SPCP shall be signed by the Permittee in accordance with Section 8.21.4 of this general permit.
- b. The SPCP shall include certification by all contractors and subcontractors in accordance with Section 5.2.1.2.i of this general permit.
- c. The SPCP shall include a copy of the certification by a professional engineer or landscape architect made in accordance with Section 2.2.14 of this general permit.

5.2.5.7 Plan Review Certification

For a Locally Approvable project pursuant to Section 3.3.2 of this general permit, a copy of the SPCP Review Certification made in accordance with Section 2.2.15 or 2.2.16 of this general permit, as applicable, shall be maintained with the SPCP. (Note: Construction activities reviewed and certified pursuant to those Sections are still subject to the local erosion and sediment control and stormwater management regulations of the municipality in which the activity is conducted.)

5.3 Reporting and Record Keeping Requirements

5.3.1 Record Keeping

- 5.3.1.1 For a period of at least five (5) years from the date the Notice of Termination is accepted by the Commissioner, the Permittee shall retain copies of the SPCP and all reports required by this general permit, and records of all data used to complete the application for this general permit, unless the Commissioner specifies another time period in writing.
- 5.3.1.2 The Permittee shall retain an updated copy of the SPCP required by this general permit at the construction site from the date construction is initiated at the site until the date construction at the site is completed and the site is fully stabilized.
- 5.3.1.3 Inspection records must be retained as part of the SPCP for a period of five (5) years after the date of inspection. In addition, the following inspection reports shall be kept on-site with the SPCP and shall be submitted to the Commissioner upon request:
- a. Plan Implementation Inspections conducted in accordance with Section 5.1.6.3 and recorded on checklist forms prepared pursuant to Section 5.2.1.2.h.i.
 - b. Routine Inspections conducted in accordance with Section 5.2.4.2 and recorded on checklist forms prepared pursuant to Section 5.2.1.2.h.ii.
- 5.3.1.4 Plan Modification
- SPCP modifications made pursuant to Section 5.2.5.4 of this general permit and any documentation associated with such modification shall be kept on-site with the SPCP.

5.3.2 Reporting

- 5.3.2.1 All reports requested by the Commissioner, except turbidity monitoring reports pursuant to Section 5.2.2.8.b, shall be provided to the Commissioner within the timeframe specified in any request by the Commissioner, and if no timeframe is specified, no later than thirty (30) days after the date of any such request. If requested by the Commissioner, the reports shall be submitted to the Commissioner by email to DEEP.StormwaterConstruction@ct.gov. Solar Array Projects subject to Appendix I shall also submit the reports prescribed in that Section of the permit by email.
- 5.3.2.2 Turbidity Monitoring Reports
- Records of turbidity monitoring conducted pursuant to Sections 5.2.2.8.b. shall be submitted to the Commissioner on the first day of each month following the initiation of the dewatering discharge for as long as the discharge exists. Turbidity Monitoring Reports shall be submitted by email to DEEP.StormwaterConstruction@ct.gov with the subject line “Construction turbidity monitoring” on forms prescribed by the Commissioner.

Section 6 Duty to Correct, Record, and Report Violations

6.1 Corrective Actions

Immediately upon learning of a violation of a condition of this general permit, the permittee shall immediately take all reasonable actions to determine the cause of the violation, correct the violation, mitigate the impact of the violation, and prevent its recurrence.

6.2 Reporting Violations

6.2.1 Noncompliance with Permit Terms or Conditions

In accordance with Section 22a-430-3(j)(8), 22a-430-3(j)(11)(D), 22a-430-3(k)(4), and 22a-430-3(i)(3) of the RSCA, the Permittee shall notify the Commissioner of the following actual or anticipated noncompliance with the terms or conditions of this permit within two hours of becoming aware of the circumstances. All other actual or anticipated violations of the permit shall be reported to the Commissioner within 24 hours of becoming aware of the circumstances:

- a noncompliance that is greater than two times an effluent limitation.
- a noncompliance of any minimum or maximum daily limitation or excursion beyond a minimum or maximum daily range.
- any condition that may endanger human health or the environment.
- a failure or malfunction of monitoring equipment used to comply with the monitoring requirements of this permit.
- any actual or potential bypass of the Permittee's collection system or treatment facilities.
- expansions or significant alterations of any wastewater collection, treatment components, or its method of operation for the purpose of correcting or avoiding a permit violation.

Notifications shall be submitted via the Commissioner's online Noncompliance Notification Form:

<https://portal.ct.gov/deep/water-regulating-and-discharges/stormwater/stormwater-management>

6.2.2 Five-Day Follow Up Report

Within five (5) days of any notification of noncompliance in accordance with this permit, the Permittee shall submit a follow-up report within five days of the noncompliance using the Commissioner's online Noncompliance Follow-up Report Form:

<https://portal.ct.gov/deep/water-regulating-and-discharges/stormwater/stormwater-management>

The follow-up report shall contain, at a minimum, the following information:

- a description of the noncompliance and its cause.
- the period of noncompliance, including exact dates and times.
- if the noncompliance has not been corrected, the anticipated time it is expected to continue.
- steps taken or planned to correct the noncompliance and reduce, eliminate and prevent recurrence of the noncompliance.

Notification of an actual or anticipated noncompliance or site modification does not stay any term or condition of this permit.

6.2.3 Additional Notification Requirements

In accordance with Section 22a-430-3(j)(11)(ED) of the RSCA, the Permittee shall notify the Commissioner within seventy-two (72) hours and in writing within 30 days when he or she knows or has reason to believe that the concentration in the discharge of any substance listed in the application, or any toxic substance as listed in Appendix B or D of RSCA Section 22a-430-4, has exceeded or will exceed the highest of the following levels:

- one hundred micrograms per liter.
- two hundred micrograms per liter for acrolein and acrylonitrile, five hundred micrograms per liter for 2,4-dinitrophenol and for 2-methyl-4, 6-dinitrophenol; and one milligram per liter for antimony.
- an alternative level specified by the Commissioner, provided such level shall not exceed the level which can be achieved by the permittee's treatment system.

The 72-hour initial notifications and thirty (30) day follow-up reports shall be submitted via the Commissioner's online Noncompliance Follow-up Report Form. The Forms are available on the DEEP website here:

<https://portal.ct.gov/deep/water-regulating-and-discharges/stormwater/stormwater-management>

Section 7 Regs. Conn. State Agencies Incorporated into this General Permit

The Permittee shall comply with all laws applicable to the subject discharges, including but not limited to, the following Regs. Conn. State Agencies which are hereby incorporated into this general permit, as if fully set forth herein:

7.1 Section 22a-430-3

- Subsection (b) General
- Subsection (c) Inspection and Entry
- Subsection (d) Effect of a Permit
- Subsection (e) Duty to Comply
- Subsection (f) Proper Operation and Maintenance
- Subsection (g) Sludge Disposal
- Subsection (h) Duty to Mitigate
- Subsection (i) Facility Modifications, Notification
- Subsection (j) Monitoring, Records and Report Requirements
- Subsection (k) Bypass
- Subsection (m) Effluent Limitation Violations
- Subsection (n) Enforcement
- Subsection (p) Spill Prevention and Control
- Subsection (q) Instrumentation, Alarms, Flow Recorders
- Subsection (r) Equalization

7.2 Section 221-430-4

- Subsection (a) Duty to Apply
- Subsection (b) Duty to Reapply
- Subsection (c) Application Requirements
- Subsection (o) Permit or Application Transfer
- Subsection (p) Revocation, Denial, Modification
- Subsection (q) Variances
- Subsection (t) Prohibitions

Section 8 Standard Conditions

The following standard conditions have been included in this general permit for the convenience of the permittee and are generally duplicative of the incorporated regulations in Section 6 of this general permit. If there are conflicting requirements, the regulations in Section 22a-430 take precedence.

8.1 Inspection and Entry

The Commissioner or his or her authorized representative may take any actions authorized by Sections 22a-6 (5), 22a-425 or 22a-336 of the Conn. Gen. Stat. as amended.

8.2 Reliance on Application

When evaluating an application, the Commissioner relies on information provided by the applicant. If such information proves to be false or incomplete, the authorization issued under this general permit may be suspended or revoked in accordance with law, and the Commissioner may take any other legal action provided by law.

8.3 Submission of Documents

Any document, other than a DMR, required to be submitted to the Commissioner under this Section of the permit will, unless otherwise specified in writing by the Commissioner or through this general permit, be directed to DEEP.StormwaterConstruction@ct.gov with the subject line: "ATTN: Construction Stormwater GP".

8.4 Violations

Violations of any of the terms, conditions, or limitations contained in this permit may subject the permittee to enforcement action including, but not limited to, seeking penalties, injunctions and/or forfeitures pursuant to applicable Sections of the Conn. Gen. Stat. and Regs. Conn. State Agencies.

8.5 Enforcement

The Commissioner may take any enforcement action provided by law, including but not limited to seeking injunctions, penalties and forfeitures as provided in Sections 22a-6, 22a-7, 22a-430, 22a-432, 22a-435, 22a-438 and 22a-471 of the Conn. Gen. Stat. as amended, for any violations or acts of noncompliance with chapter 446k of the Conn. Gen. Stat. or any regulation, order, permit or approval issued there under.

8.6 Need to Halt or Reduce Activity Not a Defense

It shall not be a defense for a permittee in an enforcement action that it would have been necessary to halt or reduce the permitted activity in order to maintain compliance with the conditions of the permit.

8.7 No Assurance

No provision of this permit and no action or inaction by the Commissioner shall be construed to constitute an assurance by the Commissioner that the actions taken by the permittee pursuant to this permit will result in compliance or prevent or abate pollution.

8.8 Relief

Nothing in this permit shall relieve the permittee of other obligations under applicable federal, state, and local law.

8.9 Duty to Provide Information

The Commissioner may require any permittee to provide within a reasonable time (30 days) any information which the Commissioner may request to determine whether cause exists for modifying or revoking the permit or to determine compliance with the permit, including but not limited to copies of records required to be kept by the permittee.

8.10 Duty to Comply

The permittee shall comply with all terms and conditions of the permit. Any permit noncompliance constitutes a violation of Chapter 446k of the Conn. Gen. Stat. Permit noncompliance is grounds for enforcement action, permit revocation or modification, or denial of a permit renewal application.

The permittee shall comply with effluent limitations, standards or prohibitions established under Section 307 (a) CWA which are adopted in Subsection (l) of section 22a- 430-4 of the Regs. Conn. State Agencies for toxic substances upon adoption, even if the permit has not yet been modified to incorporate the requirement.

Except for any toxic effluent standards and prohibitions imposed under Section 307 CWA, compliance with a permit during its term shall constitute compliance, for purposes of enforcement, with Sections 301, 302, 306, 307, 318, 403 and 405 of the Clean Water Act.

The Commissioner may modify or revoke a permit during its term for cause as provided in Section 22a-430-4 of the Regs. Conn. State Agencies.

It shall not be a defense for a permittee in an enforcement action that it would have been necessary to halt or reduce the permitted activity in order to maintain compliance with the conditions of the permit.

8.11 Duty to Mitigate

The permittee shall take all reasonable steps to minimize or prevent any discharge in violation of the permit or any discharge which has a reasonable likelihood of adversely affecting human health or the environment.

8.12 Sludge Disposal

The permittee shall dispose of screenings, sludges, chemicals, and oils and any solid or liquid wastes resulting from the wastewater treatment processes at locations approved by the Commissioner for disposal of such materials, or by means of a waste hauler licensed under the provisions of the Conn. Gen. Stat.

8.13 Resource Conservation

All permittees shall implement and maintain practices and/or facilities which, to the maximum extent practicable, result in the minimum amount of wastewater discharged. Such results may be achieved by methods including but not limited to water conservation, resource recovery, waste recycling, wastewater reuse, and material or product substitution. Excessive use of water or the addition of water to dilute an effluent in order to meet any permit limitations or conditions is prohibited.

8.14 Spill Prevention and Control

The permittee shall maintain practices, procedures and facilities designed to prevent, minimize and control spills, leaks, or such other unplanned releases of all toxic or hazardous substances and any other substances as the Commissioner deems necessary to prevent pollution of the waters of the State. Such requirements shall, unless otherwise allowed by the Commissioner, apply to all facilities used for storing, handling transferring, loading, or unloading such substances, including manufacturing areas.

The requirements of this Section do not apply to site components or systems already covered by plans prepared or approved under the Resource Conservation and Recovery Act and the Spill Prevention, Control and Countermeasure program.

8.15 Duty to Reapply

The permit shall be effective for a fixed term not to exceed five (5) years unless administratively extended. The Department will provide permit renewal directions.

8.16 Equalization

All treatment facilities shall be designed to prevent upsets, malfunctions or instances of noncompliance resulting from variations in wastewater strength or flow rate, and shall include, as the Commissioner deems necessary, equalization facilities separate from the treatment facilities.

8.17 Effect of an Upset

An upset does not include noncompliance to the extent caused by operational error, improperly designed treatment facilities, inadequate treatment facilities, lack of preventive maintenance, or careless or improper operation. In any enforcement proceeding the permittee seeking to establish the occurrence of an upset has the burden of proof.

A permittee who wishes to establish the affirmative defense of upset shall demonstrate, through properly signed, contemporaneous operating logs, or other relevant evidence that:

- an upset occurred and that the permittee can identify the cause(s) of the upset.
- the permitted site was at the time being properly operated.
- the permittee submitted notice of the upset timely as required in Section 6.2 of this general permit.
- the permittee complied with all remedial measures.

8.18 Bypass

The permittee shall not at any time bypass the collection system or treatment facilities or any part thereof unless such bypass is unanticipated, unavoidable, and necessary to prevent loss of life, personal injury or severe property damage, and there were no feasible alternatives to the bypass, including but not limited to the use of auxiliary or back-up treatment facilities, retention of untreated wastes, stopping the discharges, or maintenance during normal periods of equipment downtime; or the permittee receives prior written approval of the bypass from the Commissioner in order to perform essential maintenance, and the bypass does not cause effluent limitations to be exceeded.

8.18.1 Necessary Bypass

In the event such a bypass is necessary, the permittee shall to the extent possible minimize or halt production and/or all discharges until the site is restored or an alternative method of treatment is provided.

8.18.2 Bypass Prevention

In order to prevent a bypass, the permittee may schedule maintenance during periods when no discharge is occurring or employ any necessary means, including but not limited to duplicate units and systems or alternative collection and treatment or pretreatment schemes. Any such means shall insure that the effluent limitations specified in the permit are achieved; be approved by DEEP in writing prior to its use, which approval shall include an alternative schedule for monitoring if appropriate; and be discontinued upon completion of the performance of the essential maintenance.

8.18.3 Notification to DEEP

8.18.3.1 The permittee shall provide notice to DEEP not less than twenty-four (24) hours prior to the use of any alternative scheme and monitor and record the quality and quantity of the discharge in accordance with permit terms and conditions or an approved alternative schedule. Such monitoring shall be submitted with the next monitoring report required by the permit and shall not be used to meet routine scheduled monitoring report requirements of the permit.

8.18.3.2 If any bypass occurs or may occur, the permittee shall, within two hours of becoming aware of such condition or need, notify DEEP's 24-hour Emergency Response Unit at 860-424-3338 or 866-337-7745 and submit within five days a written report including the cause of the problem, duration

including dates and times and corrective action taken or planned to prevent other such occurrences. Information about incident reporting can be found on DEEP's Emergency Response and Spill Prevention website <https://portal.ct.gov/deep/emergency-response-and-spill-prevention/emergency-response-and-spill-prevention>.

- 8.18.3.3 If the permittee has reason to believe that any effluent limitation specified in the permit may be violated, the permittee shall immediately take steps to prevent or correct such violation, including but not limited to employing an alternative scheme of collection or treatment, and/or control the production of the wastewater and shall monitor and record the quality and quantity of the discharge in accordance with the permit terms and conditions or an approved alternative schedule. Such monitoring shall be submitted with the next monitoring report required by the permit and shall not be used to meet the routine monitoring requirements of the permit.

8.19 Proper Operation and Maintenance

The permittee shall at all times properly operate and maintain all facilities and systems and parts thereof for wastewater collection, storage, treatment, and control which are installed or used by the permittee to achieve compliance with the terms and conditions of the permit. Proper operation and maintenance includes, but is not limited to, effective performance, adequate funding, and adequate operator staffing and training, including the employment of certified operators as may be required by the Commissioner pursuant to Sections 22a-416-1 through 22a-416-10 of the Regs. Conn. State Agencies, as amended, and adequate laboratory and process controls, including appropriate quality assurance procedures.

In accordance with Sections 22a-416 through 22a-471 of the Conn. Gen. Stat. as amended, the permittee is required to install and operate a back-up or auxiliary facilities or similar systems or the inventory of spare parts and appurtenances.

8.20 Instrumentation, Alarms, and Flow Records

Except for batch treatment systems unless required by the Commissioner, process wastewater treatment systems shall include instrumentation to automatically and continuously indicate, record and/or control those functions of the system and characteristics of the discharge which the Commissioner deems necessary to assure protection of the waters of the State.

8.21 Signatory Requirements

8.21.1 Signatory

All permit applications and permit modification requests submitted to the Commissioner shall be signed as follows:

- 8.21.1.1 For a corporation, the signatory shall be a responsible corporate officer.

For the purposes of this Section, a responsible corporate officer means a president, secretary, treasurer, or vice-president of the corporation in charge of a principal business function; any other person who performs similar policy or decision-making functions for the corporation; or the manager of one or more manufacturing, production, or operating facilities employing more than 250 persons or having gross annual sales or expenditures exceeding twenty-five million dollars (in second quarter 1980 dollars), if authority to sign documents has been assigned or delegated to the manager in accordance with corporate procedures.

- 8.21.1.2 For a partnership or sole proprietorship, the signatory shall be a general partner or the proprietor, respectively.

- 8.21.1.3 For a municipality, State, Federal, or other public agency, the signatory shall be either a principal executive officer or a ranking elected official.

For purposes of this Section, a principal executive officer of a federal agency includes the chief executive officer of the agency, or a senior executive officer having responsibility for the overall operations of a principal geographic unit of the agency.

8.21.2 Duly Authorized Representative

All reports required by permits, and other information submitted to the Commissioner shall be signed by a person described in Section 8.21.1 of this general permit or by a duly authorized representative of that person. A person is a duly authorized representative only if:

- 8.21.2.1 The authorization is made in writing by a person described in Section 8.21.1 of this general permit,
- 8.21.2.2 The authorization specifies either an individual or a position having responsibility for the overall operation of the regulated site or activity, such as the position of plant manager, operator of a well or well field, superintendent, position of equivalent responsibility, or an individual or position having overall responsibility for environmental matters for the company. A duly authorized representative may thus be either a named individual or any individual occupying a named position; and
- 8.21.2.3 The written authorization is submitted to the Commissioner.

8.21.3 Notification to DEEP

If an authorization under this subsection is no longer accurate because a different individual or position has assumed the applicable responsibility, a new authorization satisfying the requirements of this section must be submitted to the Commissioner prior to or together with any reports or other information to be signed by an authorized representative.

8.21.4 Certification

Any person signing a document under this section shall make the following certifications:

“I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information is, to the best of my knowledge and belief, true, accurate and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.”

“I have personally examined and am familiar with the information submitted in this document and all attachments thereto, and I certify that, based on reasonable investigation, including my inquiry of those individuals responsible for obtaining the information, the submitted information is true, accurate and complete to the best of my knowledge and belief. I understand that a false statement made in the submitted information may be punishable as a criminal offense, in accordance with Section 22a-6 of the Conn. Gen. Stat., pursuant to Section 53a-157b of the Conn. Gen. Stat., and in accordance with any other applicable statute.”

8.22 Date of Filing

For purposes of this general permit, the date of filing with the Commissioner of any document is the date such document is received by the Commissioner.

8.23 False Statements

Any false statement in any information submitted pursuant to this general permit may be punishable as a criminal offense, in accordance with Section 22a-6 of the Conn. Gen. Stat., pursuant to Section 53a-157b of the Conn. Gen. Stat., and in accordance with any other applicable statute.

8.24 Correction of Inaccuracies

Within fifteen (15) days after the date a permittee becomes aware of a change in any of the information submitted pursuant to this general permit, becomes aware that any such information is inaccurate or misleading, or that any relevant information has been omitted, such permittee shall correct the inaccurate or misleading information or supply the omitted information in writing to the Commissioner. Such information shall be certified in accordance with Section 8.21.4 of this general permit. A Notice of Change shall be submitted for any changes made pursuant to Section 3.5 of this general permit.

8.25 Transfer of Authorization

Any authorization under this general permit shall not be transferable.

8.26 Other Applicable Law

Nothing in this general permit shall relieve the permittee of the obligation to comply with any other applicable federal, state, and local law, including but not limited to the obligation to obtain any other authorizations required by such law.

8.27 Duty to Reapply

The permit will be effective for a fixed term not to exceed five (5) years unless administratively extended. The general permit will provide instructions on how and when to reapply.

8.28 Other Rights

This general permit is subject to and does not derogate any present or future rights or powers of the State of Connecticut and conveys no rights in real or personal property nor any exclusive privileges and is subject to all public and private rights and to any federal, state, and local laws pertinent to the property or activity affected by such general permit. In conducting any activity authorized hereunder, the permittee may not cause pollution, impairment, or destruction of the air, water, or other natural resources of this state. The issuance of this general permit shall not create any presumption that this general permit should or will be renewed.

8.29 Effect of a Permit

The issuance of a permit does not convey any property rights of any sort, or any exclusive privilege, authorize any injury to persons or property or invasion of other private rights, authorize any infringement of the Conn. Gen. Stat., Regs. Conn. State Agencies or municipal ordinances, or affect the responsibility of the permittee to obtain all applicable federal, State and municipal authorizations or permits for the discharge and activities which generate the discharge.

Section 9 Commissioner's Powers

9.1 Abatement of Violations

The Commissioner may take any action provided by law to abate a violation of this general permit, including but not limited to penalties of up to \$25,000 per violation per day under Chapter 446k of the Conn. Gen. Stat., for such violation. The Commissioner may, by summary proceedings or otherwise and for any reason provided by law, including violation of this general permit, revoke a Permittee's authorization hereunder in accordance with Sections 22a-3a-2 through 22a-3a-6, inclusive, of the Regs. Conn. State Agencies. Nothing herein shall be construed to affect any remedy available to the Commissioner by law.

9.2 General Permit Revocation, Suspension, or Modification

The Commissioner may, for any reason provided by law, by summary proceedings or otherwise, revoke or suspend this general permit or modify to establish any appropriate conditions, schedules of compliance, or other provisions which may be necessary to protect human health or the environment.

9.3 Filing of an Individual Permit Application

If the Commissioner notifies a Permittee in writing that such Permittee must obtain an individual permit, the Permittee shall file an application for an individual permit within thirty (30) days of receiving the Commissioner's notice or such other time that the Commissioner specified in the notice to the Permittee. While such application is pending before the Commissioner, the Permittee shall continue to comply with the terms and conditions of this general permit. Nothing herein shall affect the Commissioner's power to revoke a Permittee's authorization under this general permit at any time.

Section 10 Definitions

The definitions of terms used in this general permit shall be the same as the definitions contained in Section 22a-423 of the Conn. Gen. Stat. and Section 22a-430-3(a) of the Regs. Conn. State Agencies. All references to an Appendix in this general permit means the applicable Appendix of this general permit. As used in this general permit, the following definitions shall apply:

“x-year, 24-hour rainfall event” means the maximum 24-hour precipitation event with a probable recurrence interval of once in the given number of years (i.e. x=2, 25 or 100), as defined by the National Oceanic and Atmospheric Administration (NOAA) Atlas 14, Volume 10, Version 2, Point Precipitation Frequency Estimates (as amended), or equivalent regional or state rainfall probability information developed therefrom.

“Annual sediment load” means the total amount of sediment carried by stormwater runoff on an annualized basis.

“Applicant” means a person or municipality which files a complete application.

“Application” means an application filed with the Commissioner pursuant to this general permit.

“Aquifer protection area” means that term as defined in Section 22a-354 of the Conn. Gen. Stat.

“Authorized Activity” means any activity authorized by this general permit.

“Best Management Practice” or *“BMP”* means a schedule of activities, practice (and prohibitions of practices), structure, vegetation, maintenance procedure, and other management practices to prevent or reduce the discharge of pollutants to waters of the State consistent with state, federal or other equivalent and technically supported guidance. BMPs also include treatment requirements, operating procedures, and practices to control site runoff, spillage or leaks, sludge or waste disposal, or drainage from material storage.

“CFR” means the Code of Federal Regulations.

“Clean Water” means water which, in the judgment of the Commissioner, is of a quality substantially similar to that occurring naturally in the receiving stream under consideration. Clean water may include minor cooling waters, residential swimming pool water, and stormwater.

“Coastal area” means coastal area as defined in Section 22a-93(3) of the Conn. Gen. Stat.

“Coastal waters” means those waters of Long Island Sound and its harbors, embayments, tidal rivers, streams and creeks which contain a salinity concentration of at least five hundred parts per million under low flow conditions.

“Commissioner” means Commissioner as defined by Section 22a-2(a) of the Conn. Gen. Stat.

“Control Measures” means any BMPs, or other methods used to prevent or reduce the discharge of pollutants to waters of the State.

“Construction Activity” means any activity and discharges associated with construction at a site or the site’s preparation for construction, including, but not limited to, clearing, grubbing, pile driving, soil disturbance, soil compaction by construction equipment, staging and stockpiling, storage, cleaning and washout, grading, excavation, and dewatering.

“Construction and Development Effluent Limitations and New Source Performance Standards” (C&D Rule), as published in 40 CFR§450, means the regulation requiring effluent limitations guidelines (ELGs) and new source performance standards (NSPS) for controlling the discharge of pollutants from construction sites.

“*Day*” means the calendar day; if any date specified in the general permit falls on a Saturday, Sunday, or legal holiday, such deadline shall be the next business day thereafter.

“*DOT*” means the State of Connecticut Department of Transportation.

“*DOT MS4*” means conveyances for stormwater including, but not limited to, roads with drainage systems, streets, catch basins, curbs, gutters, ditches, man-made channels, or storm drains owned or operated by the Connecticut Department of Transportation and discharging directly to surface waters of the State.

“*Department*” or “*DEEP*” means the Department of Energy and Environmental Protection.

“*Design-Build Project*” is an alternative project delivery method in which a developer selects a design and build team to complete the design and construction of a project rather than separate contracts with the designer and contractor. With such a project, the design and construction phases can be overlapped, so that site preparation and investigation can proceed before a final design is developed.

“*Designing Qualified Professional*” means the Qualified Professional engineer or qualified soil erosion and sediment control professional, as defined below, who developed the original Stormwater Pollution Control Plan for which authorization was granted under this general permit.

“*Developer*” means a person, municipality, or state or federal agency that is responsible, either solely or partially through contract, for the design and construction of a project site.

“*Dewatering water*” means water associated with the construction activity generated from the lowering of the groundwater table, the pumping of accumulated uncontaminated stormwater or uncontaminated groundwater from an excavation, the pumping of surface water from a cofferdam, or pumping of other surface water that has been diverted into a construction site.

“*Discharge*” means the emission of any water, substance, or material into the waters of the State, whether or not such substance causes pollution as defined in Section 22a-423 of the Conn. Gen. Stat.

“*District*” means a Soil and Water Conservation District established pursuant to Section 22a-315 of the Conn. Gen. Stat. Appendices E and F list the Districts, their geographic delineations, and contact information.

“*Disturbance*” means the area on a site where soil will be exposed or susceptible to erosion during any construction activity.

“*Drought-Stricken Area*”, for the purposes of this permit, means an area in which the National Oceanic and Atmospheric Administration’s U.S. Seasonal Drought Outlook indicates for the period during which the construction will occur that any of the following conditions are likely: (1) “Drought to persist or intensify”, (2) “Drought ongoing, some improvement”, (3) “Drought likely to improve, impacts ease”, or (4) “Drought development likely”. See http://www.cpc.ncep.noaa.gov/products/expert_assessment/sdo_summary.php.

“*Early Release Construction*” or “*ERC*” means the preliminary construction activity for a design-build project conducted in order to investigate site conditions and obtain the information necessary to develop the final design for the project.

“*Effective Impervious Cover*” is the area of impervious cover that is hydraulically connected to a water or wetland by means of continuous paved surfaces, gutters, swales, ditches, drain pipes, or other conventional conveyance and detention structures that do not reduce runoff volume.

“*Engineered stormwater management system*” means any control measure and related appurtenances which requires engineering analysis and/or design by a professional engineer.

“*Erosion*” means the detachment and movement of soil or rock fragments by water, wind, ice and gravity.

“*Final Design Phase*” means the final design phase of a design-build project. This phase of the design-build project follows the Site Preparation Phase.

“*Final stabilization*” means that no disturbed areas remain exposed and there are no signs of erosion or sedimentation on site; the vegetation must be at least 6 inches tall with a minimum of one hundred (100) plants per square foot across all seeded areas, or a permanent non-vegetative ground cover has been fully established over the entire site.

“*Fresh-tidal wetland*” means a tidal wetland located outside of coastal waters.

“*General Permit*” or “*this permit*” means the *General Permit for the Discharge of Stormwater from Construction Activities* issued by the Commissioner.

“*Groundwater*” means those waters of the State that naturally exist or flow below the surface of the ground.

“*Guidelines*” means the Connecticut Guidelines for Soil Erosion and Sediment Control, as amended, established pursuant to Section 22a-328 of the Conn. Gen. Stat.

“*High Quality Waters*” means those waters defined as high quality waters in Regs. Conn. State Agencies Section 22a-426-1, as may be amended.

“*Impaired water(s)*” for the purposes of this permit, means any waterbody that does not meet applicable water quality standards, including but not limited to waters listed in categories 5 or 4b on the Connecticut Integrated Report of waters listed pursuant to Clean Water Act Section 303(d) and 305(b). Impaired Waters are also known as “*Water Quality Limited Waters*.”

“*Impervious Cover*” means hard surfaces which prevent or impede the infiltration of water. Such surfaces include, but are not limited to, roof areas, compacted gravel, paved walkways, paved parking areas, paved driveways, and other paved surfaces.

“*In Responsible charge*” means professional experience for which the Commissioner determines that a professional’s primary duties consistently involve a high level of responsibility and decision making in the planning and designing of engineered stormwater management systems or in the planning and designing of soil erosion and sediment controls for residential and commercial construction projects. The Commissioner shall consider the following in determining whether a professional’s experience qualifies as responsible charge experience:

- (i) The level of independent decision-making exercised.
- (ii) The number of individuals and the disciplines of the other professionals that the professional supervised or coordinated.
- (iii) The extent to which a professional’s responsibilities consistently involved the review of work performed by other professionals involved the planning and designing of engineered stormwater management systems or the planning and designing of soil erosion and sediment controls for residential and commercial construction projects.
- (iv) The extent to which a professional’s responsibilities consistently involved the planning and designing of engineered stormwater management systems or the planning and designing of soil erosion and sediment controls for residential and commercial construction projects and whether such responsibilities were an integral and substantial component of the professional’s position.

(v) The nature of a professional's employer's primary business interests and the relation of those interests to planning and designing of engineered stormwater management systems or to planning and designing of soil erosion and sediment controls for residential and commercial construction projects.

(vi) The extent to which a professional has engaged in the evaluation and selection of scientific or technical methodologies for planning and designing of engineered stormwater management systems or for planning and designing of soil erosion and sediment controls for residential and commercial construction projects.

(vii) The extent to which a professional drew technical conclusions, made recommendations, and issued opinions based on the results of planning and designing of engineered stormwater management systems or of planning and designing of soil erosion and sediment controls for residential and commercial construction projects.

(viii) Any other factor that the Commissioner deems relevant.

"Individual permit" means a permit issued to a named person under Section 22a-430 of the Conn. Gen. Stat.

"Infeasible" means not technologically possible, or not economically practicable and achievable in light of best industry practices.

"Inland wetland" means wetlands as defined in Section 22a-38 of the Conn. Gen. Stat.

"Landscape Architect" means a person with a currently effective license issued in accordance with chapter 396 of the Conn. Gen. Stat.

"Linear Project" includes the construction of roads, railways, bridges, bikeways, conduits, substructures, pipelines, sewer lines, towers, poles, cables, wires, connectors, switching, regulating and transforming equipment and associated ancillary facilities in a long, narrow area.

"Locally Approvable Project" or *"Locally Approvable"* means a construction activity that is not carried out by or on behalf of a municipal, state or federal entity and is required to obtain municipal approval for the project.

"Locally Exempt Project" or *"Locally Exempt"* means a construction activity which is either; (i) carried out by or on behalf of a municipal, state, or federal entity; or (ii) is not subject to local (municipal) approval.

"Low Impact Development" or *"LID"* means a site design and stormwater management strategy that maintains, mimics or replicates pre-development hydrology through the use of numerous site design principles and small-scale structural stormwater practices distributed throughout a site to manage runoff volume and water quality at the source.

"Minimize" means to reduce and/or eliminate to the extent achievable using stormwater controls that are technologically available and economically practicable and achievable in light of best industry practices.

"Municipal separate storm sewer system" or *"MS4"* means conveyances for stormwater (including roads with drainage systems, streets, catch basins, curbs, gutters, ditches, man-made channels or storm drains) owned or operated by any municipality, DOT, or by any other state or federal institution.

"Municipality" means any metropolitan district, town, consolidated town and city, consolidated town and borough, city, borough, village, fire and sewer district, sewer district and each municipal organization having authority to levy and collect taxes or make charges for its authorized function as defined by Section 22a-423 of the Conn. Gen. Stat.

"New discharger" means any building, structure, facility, or installation:

(a) From which there is or may be a "discharge of pollutants."

(b) That did not commence the “discharge of pollutants” at a particular “site” prior to August 13, 1979.

(c) Which is not a “new source.”

(d) Which has never received a finally effective NPDES permit for discharges at that “site.”

“*New or Increased Discharge*” means new discharge or activity as defined in Section 22a-426-8(b)(3) and increased discharge or activity as defined in Section 22a-426-8(b)(2), as referenced to the Regs. Conn. State Agencies.

“*New source*” means any building, structure, facility, or installation from which there is or may be a “discharge of pollutants,” the construction of which commenced after February 1, 2010.

“*Normal Working Hours*” are considered to be, at a minimum, Monday through Friday, between the hours of 8:00 am and 6:00 pm, unless additional working hours are specified by the Permittee.

“*Notice of Termination*” (NOT) means the form (electronic or paper) required for terminating coverage under the Construction General Permit.

“*NPDES Permit*” means a permit authorizing a discharge to the surface waters of the State either directly, or indirectly by means other than through a POTW or the ground waters, which is issued by the Commissioner pursuant to Section 22a-430 of the Conn. Gen. Stat.

“*Permittee*” means any person who or municipality which initiates, creates or maintains a discharge in accordance with this general permit.

“*Person*” means person as defined in Section 22a-2(b) of the Conn. Gen. Stat.

“*Phase*” means a portion of a project possessing a distinct and complete set of activities that have a specific functional goal wherein the work to be completed in the phase is not dependent upon the execution of work in a later phase in order to make it functional.

“*Point Source*” means any discernible, confined and discrete stormwater conveyance (including but not limited to, any pipe, ditch, channel, tunnel, conduit, discrete fissure, container, rolling stock, concentrated animal feeding operation, landfill leachate collection system, vessel or other floating craft) from which pollutants are or may be discharged. Point source does not include agricultural stormwater discharges and return flows from irrigated agriculture.

“*Professional Engineer*” or “*P.E.*” means a person with a currently effective license issued in accordance with chapter 391 of the Conn. Gen. Stat.

“*Qualified Inspector*” means an individual possessing either (1) a professional license or certification issued by EPA (<https://www.epa.gov/npdes/construction-general-permit-inspector-training>) or a professional organization recognized or approved by the Commissioner related to civil engineering, landscape architecture, soil science, and two years of demonstrable and focused experience in erosion and sediment control plan review, installation, inspection and/or report writing for residential and commercial construction projects in accordance with the Guidelines; or (2) certification by the CTDOT.

“*Qualified Professional engineer*” means a professional engineer who has, for a minimum of eight years, engaged in the planning and designing of engineered stormwater management systems for residential and commercial construction projects in accordance with the Guidelines and the Stormwater Quality Manual including, but not limited to, a minimum of four years in responsible charge of the planning and designing of engineered stormwater management systems for such projects. Such Qualified Professional engineer shall remain in good standing with the Connecticut Department of Consumer Protection and the Commissioner.

“Qualified soil erosion and sediment control professional” means a landscape architect or a professional engineer who: (1) has for a minimum of eight years engaged in the planning and designing of soil erosion and sediment controls for residential and commercial construction projects in accordance with the Guidelines including, but not limited to, a minimum of four years in responsible charge of the planning and designing of soil erosion and sediment controls for such projects; or (2) is currently certified as a professional in erosion and sediment control as designated by EnviroCert International, Incorporated (or other certifying organization acceptable to the Commissioner) and has, for a minimum of six years, engaged in the planning and designing of soil erosion and sediment controls for residential and commercial construction projects in accordance with the Guidelines including, but not limited to, a minimum of four years in responsible charge in the planning and designing of soil erosion and sediment controls for such projects. Such qualified soil erosion and sediment control professional shall remain in good standing with the Connecticut Department of Consumer Protection and the Commissioner.

“Regs. Conn. State Agencies” means the Regulations of Connecticut State Agencies.

“Regulated Municipal Separate Storm Sewer System” or *“Regulated MS4”* means any MS4 (as defined above) authorized by the most recently issued General Permit for the Discharge of Stormwater from Small Municipal Separate Storm Sewer Systems, as well as the separate storm sewer system of the CTDOT and the City of Stamford.

“Retain” means to hold runoff on-site to promote vegetative uptake and groundwater recharge through the use of runoff reduction or LID practices or other measures. In addition, it means there shall be no subsequent point source release to surface waters from a storm event defined in this general permit or as approved by the Commissioner.

“Runoff reduction practices” means those post-construction stormwater management practices used to reduce post-development runoff volume delivered to the receiving water, as defined by retaining the volume of runoff from a storm up to the Water Quality Volume, as defined in the Stormwater Quality Manual, as amended. Runoff reduction is quantified as the total annual post-development runoff volume reduced through canopy interception, soil amendments, evaporation, rainfall harvesting, engineered infiltration, extended filtration or evapo-transpiration.

“Sediment” means solid material, either mineral or organic, that is in suspension, is transported, or has been moved from its site of origin by erosion.

“Site” means geographically contiguous land on which a construction activity takes place or on which a construction activity for which authorization is sought under this general permit is proposed to take place. Non-contiguous land or water owned by the same person shall be deemed the same site if such land is part of a linear project or is otherwise connected by a right-of-way, which such person controls.

“Site Preparation Phase” means the initial Early Release Construction activity of a design-build project. This phase of a design-build project is followed by the Final Design Phase.

“Small Construction” or *“Small Construction Activity”* defined at 40 CFR §122.26(b)(15) and incorporated here by reference, means a small construction activity, including clearing, grading, and excavating, resulting in a land disturbance equal to or greater than one (1) acre and less than five (5) acres of land or which will disturb less than one (1) acre of total land area but is part of a larger common plan of development or sale that will ultimately disturb equal to or greater than one (1) acre but less than five (5) acres. Small construction activity does not include routine maintenance that is performed to maintain the original line and grade, hydraulic capacity, or original purpose of the site.

“Soil” means any unconsolidated mineral and organic material of any origin.

“Soil Scientist” shall be as defined in Conn. Gen. Stat. § 22a-38.

“Solar Array” or *“Soil Array Project”* means an on-the-ground installation of arrays of photovoltaic cell panels, supporting structures and related equipment for the production of electricity.

“Stabilize” means the use of measures as outlined in the Connecticut Guidelines for Soil Erosion and Sediment Control, as amended, or as approved by the Commissioner, to prevent the visible movement of soil particles and development of rills. A site or area of a site is stabilized when there is no evidence of erosion or sedimentation and temporary or permanent vegetative and/or non-vegetative measures have been applied to all disturbed areas.

“Standard of care”, as used in Section 2.2, means to endeavor to perform in a manner consistent with that degree of care and skill ordinarily exercised by members of the same profession currently practicing under similar circumstances.

“Stormwater” means waters consisting of rainfall runoff, including snow or ice melt during a rain event.

“Stormwater Pollution Control Plan” or *“SPCP”*, means a site-specific, written document that, at a minimum: (1) identifies potential sources of stormwater pollution at the construction site; (2) describes stormwater controls to reduce or eliminate pollutants in stormwater discharges from the construction site; and (3) identifies procedures to be implemented to comply with the terms and conditions of this general permit.

“Storm Sewer System” means a conveyance or system of conveyances (including roads with drainage systems, municipal streets, catch basins, curbs, gutters, ditches, manmade channels, or storm drains) designed or used for collecting or conveying stormwater.

“Stormwater Quality Manual” means the Connecticut Stormwater Quality Manual published by the Connecticut Department of Energy & Environmental Protection, as amended, and maintained at <http://www.ct.gov/deep/stormwaterqualitymanual>.

“Surface water” means those waters of the State which are not ground water and the waters of Long Island Sound, its harbors, embankments, tidal wetlands, and creeks; rivers and streams, brooks, waterways, lakes, ponds, marshes, swamps, bogs, federal jurisdictional wetlands, and other natural or artificial, public or private, vernal or intermittent bodies of water. Surface water does not include ground water.

“Structural measure” means a measure constructed for the temporary storage and/or treatment of stormwater runoff.

“Tidal wetland” means a wetland as that term is defined in Section 22a-29(2) of the Conn. Gen. Stat.

“Total disturbance” means the total area of disturbance on a site during all phases of construction activity.

“Total Maximum Daily Load” or *“TMDL”* means a calculation of the maximum amount of a pollutant that a waterbody can receive and still meet water quality standards, and an allocation of that amount to the pollutant's sources. A TMDL includes wasteload allocations (“WLAs”) for point source discharges, load allocations (“LAs”) for nonpoint sources and/or natural background, and must include a margin of safety (“MOS”) and account for seasonal variations.

“Upland soils” means soils which are not designated as poorly drained, very poorly drained, alluvial, or flood plain by the National Cooperative Soils Survey, as may be amended, of the Natural Resources Conservation Service of the United States Department of Agriculture and/or the inland wetlands agency of the municipality in which the project will take place.

“Water company” means water company as defined in Section 25-32a of the Conn. Gen. Stat.

“*Waters*” shall be as defined in § 22a-423, Conn. Gen. Stat., and for clarification shall include vernal pools and intermittent waters.

“*Water Quality Standards*” means those water quality standards or classifications contained in Sections 22a-426-1 through 22a-426-9, inclusive, of the Regs. Conn. State Agencies and the Classification Maps adopted pursuant to Section 22a-426 of the Conn. Gen. Stat., which together constitute the Connecticut Water Quality Standards, as may be amended.

“*Water Quality Volume*” or “*WQV*” means the volume of runoff generated on a site by the Water Quality Storm as defined in the Connecticut Stormwater Quality Manual, as amended.

“*Watercourse*” means a watercourse as that term is defined in Section 22a-38 of the Conn. Gen. Stat.

“*Wetland*” shall mean and include both “*wetland*” as defined in § 22a-29, Conn. Gen. Stat., and “*wetlands*” as defined in § 22a-38, Conn. Gen. Stat.

Section 11 Appendices

The following appendices are incorporated into this general permit.

11.1 Appendix A – Endangered and Threatened Species

11.2 Appendix B – RESERVED

11.3 Appendix C – Aquifer Protection Guidance Information

11.4 Appendix D – Coastal Management Act Determination Form

11.5 Appendix E & F – Memoranda of Agreement Between DEEP and Conservation Districts

11.6 Appendix G – Historic Preservation Review

11.7 Appendix H – Wild & Scenic Rivers Guidance

11.8 Appendix I – Stormwater Management at Solar Array Construction Projects

11.9 Appendix J – CT DEEP Financial Assurance Irrevocable Letter of Credit
